



बिहार BIHAR

500

23/6
2014

500/

मन्मथ कुमार
मन्मथ कुमार
लाल मन्मथ

L 803711

मौली परमानन्द
नवम्बर 108/1913-74
अप्राप्त नवम्बर, 1913

TREASURY OFFICE
Kaimur (Rhabua)

AGREEMENT No. 139 SBD of 2014-15

Name of Work : Construction of Senior Secondary Schools on Panchayat Level
in Bihar- Group no. SSS-153 (M.S. at Kaser, M.S.
at Sindhi in the District of Kaimur)


Name of Agency : Ajay Kumar singh,
Date of Commencement : 20.02.2014
Time of completion : Fifteen Months
Estimate Cost : Rs 2,10,10,782/-
Agreement Value : Rs. 2,07,98,573/- (1.01 % below BOQ rates)
Earnest Money :
Performance Security : Rs. 4,77,000/- (Details attached)

This agreement, made the 25th June 2014 between Bihar State
Educational Infrastructure Development Corporation Ltd. Patna. Hereinafter called

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

अजय कुमार सिंह

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

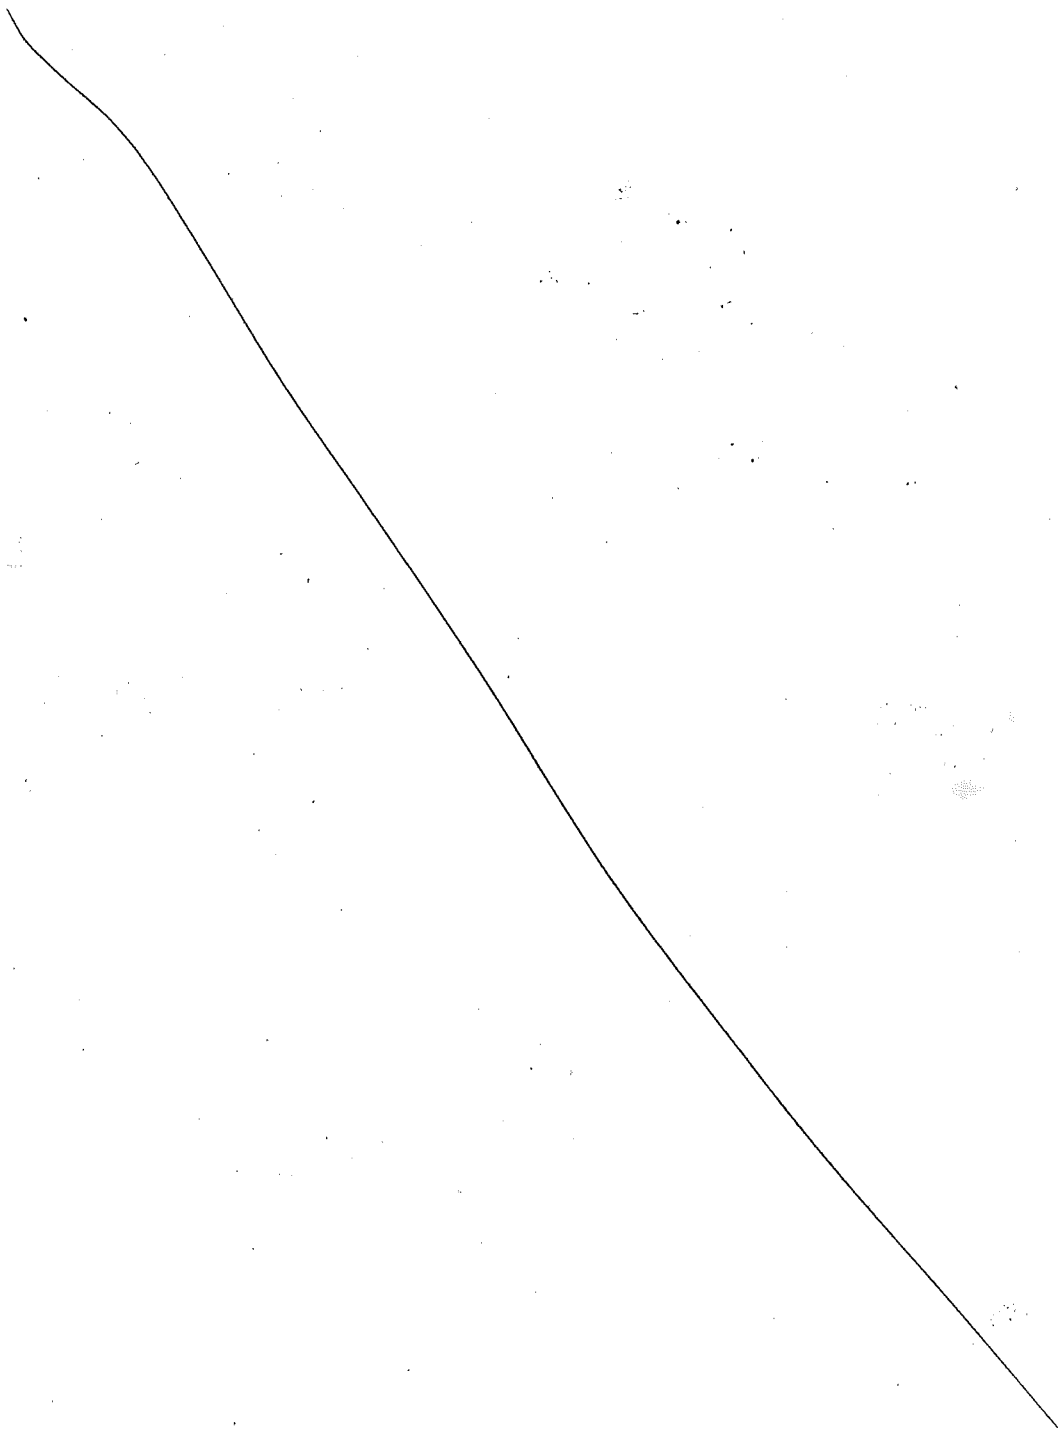

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

- 3 -

NOW THIS AGREEMENT WITNESSETH as follows :

1. In this Agreement, words and expression shall have the same meaning as are respectively assigned to them in the conditions of contract hereinafter referred to and they shall be deemed to form and be read and construed as part of this Agreement.
2. In consideration of the payments to be made by the Employer to the Contractor as hereinafter mentioned, the Contractor hereby covenants with the Employer to execute and complete the works and remedy any defects therein in conformity in all aspects with the provisions of the contract.
3. The Employer hereby covenants to pay the Contractor in consideration of the Execution and completion of the works and the remedying the defects wherein contract Price or such other sum as may become payable under the provisions of the Contract at the times and in the manner prescribed by the contract.
4. The following documents shall be deemed to form and be ready and construed as part of this Agreement Viz.
 - i) Letter of Acceptance
 - ii) Notice to proceed with the work.
 - iii) Contractor's Bid
 - iv) Condition of Contract: General and Special
 - v) Contract Data
 - vi) Additional Condition
 - vii) Drawing
 - viii) Bill of Quantities and
 - ix) Any other documents listed in the Contract Data as forming part of the contract.

In witnessed whereof the parties there to have caused this Agreement to be executed the day and year first before written.

The common Seal of

was hereunto affixed in the presence of :

Signed, Sealed and Delivery by the Said.....


In the Presence of :

Binding Signature of Employer.....

Binding Signature of Contractor.....

आजय कुमार सिंह

25-6-2014
Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Emg

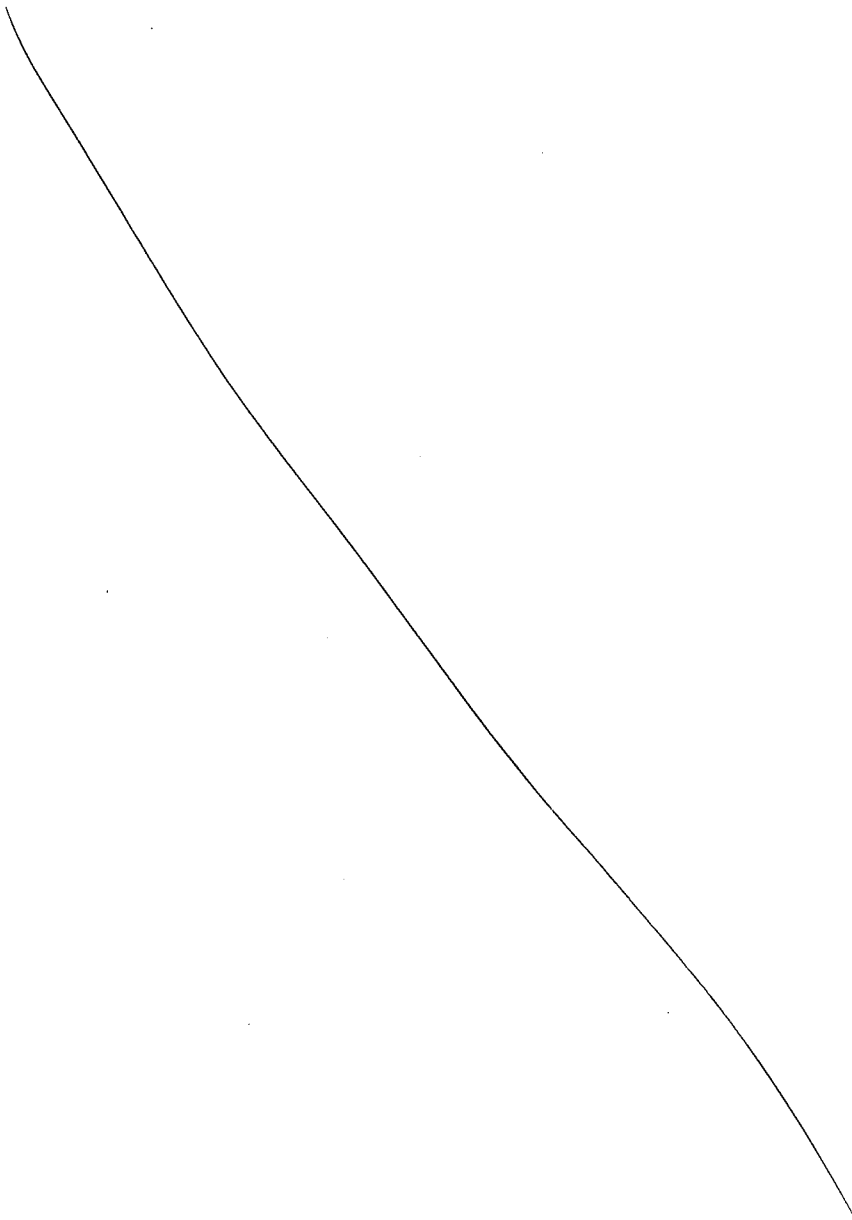

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

Performance Security

Name of Agency – “Ajay Kumar singh”

Performance Security of “Ajay Kumar Singh” Of “SSS-153”

<u>Pass Book. No.</u>	<u>DOI</u>	<u>Amount</u>
31350617- 24	03.08.13 48000*8	3,84000.00
31350625	03.08.13	24,000.00
31351514	04.01.14	21,000.00
31352476	08.05.14	48,000.00
Total		4,77,000.00

(Rupees Four Lacs Seventy Seven Thousands Only.)

Anil Kr Sar
20/6/14

लेखा पदाधिकारी
बिहार राज्य प्रौद्योगिक आवागमन संरचना
विकास निगम लि०, पटना

20-06-14

आजय कुमार सिंह

Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Rm8



Chief Engineer
B.S.E.I.D.C. Ltd., Patna

BIHAR STATE EDUCATIONAL INFRASTRUCTURE DEVELOPMENT CORPORATION LTD.

(A Govt. Of Bihar Undertaking)
Shiksha Bhawan, Bihar Rastrabhasa Parishad Campus, Acharya Shiv Pujan Sahay Path, Saidpur,
PATNA-800004. (Tel. No: 0612-2910314)

Letter no :- BSEIDC/TECH/164/2013-3894

Date- 31/12/13

CORRIGENDUM NOTICE NO.-3

With reference to N.I.T. No.36/2013-14 dated 12.12.2013 for "Construction of Senior Secondary School on Panchayat Level" in different Districts of Bihar, at Sl. No. 62 in "B.O.Q. for 10+2 Schools in Bihar" attached in financial bid, the details of item of work "Construction of 125mmX 40mmX 90m Tube well" are as below:-

Detailed Estimate for construction of 125 mm x 40 mm x 90 m Tube well						
Manual Boring						
Sl. No.	S.O.R	Description of Item	Quantity	Unit	Rate	Amount
Construction of 125mm x 40mm x 90m T/well						
Part 'A' - Cost of Materials						
1		125mm dia UPVC casing pipe confirming to ISS	27	Meter	315.00	8,505.00
2		40mm dia UPVC pipe confirming to ISS	48	Meter	99.38	4,770.24
3		40mm dia PVC ribbed strainer of approved quality	8	Meter	182.00	1,456.00
4		Reducing socket 125mm x 40mm	1	Each	270.00	270.00
5		Supplying all labour and materials & fitting & fixing PVC cap over the new sink T/well	1	Each	140.00	140.00
6	B.S.R 1548	Providing and fixing of G.I pipes complete with G.I fittings and clamps, including, cutting and making good etc 32 mm dia (15% C.P & 1% L.Cess)	18	mtr	206.62	3,719.16
7	B.S.R 1928	32 mm nominal bore Brass Full valve (15% C.P & 1% L.Cess)	1	Each	457.78	457.78
8		Supplying all equipments, tools and installation of 1 HP single phase submersible motor pump set of KSB/ ISI make 2900 rpm capable of discharge 5000 LPH at 45 Mtr head with all necessary riser pipe, starter control panel, 1.25" Full way valve, 1.25" M.S clamp, 1.25" G.I Elbow, 1.25" check valve, 1.25" x 9" long G.I Nipple etc. all complete as per direction of E/I	1	Each	26,446.00	26,446.00
Sub - Total "A"						45,764.18

उत्तराखण्ड


 Chief Engineer
 B.S.E.I.D.C. Ltd, Patna
 Pmb

		Boring by jet dhecki by suitable cutter of reduce as the case may be lowering 125 mm x U.P.V.C x 40 mm dia G.I pipe & strainer of standard quality iron, shoe, plug & socket etc. all complete including providing all tools and plants required for the job as per specification and direction of the engineer in charge.				
		(i) 0 to 30.5 m				
9		(a) For 125 mm dia U.P.V.C pipe	27	mtr	208.77	5,636.79
10		(b) for 40 mm dia UPVC pipe				
		(i) 0 to 30.5 m	3.5	mtr	119.03	416.61
		(ii) 30.5 m to 61.0 m				
11		(a) For 40 mm dia UPVC pipe	30.5	mtr	136.88	4,174.84
		(iii) 61.00 m to 75.00 m				
12		a) For 40mm dia UPVC pipe	14	mtr	148.79	2,083.06
		(iv) 75.00 m to above				
13		a) For 40mm dia UPVC ribbed strainer of approved quality	8	mtr	148.79	1,190.32
14		Providing all labour & tools and lowering 32 mm dia G.I pipe as per specificatin etc. all Complete	24	mtr	21.34	512.16
15		Supplying labour and developing the T/Well to have sand free discharge all complete as per direction of E/I	1	Each	280.50	280.50
		Sub - Total				14,294.28
		Total C="A+B"				60,058.46

Managing Director

31.12.11

~~25-6-2014~~

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

Reade

अनाथ कुमार सिंह

BIHAR STATE EDUCATIONAL INFRASTRUCTURE DEVELOPMENT CORPORATION LTD.

(A Govt. Of Bihar Undertaking)
Shiksha Bhawan, Bihar Rastrabhasa Parishad Campus, Acharya Shiv Pujan Sahay Path, Saidpur,
PATNA-800004. (Tel. No: 0612-2910314)

ASST. Engineer Bids.

Letter of Acceptance

Letter no :- BSEIDC/TECH/164/2013- 817


Patna. Date 20.02.14

With reference to N.I.T. No.-29/2013-14. Dated-30.12.2013. N.I.T. No.-31/2013-14. Dated- 01.01.2014. N.I.T. No.-32/2013-14. Dated-07.01.2014 & N.I.T. No.-36/2013-14. Dated-13-01-2014 for execution of "Construction of Senior Secondary School on Panchayat Level in Bihar" the bids have been accepted in favour of the Agencies as per details below:-

Sl No	Name of Group No.	Name of District	Name of Schools	Name & Address of Agency	Estimated value (in Rs.)	Tendered value (In Rs.)	Performance security to be deposited (In Rs.)	Time of work completion.
1	SSS-5	पूर्वी चंपारण	1 मध्य विद्यालय, मुरला	Virendra Kumar Chaudhari, Ajagari East Champaran, Bihar.	1,11,41,374.00	1,09,89,851.00 (1.36% below)	2,58,000.00	15 माह.
2	SSS-11	पूर्वी चंपारण	1 उत्कर्मित मध्य विद्यालय, मच्छहौ	Keshav Kumar Keshri, Vill+P.O.- Khairimal, P.S.- Pipra, Dist.- East Champaran, Bihar.	1,08,82,104.00	99,81,066.00 (8.28% below)	4,89,000.00	15 माह
3	SSS-13	पूर्वी चंपारण	1 मध्य विद्यालय, तेलहरा कला	R.S. Construction, Telharakala, East Champaran.	1,10,53,173.00	1,10,25,540.00 (0.25% below)	2,28,000.00	15 माह
4	SSS-14	पूर्वी चंपारण	1 उत्कर्मित मध्य विद्यालय, बरवा 2 उत्कर्मित मध्य विद्यालय, लक्ष्मीपुर 3 मध्य विद्यालय, गवानीपुर बाजार	Vijay Kumar Singh, Ibrahimpur, Persouni, East Champaran, Bihar.	3,35,31,401.00	3,19,01,775.00 (4.86% below)	10,26,000.00	15 माह
5	SSS-16	पूर्वी चंपारण	1 मध्य विद्यालय, विशुनपुर बसत 2 मध्य विद्यालय, देवसा 3 मध्य विद्यालय, परसौनी कोठी	Vijay Kumar Singh, Ibrahimpur, Persouni, East Champaran, Bihar.	3,29,07,705.00	3,16,37,468.00 (3.86% below)	9,39,000.00	15 माह

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

Chief Constable/Technician
Patna. Date 20.02.14

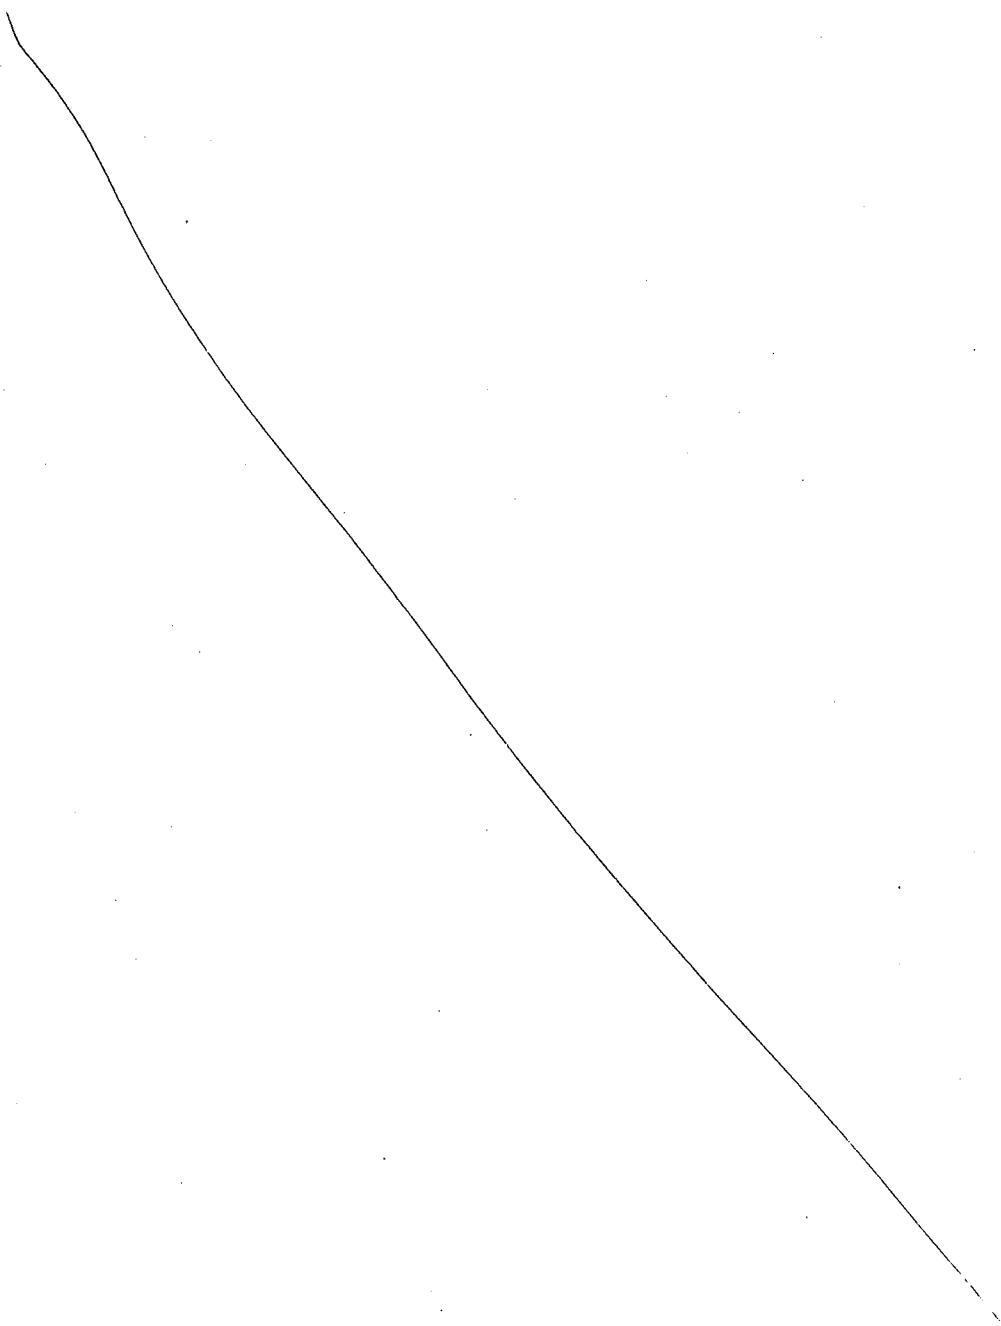


Chief Engineer
B.S.E.I.D.C. Ltd, Patna

47	SSS-153	कैमूर	1 उत्कर्मित मध्य विद्यालय, कसेर 2 उत्कर्मित मध्य विद्यालय, सिंधी	Ajay Kumar Singh, AT- Baré, Bhabua, kaimur, Bihar.	2,10,10,782.00	2,07,98,573.00 (1.01% below)	4,69,000.00	15 माह
48	SSS-156	कैमूर	1 मध्य विद्यालय, बढौना	M/S Gupta Dham Construction, Theloe, Kaimur, Bhabhua.	1,05,12,550.00	97,50,390.00 (7.25% below)	4,27,000.00	15 माह
49	SSS-157	कैमूर	1 उत्कर्मित मध्य विद्यालय, चफना 2 उत्कर्मित मध्य विद्यालय, न्यू	Ajay Kumar Singh, AT- Bare, Bhabua, kaimur, Bihar.	2,16,40,829.00	2,14,22,257.00 (1.01% below)	4,83,000.00	15 माह
50	SSS-160	मुंगेर	1 मध्य विद्यालय, बिहमा 2 मध्य विद्यालय, रामपुर 3 मध्य विद्यालय, खुटिया	Rajendra Kumar, AT- Pipradih, P.O.- Jhajha, Distt.- Jamui.	3,16,54,981.00	3,05,43,891.00 (3.51% below)	8,79,000.00	15 माह
51	SSS-161	मुंगेर	1 मध्य विद्यालय, बोचाही	Puja Kumari, AT- Bari Mohali, P.O.- Basudeopur, Distt.- Munger.	1,04,22,333.00	1,01,51,352.00 (2.60% below)	2,70,000.00	15 माह
52	SSS-162	मुंगेर	1 मध्य विद्यालय, मासुमगंज	Rajesh Kumar Singh, AT- Bahramba, Sikandara, Jamui.	1,05,09,845.00	1,02,47,099.00 (2.50% below)	2,69,000.00	15 माह
53	SSS-164	शेखपुरा	1 उत्कर्मित मध्य विद्यालय, करकी 2 उत्कर्मित मध्य विद्यालय, बेलछी 3 उत्कर्मित मध्य विद्यालय, वरुणा	Anil Kumar Singh, Station Road, Prof. Colony, Sheikhpura.	3,11,85,733.00	2,99,72,608.00 (3.89% below)	8,91,000.00	15 माह
54	SSS-168	बेगूसराय	1 मध्य विद्यालय, बखरी 2 मध्य विद्यालय, चक्करमीड, नदेल 3 मध्य विद्यालय, मिर्जापुर चौद 4 उत्कर्मित मध्य विद्यालय, भवनगामा 5 पुनर्वास 6 उत्कर्मित मध्य विद्यालय, असुरारी 7 मध्य विद्यालय, केशवे	M/S Bairam Kumar, Kapasiya, Begusarai, Bihar.	2,14,48,463.00	2,14,37,739.00 (0.05% below)	4,32,000.00	15 माह
55	SSS-169	बेगूसराय	1 उत्कर्मित मध्य विद्यालय, चर्कीया 2 पुनर्वास 3 उत्कर्मित मध्य विद्यालय, अंसुरारी 4 उत्कर्मित मध्य विद्यालय, केशवे	Budha Infrastructure Pvt. Ltd., Hanuman Nagar, Kankarbagh, Patna.	5,20,62,987.00	5,02,09,545.00 (3.56% below)	14,52,000.00	15 माह
56	SSS-170	बेगूसराय	1 मध्य विद्यालय, पपरीर	M/S Daya Ram Singh, Kapasiya, Nagdah, Begusarai, Bihar.	1,03,94,127.00	1,01,91,442.00 (1.95% below)	2,54,000.00	15 माह
57	SSS-171	बेगूसराय	1 उत्कर्मित मध्य विद्यालय, कुसमौत	M/S Saheb Singh Construction, Muri Barari, P.O.- Dahibhatta, Distt.- Gopalganj.	1,04,70,255.00	1,03,39,377.00 (1.25% below)	2,40,000.00	15 माह
58	SSS-172	बेगूसराय	1 मध्य विद्यालय, दरियापुर 2 मध्य विद्यालय, गोदरगामा	M/S Daya Ram Singh, Kapasiya, Nagdah, Begusarai, Bihar.	2,10,47,524.00	2,10,47,524.00 (At estimated value)	4,21,000.00	15 माह

Construction of Senior Secondary Schools on Panchayat Level in Bihar

Chief Engineer
B.S.E.I.D.C. Ltd, Patna


Bihar State Educational Infrastructure
Development Corporation Ltd., Patna

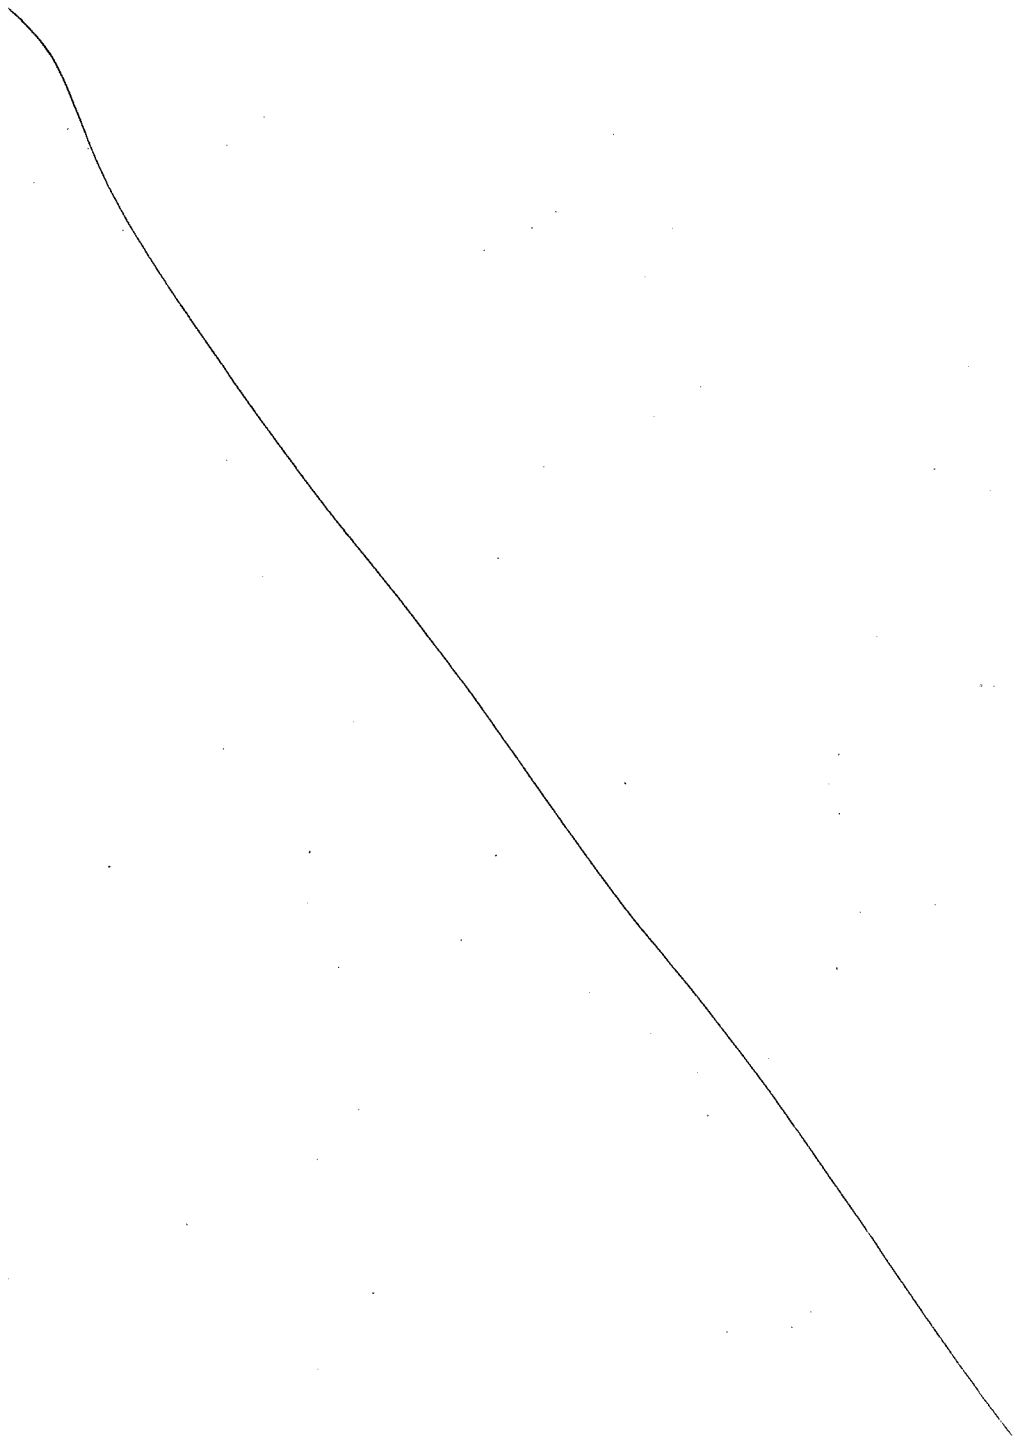

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

RCD. Govt. of Bihar, vide letter no. 3376 (E) dt. 17.08.2010. The Performance Security should be deposited within 10 (Ten) days of receipt of this Letter of Acceptance (LOA) valid up to 28 (Twenty eight) days from the date of expiry of defect liability period.

In the interest of the work Agencies are instructed to proceed with the execution of the said work in consultation with concerned Engineer-in-Charge with immediate effect. The date of start of this work will be the date of issue of this letter. The agreement will be executed after verification of Performance Security and Registration in appropriate category in this Corporation.

Yours faithfully


Chief Consultant(Technical)

Patna. Date. 20.02.14


817

Memo no: BSEIDC/TECH/164/2013-


Copy forwarded to : i) Executive Engineer I/C of the Project.


ii) Senior Account Officer. BSEIDC. Patna.

Chief Consultant(Technical)


Chief Consultant (Technical)
Bihar State Educational Infrastructure
Development Corporation Ltd., Patna

Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Pmb


25-6-2014

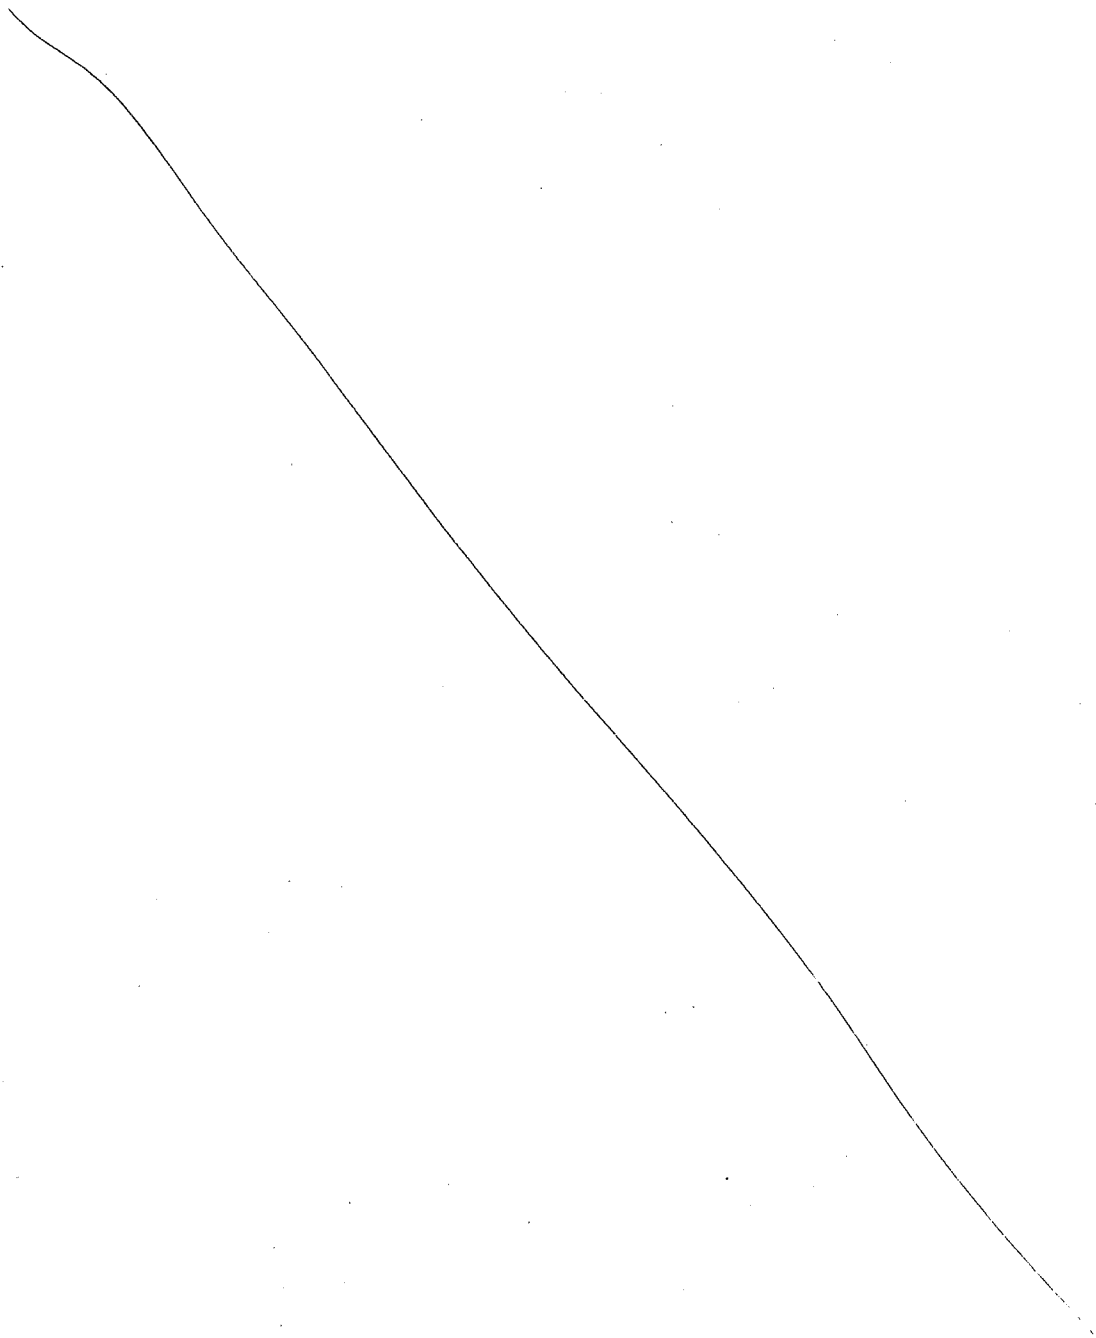

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

BIHAR STATE EDUCATIONAL INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.							
SHIKSHA BHAWAN, SAIDPUR, PATNA							
B.O.Q FOR 10+2 SCHOOLS IN BIHAR							
THE ITEM RATES ARE BASED ON S.O.R BCD BIHAR, Dated-11.08.2013 & DSR (CIVIL&ELECTRICAL) 2012.							
Group No. :- S.S.S-153							
Sl. No.	District	Name of School					
1		10 + 2 SCHOOL, KASER					
2	KAIMUR	10 + 2 SCHOOL, SINDHI					
Amount of B.O.Q				:- Rs. 2,10,10,782			
Earnest Money				:-Rs. 4,20,216			
Cost of B.O.Q				:- Rs. 15,650			
Time of Completion				:- 15 Months			
BUILDING WORKS: (Quantity Per School)							
Sl. No.	SOR Item No.	SUB No.	Item of Work	Qty.	Unit	Rate (Rs.)	Amount (Rs.)
1	2	3	4	5	6	7	8
			CIVIL WORKS (1% labour cess included in SOR)				
1	23.2		Boring providing and installing bored cast in-situ <u>reinforced cement concrete pile</u> of specified diameter and length below the pile cap in cement concrete 1:1.5:3(1 cement: 1.5 coarse sand :3 graded stone aggregate 20 mm nominal size) to carry a safe working load not less than specified, excluding the cost of steel reinforcement but including the cost of boring with casing and /or bentonite solution and the length of the pile to be embedded in the pile cap. (Length of pile for payment shall be measured upto bottom of pile cap).				
		23.2.1	300 mm dia Pile	0.000	Meter	385.200	Rs. Three hundred eighty five and paise twenty only.
		23.2.2	400 mm dia Pile	0.000	Meter	686.000	Rs. Six hundred eighty six only.
		23.2.3	450 mm dia Pile	0.000	Meter	868.600	Rs. Eight hundred sixty eight and paise sixty only.
		23.2.4	600 mm dia Pile	0.000	Meter	1544.300	Rs. One thousand five hundred forty four and paise thirty only.
		23.2.5	Making 25 cm (10") dia bore up to 4 mtr depth below ground with hand auger of approved quality in ordinary soil (vide classification of soil item A) true to plumb and without eccentricity in any stage of operation and disposal of the excavated earth up to 50 mtr, Lead including all lifts , all complete as per approved design and direction of E/I.	0.000	Meter	80.400	Rs. Eighty and paise forty only.

310723712 RAE


Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Rmb

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

		23.2.6	63 CM (25) UNDER -REAM Making 63 cm (25) dia under ream as required with hand auger of approved quality in ordinary soil (vide classification of soil item - A) true to plumb and without eccentricity in any stage of operation and disposal of the excavated earth up to 50 mts lead including all lifts , all complete as per approved design and direction of (E/I).	0.000	Meter	85.700	Rs. Eighty five and paise seventy only.
2	23.3		Boring, Providing and installing cast in situ <u>single under reamed piles</u> of specified diametre and length below pile cap in cement concrete piles with mix 1:1.5:3 (1 cement:1.5 coarse sand:3 graded stone aggregate 20 mm nominal size) to carry a safe working load not less than specified, excluding the cost of steel reinforcement but including the cost of boring with bentonite solution and the length of the pile to be embedded in pile cap etc all complete.(Length of piie for payment shall be measured upto to the bottom of pile cap).				
		23.3.1	300 mm dia Pile	0.000	Meter	446.300	Rs. Four hundred forty six and paise thirty only.
		23.3.2	400 mm dia Pile	0.000	Meter	846.100	Rs. Eight hundred forty six and paise ten only.
		23.3.3	450 mm dia Pile	0.000	Meter	1090.500	Rs. One thousand ninety and paise fifty only.
		23.3.4	500 mm dia Pile	0.000	Meter	1315.300	Rs. One thousand three hundred fifteen and paise thirty only.
3	23.4		Extra over item no 23.3 for boring,providing and installing cast in situ double under reamed piles, instead of single under ream of specified diameter and length. (Only the quantity of extra bulbs are to be paid).	0.000	Each	614.700	Rs. Six hundred fourteen and paise seventy only.
4	2.8		Earthwork in excavation in areas(exceeding 30cm in depth. 1.5 m in width as well es 10 sqm on plan) including dressing of sides and ramming of bottom,lift upto 1.5m including getting out the excavated soil and disposal of surplus soil as directed within a lead of				
		2.8.1	All Kind of soil 10+2,Building =670.430 cum Septic Tank =31.89 cum Total quantity =702.32cum	702.320	cum	178.40	Rs. One hundred seventy eight and paise forty only.
5	2.29		Surface dressing of the ground including removing vegetation and inequalities not exceeding 15 cm depth and disposal of rubbish, lead upto 50 m and lift upto 1.5 m.				

अजय कुमार सिंह

Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Rm8

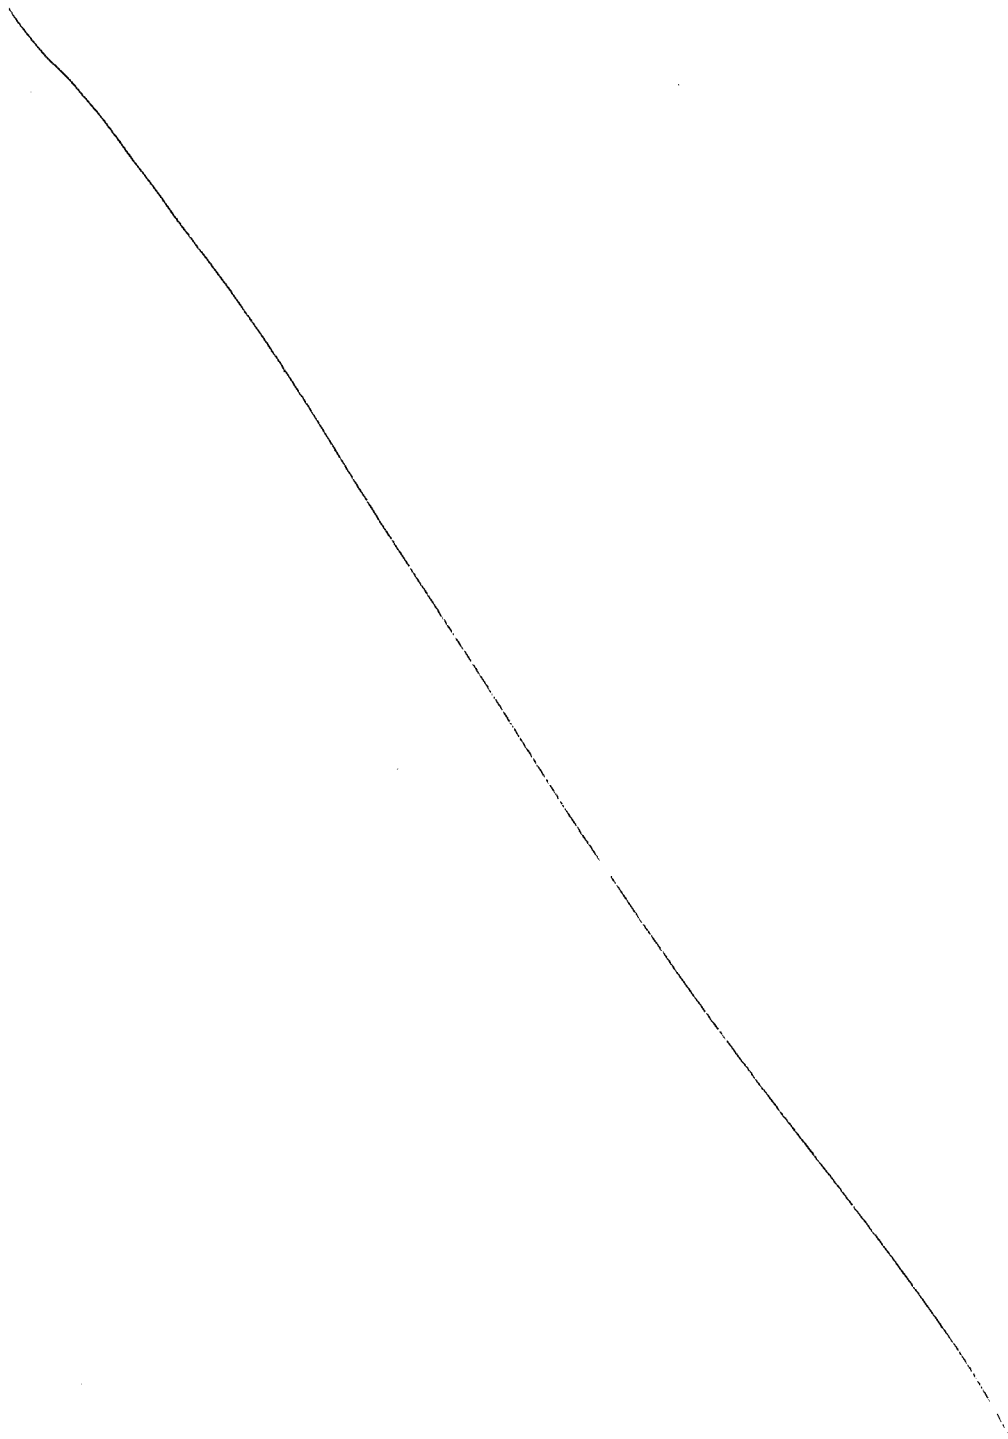


		2.29.1	All Kind of soil 10+2,Building =472.560 sqm	472.560	100 sqm	642.50	Rs. Six hundred forty two and paise fifty only.
6	2.26		Filling available excavated earth (excluding rock) in trenches and plinth, side of foundation etc. in layers not exceeding 20 cm. in depth consolidating each deposited layer by ramming and watering lead.	506.490	cum	57.80	Rs. Fifty seven and paise eighty only.
7	2.28		Supplying and filling in plinth with local sand and under floors including watering, ramming consolidating and dressing complete. 10+2,Building =406.030 cum Septic Tank =1.02 cum Total quantity =407.05cum	407.050	cum	186.30	Rs. One hundred eighty six and paise thirty only.
8	11.72		Providing designation 100A one brick flat soling joints filled with local sand including cost of watering taxes royalty all complete as per building specification and direction of E/I. 10+2,Building =791.720 sqm Septic Tank =13.57 sqm Total quantity =805.29 sqm	805.290	sq.m	212.900	Rs. Two hundred twelve and paise ninety only.
9	4.5		Providing and laying in position cement concrete of specified grade excluding the cost of centring and shuttering- all work upto plinth level.				
		4.5.5	1:3:6 (1cement: 3 coarse sand : 6 graded stone aggregate 20mm nominal size) 10+2,Building =33.130 cum Septic Tank =2.98 cum Total quantity =36.11cum	36.110	cum	2688.70	Rs. Two thousand six hundred eighty eight and paise seventy only.
		4.5.8	1:4:8 (1cement: 4 coarse sand : 8 graded stone aggregate 40mm nominal size) 10+2,Building =26.250 cum	26.250	cum	2245.10	Rs. Two thousand two hundred forty five and paise ten only.
10	11.38		Providing and laying Ceramic glazed floor tiles 300x300 mm (thickness to be specified by the manufacturer) of 1st quality conforming to IS : 15622 of approved make in all colours, shades, except White, Ivory, Grey, Fume Red Brown laid on 20mm thick bed of Cement Mortar 1:4 (1 cement : 4 Coarse sand) including pointing the joints with white cement and matching pigments etc. complete. 10+2,Building =34.310 cum	34.310	sq.m	922.000	Rs. Nine hundred twenty two only.

अभिषेक झा

Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Rm8

25-6-2014

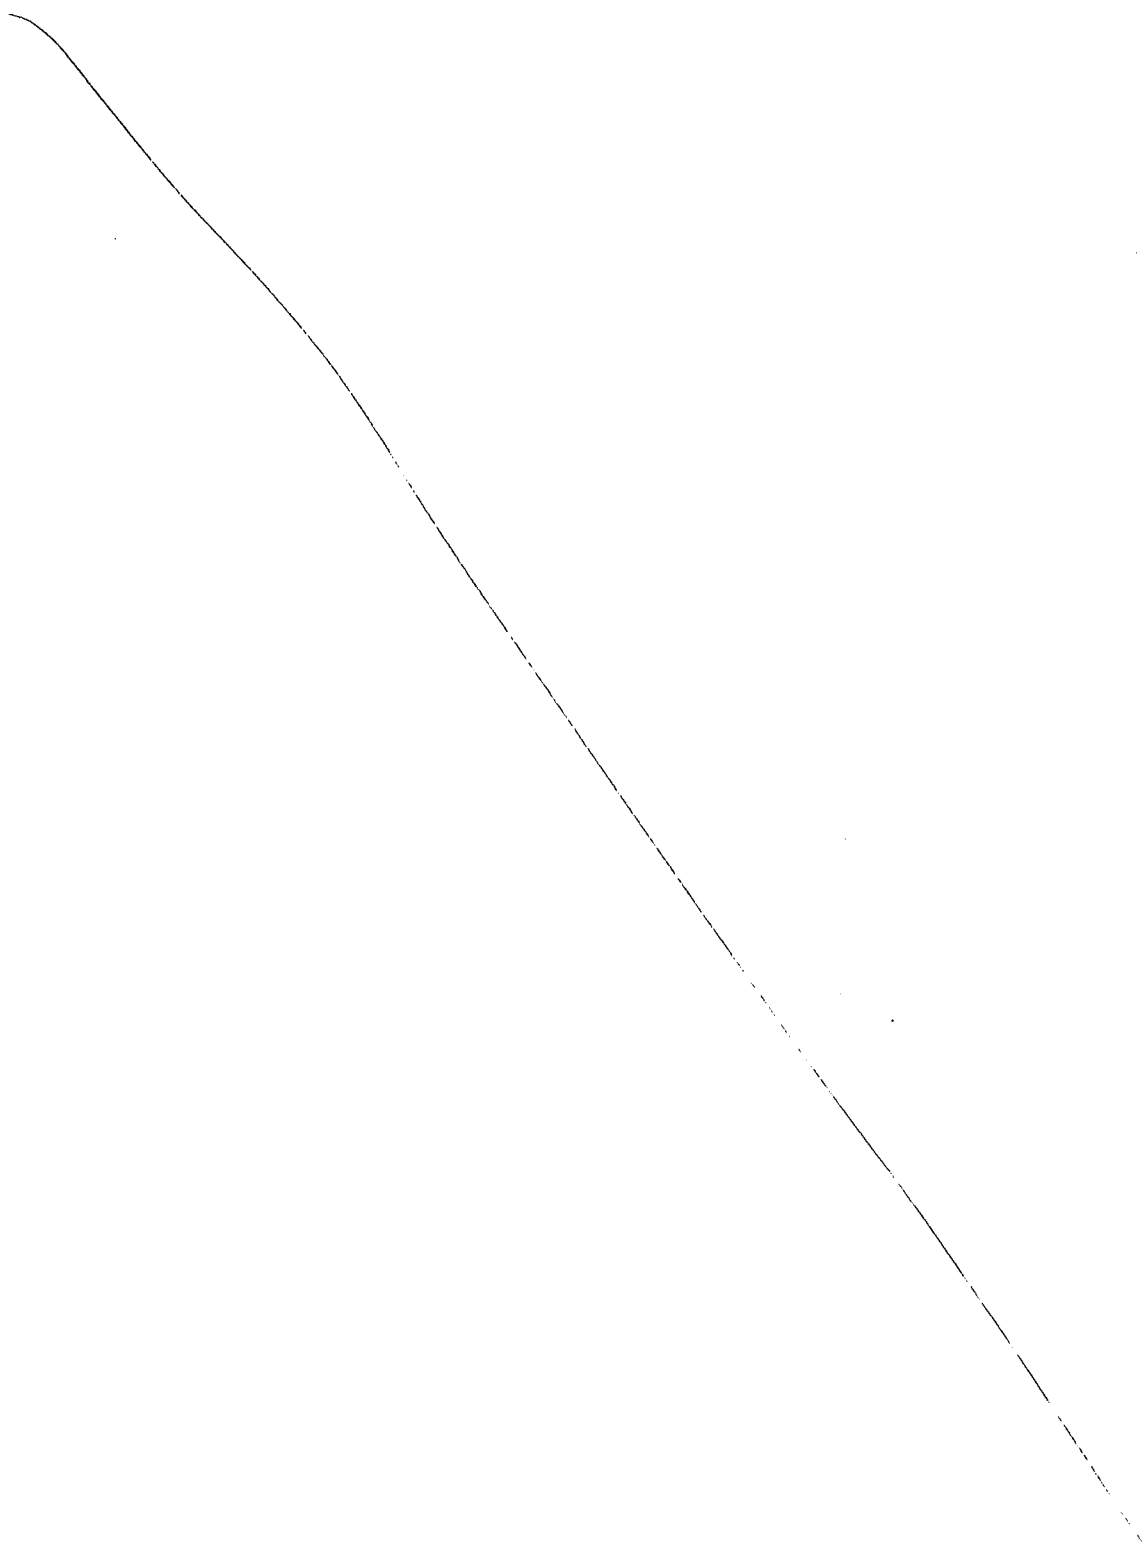


Chief Engineer
B.S.E.I.D.C. Ltd, Patna

11	11.36		Providing and fixing 1st quality Ceramic glazed wall tiles conforming to IS : 15622 (thickness to be specified by the manufacturer) of approved make in all colours, shades, except burgundy, bottle green, black of any size as approved by Engineer-in-charge in skirting, risers of step and dados over 12 mm thick bed of Cement Mortar 1:3 (1 cement : 3 Coarse sand) and jointing with grey cement slurry @ 3.3 kg per sqm including pointing in white cement mixed with pigments of matching shade complete. 10+2, Building = 127.980 cum	127.980	sq.m	844.000	Rs. Eight hundred forty four only.
12	11.17		40 mm thick marble chips flooring, rubbed and polished to granolithic finish, under layer 28 mm thick cement concrete 1:2:4 (1 cement:2 coarse sand:4 graded stone aggregate 12.5 mm nominal size) and top layer 12 mm thick with white, black, chocolate, grey, yellow or Baroda green marble chips of sizes for 7 mm to 10 mm nominal size laid in cement marble powder mix 3:1 (3 cement : 1 marble powder mix : 3 marble chips) by volume including cement slurry etc. complete				
		11.17.2	Light shade pigment with white cement 10+2, Building at Flooring = 848.933 sqm 10+2, Building at Skirting = 51.750 sqm Total quantity = 900.683 sqm	900.683	sqm	418.100	Rs. Four hundred eighteen and paise ten only.
13	11.20		Providing and fixing glass strips in joints of terrazo/cement concrete floors.				
		11.20.1	40 mm wide and 4 mm thick 10+2, Building = 2500 Meter	2500.000	Meter	24.000	Rs. Twenty four only.
14	5.1		Providing and laying in position specified grade of reinforced cement concrete excluding the cost of centring, shuttering, finishing & reinforcement - all work upto plinth level.				
		5.1.1	1:1:2 (1 cement: 1 coarse sand : 2 graded stone aggregate 20mm nominal size) 10+2, Building = 62.928 cum	62.928	cum	5145.40	Rs. Five thousand one hundred forty five and paise forty only.
		5.1.3	1:2:4 (1 cement:2 coarse sand:4 graded stone aggregate 20 mm nominal size) Septic Tank = 0.93 cum	0.930	cum	3380.80	Rs. Three thousand three hundred eighty and paise eighty only.
15	5.2		Reinforced cement concrete work in wall (any thickness), including attached pilasters, buttresses, plinth and struts etc upto floor five level excluding the cost of centring, shuttering, finishing & reinforcement.				
		5.2.1	1:1:2 (1 cement: 1 coarse sand : 2 graded stone aggregate 20mm nominal size) 10+2, Building = 44.710 cum	44.710	cum	5567.10	Rs. Five thousand five hundred sixty seven and paise ten only.

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

Per

31/12/2018

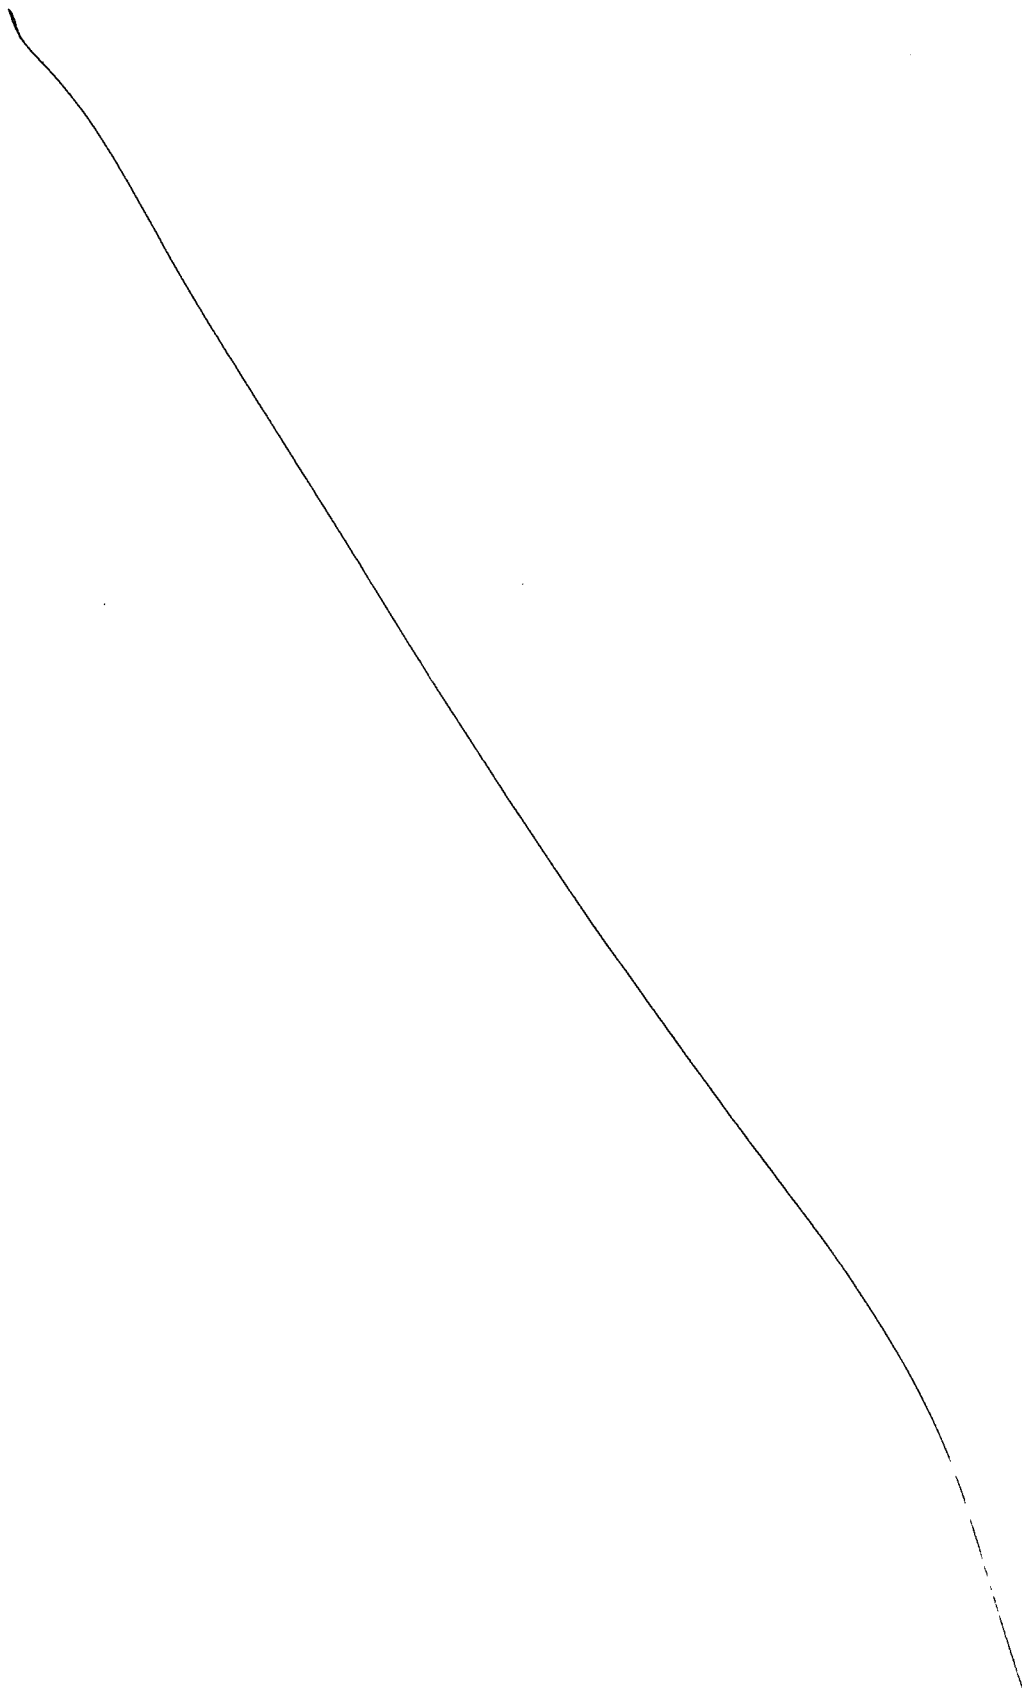


Chief Engineer
B.S.E.I.D.C. Ltd, Patna

16	5.3		Reinforced cement concrete work in beams, suspended floors, roofs having slope upto 15°, landings, balconies, shelves, chajjas, lintels, bands, plain window sills, staircases and spiral staircases upto floor five level excluding the cost of centring, shuttering, finishing & reinforcement.				
		5.3 + 5.44.4 + 5.44.1	1:2:4 (1cement: 2 coarse sand : 4 graded stone aggregate 20mm nominal size) (Extra for Providing M-20 grade RCC instead of M-15 grade RCC) (Extra for Providing M-25 grade R.C.C instead of M-20 grade R.C.C) 10+2,Building =222.050 cum	222.050	cum	4328.22	Rs. Four thousand three hundred twenty eight and paise twenty two only.
17	6.1A		Brick work with bricks of class designation 100A :				
		6.1.14A	In foundations and plinth level Cement mortar 1:6 (1 cement: 6 coarse sand) 10+2,Building =60.682 cum	60.682	cum	3713.50	Rs. Three thousand seven hundred thirteen and paise fifty only.
		6.1.14A + 6.3A	In superstructure above plinth level upto five floor in cement mortar 1:6 (1cement :6 coarse sand) 10+2,Building =263.754 cum	263.754	cum	4092.30	Rs. Four thousand ninety two and paise thirty only.
		6.1A + 6.1.12/1	In foundations and plinth level Cement mortar 1:4 (1 cement: 4 coarse sand) Septic Tank=8.75 cum	8.750	cum	3914.60	Rs. Three thousand nine hundred fourteen and paise sixty only.
18	6.18A		Half brick masonry with bricks of class designation 100A :				
		6.18.4A + 6.19A	In superstructure above plinth level upto five floor in cement mortar 1:4 (1cement :4 coarse sand) 10+2,Building =86.117 sqm	86.117	sqm	500.10	Rs. Five hundred and paise ten only.
19	6.21A		Extra for providing and placing in position 2 nos. 6 mm dia MS bars at every third course of half brik masonry (with F.P.S. brick) 10+2,Building =86.117 sqm	86.117	sqm	68.70	Rs. Sixty eight and paise seventy only.
20	13.13		20 mm cement plaster of mix ;				
		13.13.4	1:6 (1 cement: 6 coarse sand) 10+2,Building =954.147 sqm	954.147	sqm	110.00	Rs. One hundred ten only.
		13.13.1 + 13.26	1:3 (1 cement: 3 coarse sand) with neat cement punning Septic Tank=16.65 sqm	16.650	sqm	172.00	Rs. One hundred seventy two only.
			12mm thick Cement plaster of mix				

31/07/2014

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

Enb

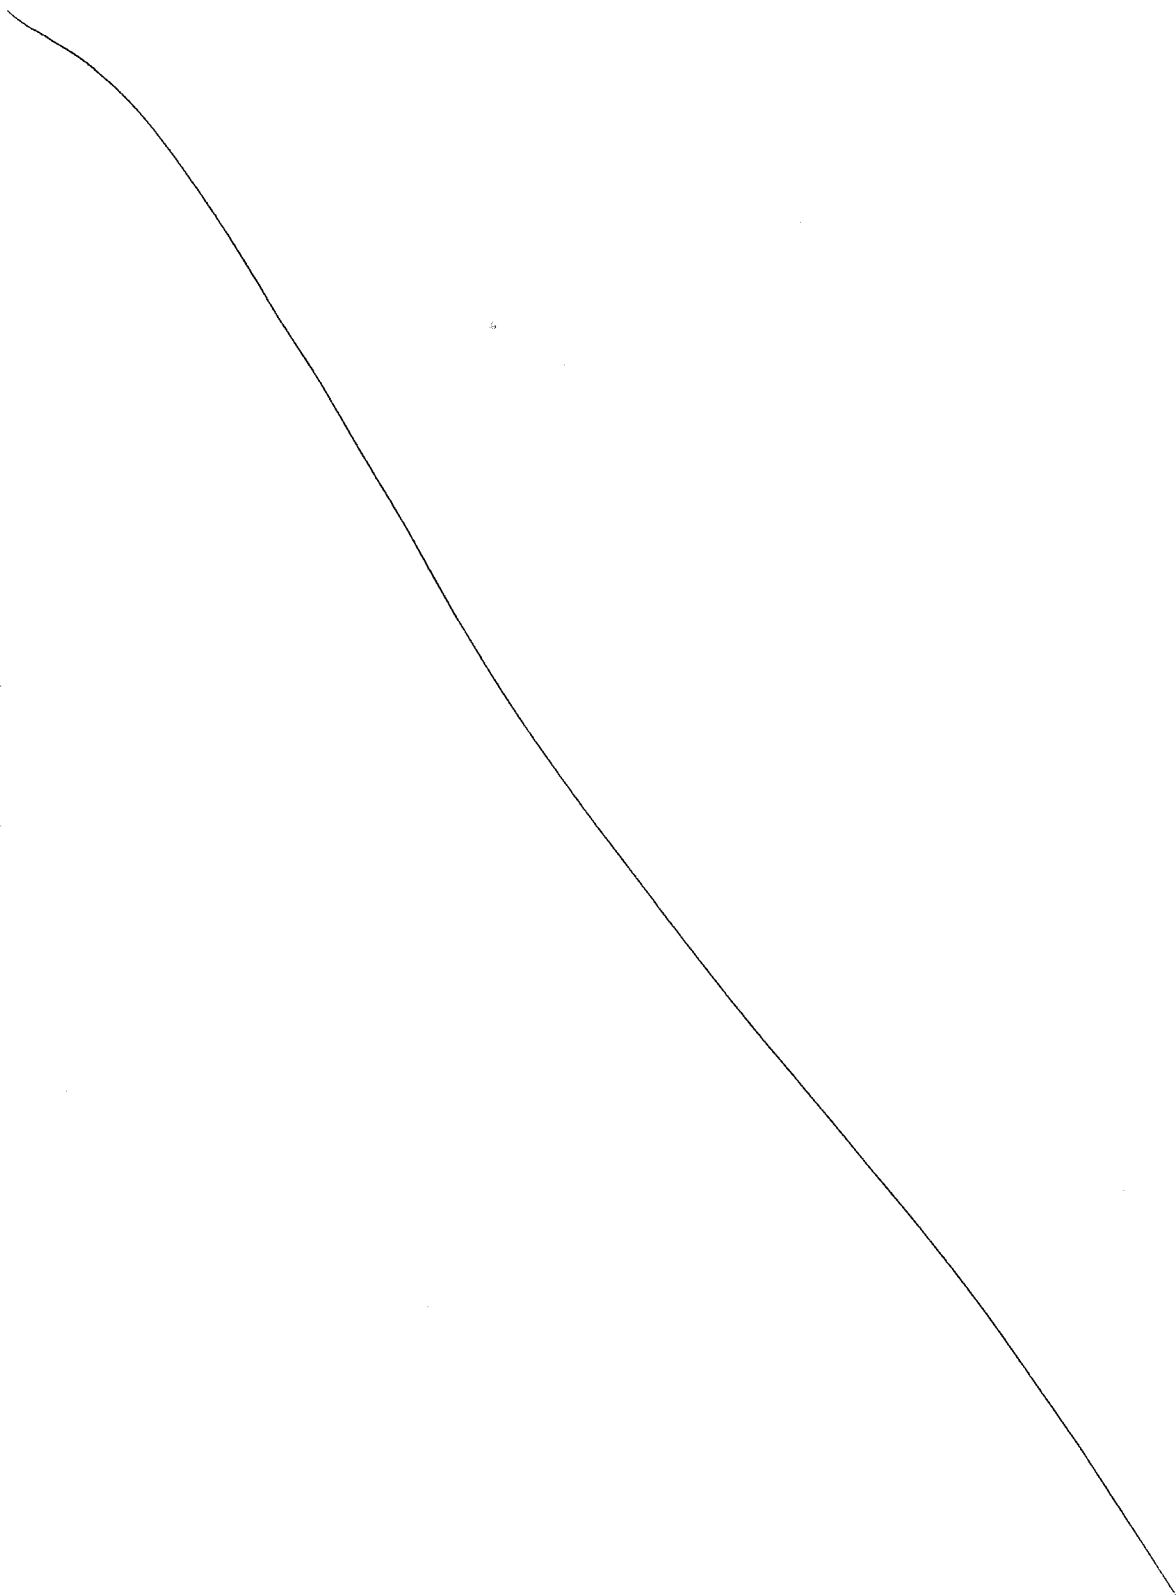

Chief Engineer
B.S.E.I.D.C. Ltd, Patna


- 14 -

21	13.11	13.11.4	1:6 (1 cement : 6 coarse sand) 10+2, Building = 1813.410 sqm	1813.410	sqm	79.10	Rs. Seventy nine and paise ten only.
22	13.17 + 13.36.1		1:3 (1 cement: 3 coarse sand) finished with a floating coat of neat cement & Extra for providing and mixing water proofing material in proportion recommended by the manufacturers 12 mm cement plaster 1:3 (1 cement : 3 sand) Septic Tank = 52.82 sqm	52.820	sqm	132.10	Rs. One hundred thirty two and paise ten only.
23	13.24	13.24.2	6mm thick Cement plaster of Ceiling Mix 1:4 (1 cement : 4 coarse sand) 10+2, Building = 861.050 sqm	861.050	sqm	68.20	Rs. Sixty eight and paise twenty only.
24	11.4		Cement concrete flooring 1:2:4 (1 cement : 2 coarse sand : 4 graded stone aggregate) finished with a floating coat of neat cement including cement slurry, etc. but excluding the cost of nosing of steps etc.				
		11.4.2 + 11.14	40 mm thick with 20 mm nominal size stone aggregate. Extra for making chequers of approved pattern on cement concrete floors, steps, landing, pavements etc.	467.230	sqm	224.20	Rs. Two hundred twenty four and paise twenty only.
25	13.77A		Distemping with 1st quality washable distemper (ready made) of approved manufacturer and of required shade and colour complete. As per manufacture's specifications.				
		13.77A.1	Two or more coats on new work. 10+2, Building External Wall = 954.147 sqm 10+2, Building Internal Wall & Ceiling = 2674.460 sqm Total quantity = 3628.607 sqm	3628.607	sqm	28.70	Rs. Twenty eight and paise seventy only.
26	13.81		Applying priming coat				
		13.81.1	with ready mixed pink or grey primer of approved brand and manufacture on wood work (hard and softwood) 10+2, Building = 257.040 sqm	257.040	sqm	20.50	Rs. Twenty and paise fifty only.
		13.81.3	with ready mixed zinc chromate yellow primer of approved brand and manufacture on steel galvanized iron/steel	145.260	sqm	16.40	Rs. Sixteen and paise forty only.
27	13.93		Painting with synthetic enamel paint of approved brand and manufacture to give				
		13.93.1	Two or more coats on new work 10+2, Building = 402.300 sqm	402.300	sqm	42.00	Rs. Forty two only.
28	10.1		Structural steel work in singal section fixed without connecting plate including cutting, hoisting, fixing in position and applying a priming coat of approved steel primer. all complete. 10+2, Building = 781.200 Kg	781.200	Kg	55.40	Rs. Fifty five and paise forty only.
			Providing and fixing flush door shutters decorative type core of block board construction with frame of 1st class hard				

31/05/2014

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

25-6-2014

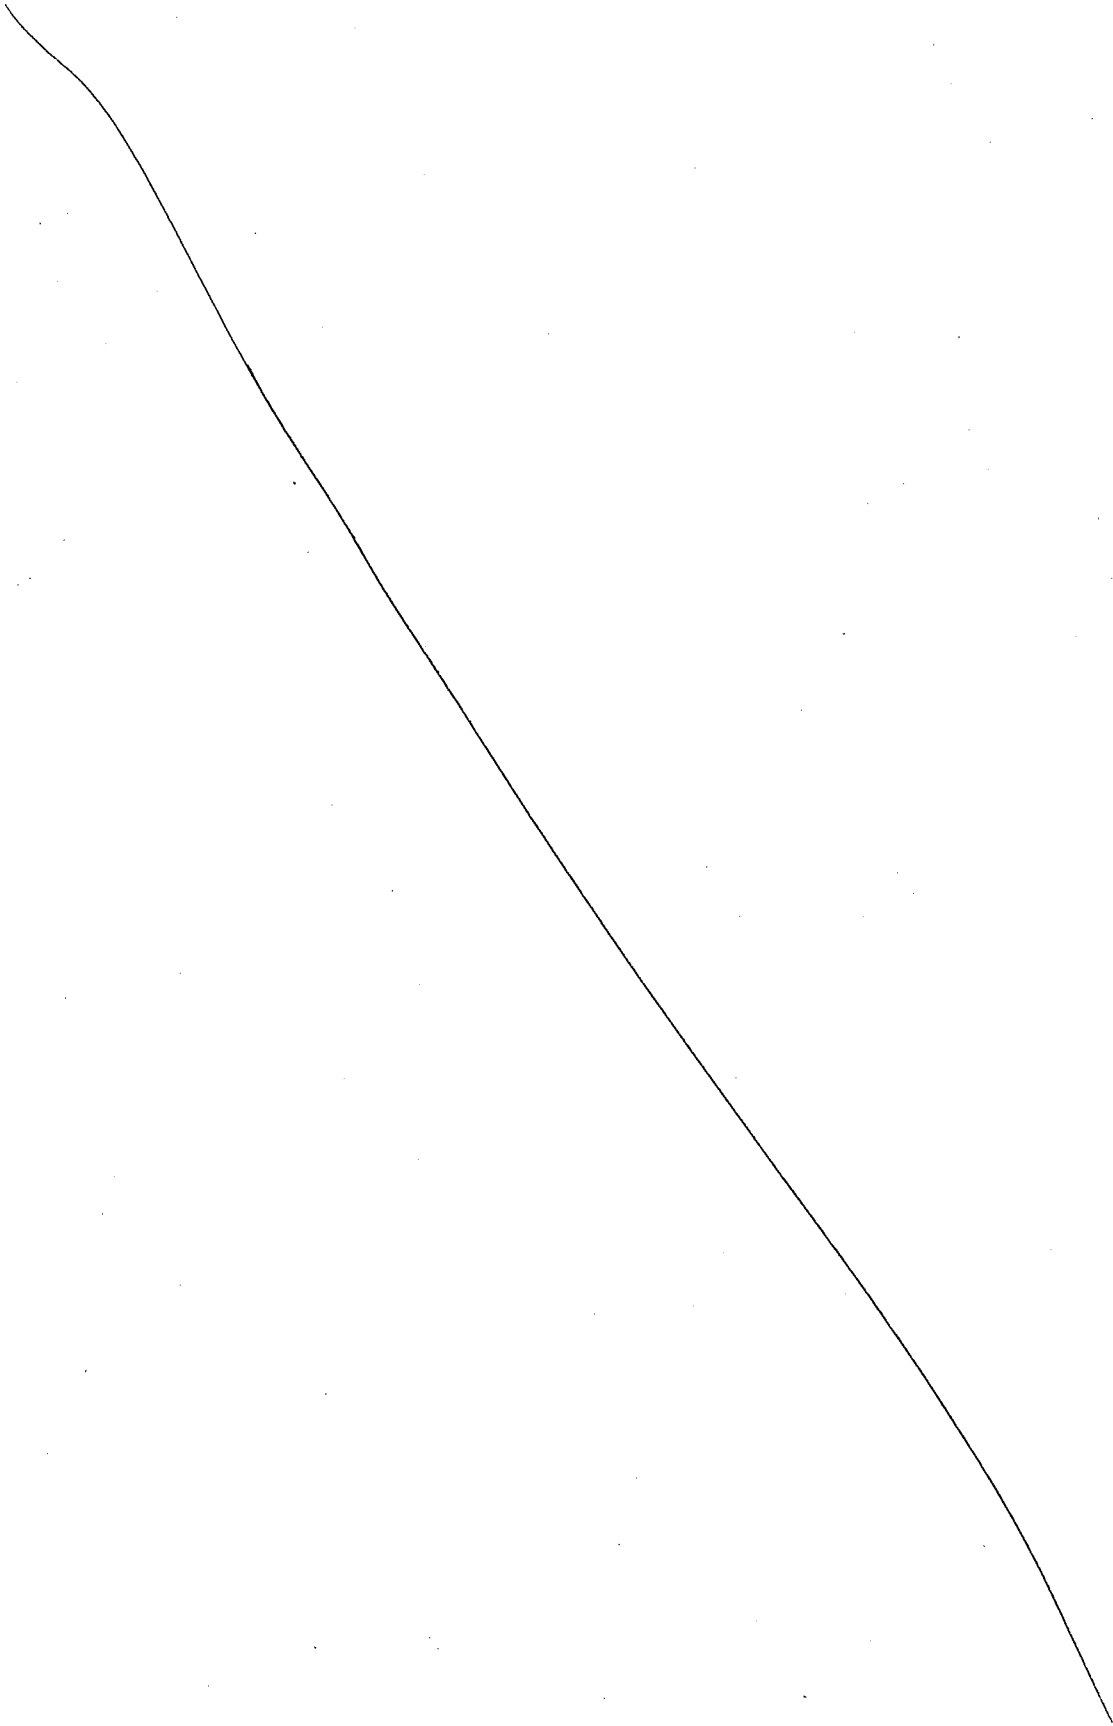


Chief Engineer
B.S.E.I.D.C. Ltd, Patna

29	9.24	9.24.2	35 mm thick including stainless steel butt hinges with necessary screws 10+2,Building =107.100 sqm	107.100	sqm	2336.40	Rs. Two thousand three hundred thirty six and paise forty only.
30	10.12		Providing and fixing glazed steel doors, windows or ventilators of standard rolled steel sections, joints mitered and welded with 15x3 mm M.S. lugs 10cm long with steel legs embedded in cement concrete blocks 15x10x10cm. of (1:3:6) (1 cement : 3 coarse sand : 6 graded stone aggregate				
		10.12.1 + 10.13B	Doors & Steel windows 10+2,Building =133.200 sqm	133.200	sqm	3197.50	Rs. Three thousand one hundred ninety seven and paise fifty only.
		10.12.1 + 10.13C	Doors & Steel ventilators 10+2,Building =5.580 sqm	5.580	sqm	3203.30	Rs. Three thousand two hundred three and paise thirty only.
31	9.82		Providing and fixing M.S. grills of required pattern in frames of windows etc. with M.S. flats, square or round bars etc all complete.				
		9.82.1	Fixed to steel windows by welding. 10+2,Building =3195.720 Kg	3195.720	Kg.	83.90	Rs. Eighty three and paise ninety only.
32	5.29		Reinforcement for RCC work including straightening, cutting, bending, placing in position and binding all complete.				
			TMTC-500				
		5.29.7A	TMTC-500 8mm dia 10+2,Building =15421 Kg Septic Tank =93 Kg Total quantity =15514 Kg	15514.000	Kg.	67.00	Rs. Sixty seven only.
		5.29.7B	TMTC-500 10mm dia 10+2,Building =919 Kg	919.000	Kg.	65.70	Rs. Sixty five and paise seventy only.
		5.29.7C	TMTC-500 12mm dia 10+2,Building =11728 Kg	11728.000	Kg.	65.10	Rs. Sixty five and paise ten only.
		5.29.7D	TMTC Fe-500 16mm dia 10+2,Building =2346 Kg	2346.000	Kg.	65.70	Rs. Sixty five and paise seventy only.
		5.29.7E	TMTC Fe-500 20mm dia 10+2,Building = 717 Kg	717.000	Kg	65.50	Rs. Sixty five and paise fifty only.
		5.29.7F	TMTC Fe-500 25mm dia 10+2,Building = 2321 Kg	2321.000	Kg	65.50	Rs. Sixty five and paise fifty only.

8/10/2018

Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Rm

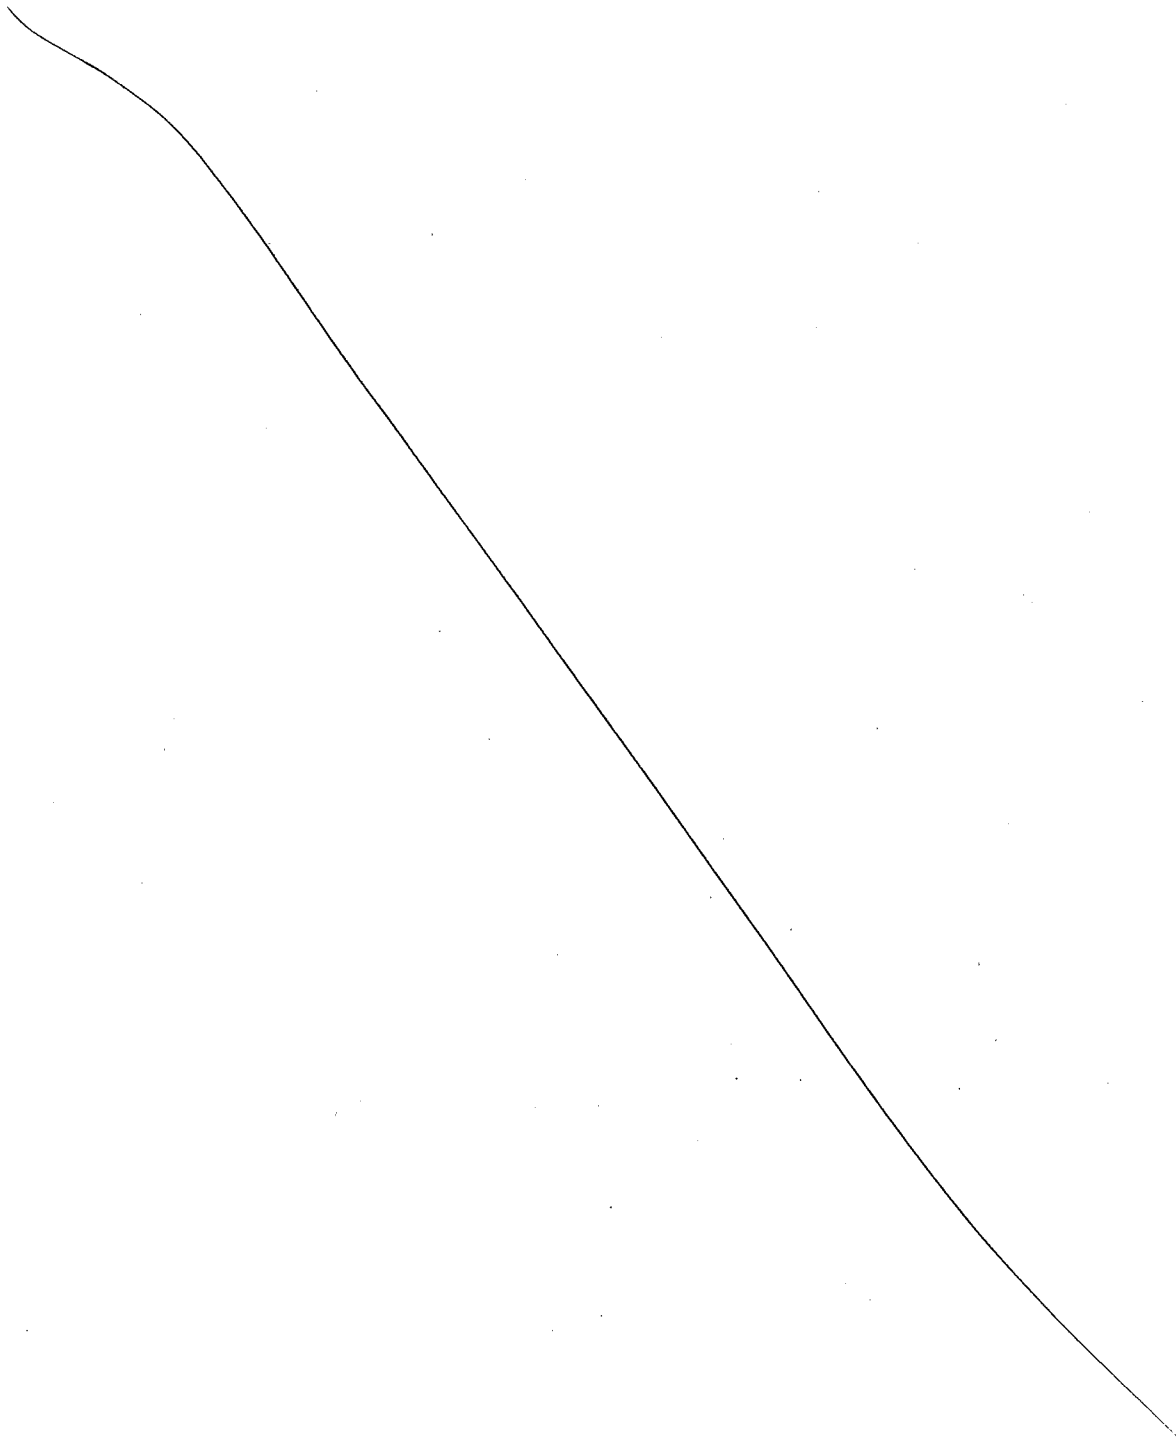


Chief Engineer
B.S.E.I.D.C. Ltd, Patna

33	10.19		Providing & fixing M.S. Fan hook of 16 mm dia M.S bar 1 Mtr. Long bent to required size and shape, placed in position and fixed in Truss Frame / RCC Slab / beam at the time of casting all complete as per building specification and direction of E/I. (Where materials is not supplied by deptt. 10+2,Building = 60.0 Each	60.000	Each	108.20	Rs. One hundred eight and paise twenty only.
34	10.33		Providing & fixing hand rail.by welding etc. to steel ladder railing & staircases railing including applying a priming coat of approved steel primer.				
		10.33.1	MS tube (medium) 40mm nominal bore. 10+2,Building = 470.0 Kg	470.000	kg.	81.60	Rs. Eighty one and paise sixty only.
35	DSR 4.17		Making plinth protection 50mm thick of cement concrete 1:3:6 (1 cement :3 coarse sand : 6 graded stone aggregate 20mm nominal size) over 75mm bed of dry brick ballast 40mm nominal size well rammend and consolidated and grouted with fine sand including finishing the top smooth. 10+2,Building = 96.713 sqm	96.713	sqm	342.14	Rs. Three hundred forty two and paise fourteen only.
36	5.14		Centring and shuttering including strutting, propping etc. and removal of				
		5.14.1	Foundation, footings, bases of columns etc. for mass concrete. 10+2,Building = 112.308 sqm	112.308	sqm	137.78	Rs. One hundred thirty seven and paise seventy eight only.
		5.14.5	Lintel, beams, plinth beams, griders, bressumers and cantilevers.	602.565	sqm	195.600	Rs. One hundred ninety five and paise sixty only.
		5.14.6	Columns, pillars, piers, abutments, posts and struts. 10+2,Building = 804.84 sqm	804.840	sqm	283.300	Rs. Two hundred eighty three and paise thirty only.
		5.14.3	Suspended floors, roofs, landings, balconies and access platform. 10+2,Building = 922.610 sqm	922.610	sqm	229.800	Rs. Two hundred twenty nine and paise eighty only.
						Total = (A)	8,485,530.96
37			Plumbing and Sanitary Works (1% labour cess has been added on current SOR as labour cess is not included in current SOR).				
38	B.S.R 12.78		Providing and fixing on wall face unplasticised PVC (working pressure 4 kgf per sqm) rain water pipes conforming to IS:4985 including jointing with seal ring conforming to IS:5382 leaving 10 mm gap for thermal expansion.				
		12.78.2	110 mm diameter. 10+2, Building =50 MTS	50.000	MTS	199.600	Rs. One hundred ninety nine and paise sixty only.
39	D.S.R 17.1		Providing and fixing water closet squatting pan (Indian type W.C. pan) with 100 mm sand cast iron P or S tap, 10 litre low white P.V.C. Flushing cistern with manually controlled device (handle lever) conforming to IS : 7231 Parryware/Hindware with all fittings and fixtures complete including cutting and making good the walls and floors wherever required.				

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

Encl.

31/04/2014

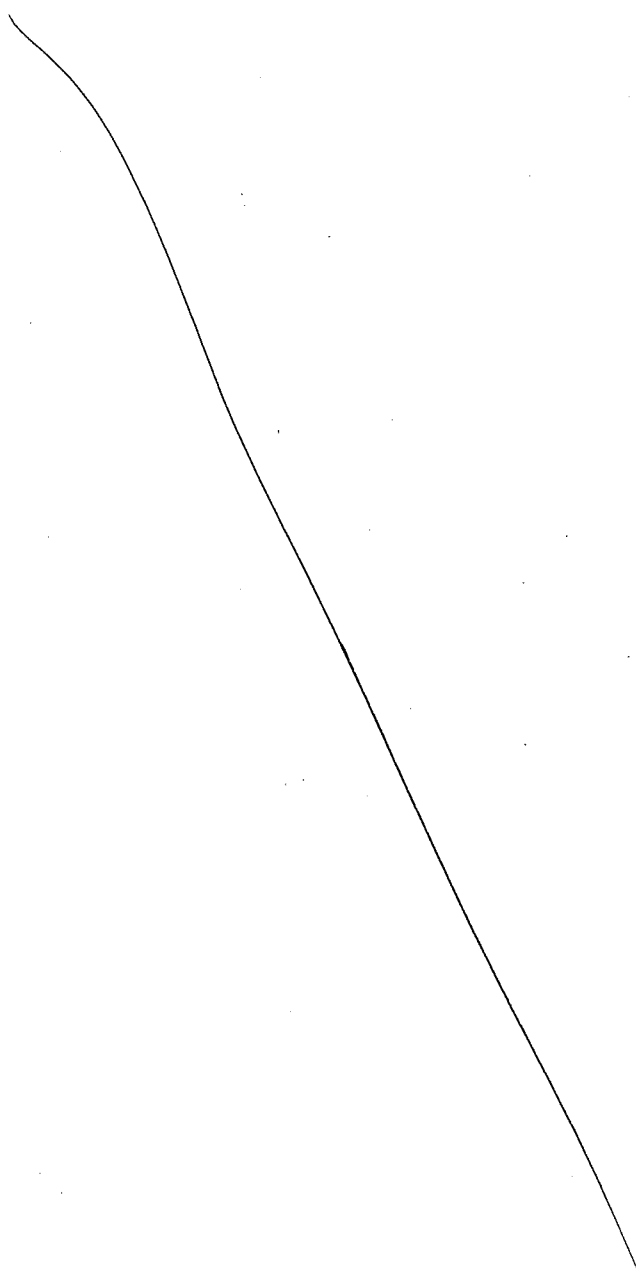


		D.S.R 17.1.1	White Vitreous China Orissa pattern W C pan of size 580 x 440 mm with integral type foot rest. 10+2, Building =5 Each	5	Each	2,993.74	Rs. Two thousand nine hundred ninety three and paise seventy four only.
40	D.S.R 17.2		Providing and fixing white vitreous china pedestal type water closet (European type W.C. pan) with seat and lid, 10 litre low level white P.V.C. flushing cistern, including flush pipe, with manually controlled device (handle lever), conforming to IS : 7231, with all fittings and fixtures complete, including cutting and making good the walls and floors wherever required :				
		D.S.R 17.2.2	W.C. pan with ISI marked black solid plastic seat and lid 10+2, Building =5 Each	5	Each	2894.00	Rs. Two thousand eight hundred ninety four only.
41	D.S.R 17.4		Providing and fixing white vitreous china flat back or wall corner type lipped front urinal basin of 430x260x350 mm and 340x410x265 mm sizes respectively with automatic flushing cistern with standard flush pipe and C.P. brass spreaders with brass unions and G.I. clamps complete, including painting of fittings and brackets, cutting and making good the walls and floors wherever required :				
		D.S.R 17.4.3	Range of three urinal basins with 10litre white P.V.C. automatic flushing cistern. 10+2, Building =6 Each	6	Each	6,292.20	Rs. Six thousand two hundred ninety two and paise twenty only.
42	D.S.R 17.7		Providing and fixing wash basin with C.I. brackets, 15 mm C.P. brass pillar taps, 32 mm C.P. brass waste of standard pattern, including painting of fittings and brackets, cutting and making good the walls wherever require :				
		D.S.R 17.7.1	White Vitreous China Wash basin size 630x450 mm with a pair of 15 mm C.P. brass pillar taps. 10+2, Building =10 Each	10	Each	1,866.83	Rs. One thousand eight hundred sixty six and paise eighty three only.
43	D.S.R 17.28		Providing and fixing P.V.C. waste pipe for sink or wash basin including P.V.C. waste fittings complete.				
		D.S.R 17.28.2.1	Flexible pipe 32 mm dia 10+2, Building =10 Each	10	Each	65.95	Rs. Sixty five and paise ninety five only.
44	D.S.R 17.32		Providing and fixing mirror of superior glass (of approved quality) and of required shape and size with plastic moulded frame of approved make and shade with 6 mm thick hard board backing :				
		D.S.R 17.32.2	Rectangular shape 453 x 357 mm 10+2, Building =10 Each	10	Each	604.28	Rs. Six hundred four and paise twenty eight only.
45	D.S.R 17.33		Providing and fixing 600 x 120 x 5 mm glass shelf with edges round off, supported on anodised aluminium angle frame with C.P. brass brackets and guard rail complete fixed with 40 mm long screws, rawl plugs etc., complete. 10+2, Building =10 Each	10	Each	344.66	Rs. Three hundred forty four and paise sixty six only.

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

31074332



Rmd

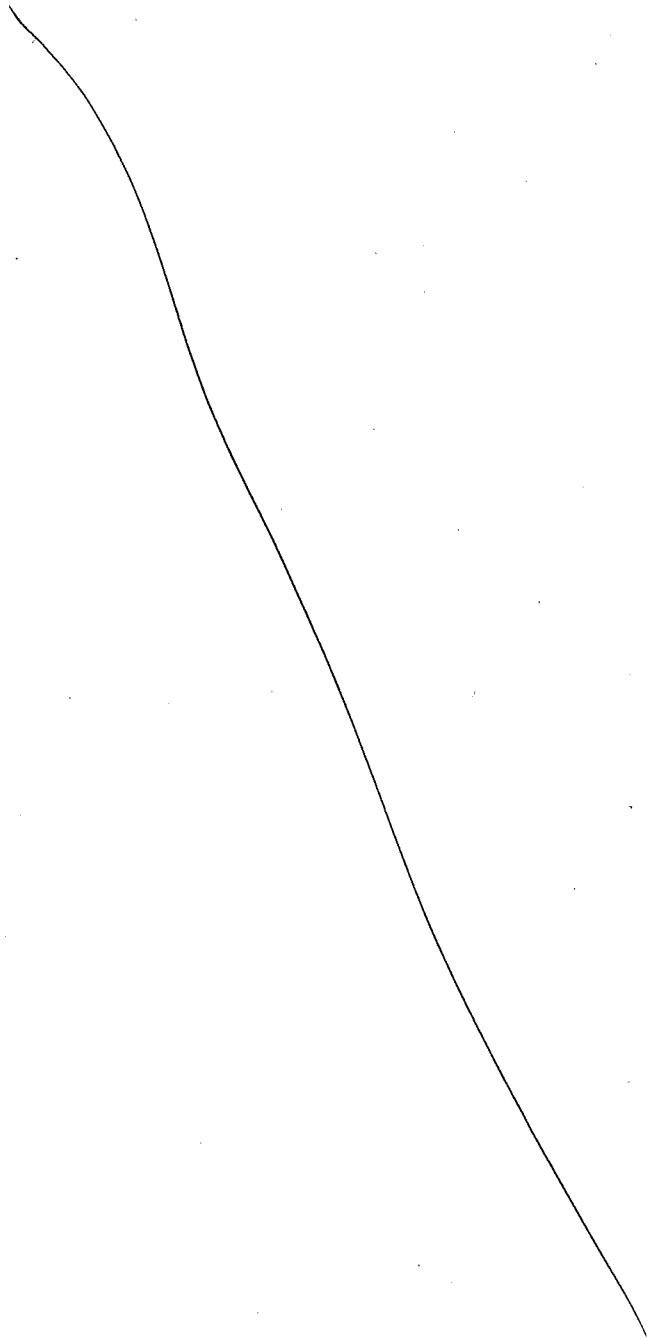

46	D.S.R 17.35		Providing & fixing soil, waste and vent pipes :				
		D.S.R 17.35.1.2	Centrifugally cast (spun) iron socket & spigot (S & S) pipe as per IS: 3989 10+2, Building =100 Meter	100	metre	865.87	Rs. Eight hundred sixty five and paise eighty seven only.
47	D.S.R 17.36		Providing and filling the joints with spun yarn, cement slurry and cement mortar 1:2 (1 cement : 2 fine sand) in S.C.I / C.I. Pipes: 100mm dia pipe				
		D.S.R 17.36.2	100mm dia pipe 10+2, Building =10 Each	10	Each	56.56	Rs. Fifty six and paise fifty six only.
48	D.S.R 17.43		Providing and fixing single equal plain junction of required degree with access door, insertion rubber washer 3 mm thick, bolts and nuts complete.				
		D.S.R 17.43.1.2	Sand cast iron S&S as per IS - 3989 10+2, Building =10 Each	10	Each	585.55	Rs. Five hundred eighty five and paise fifty five only.
49	D.S.R 17.60		Providing and fixing trap of self cleansing design with screwed down or hinged grating with or without vent arm complete, including cost of cutting and making good the walls and floors:				
		D.S.R 17.60.1.1	Sand cast iron S & S as per IS: 3989 10+2, Building =14 Each	14	Each	809.73	Rs. Eight hundred nine and paise seventy three only.
50	D.S.R 18.3		Providing and fixing Polyethelene-Aluminium-Polyethelene (PE-ALPE) Composite Pressure Pipes conforming to IS - 15450. U.V. stabilized with carbon black having thermal stability for hot & cold water supply, capable to withstand temperature up to 80 OC. including all special fittings of composite material (engineering plastic blend and brass inserts wherever required) e.g. elbows, tees, reducers, couplers & connectors etc., with trenching, refilling and testing of joints complete as per direction of the engineer in charge.				
		D.S.R 18.3.2	1620 (20 mm OD) pipe 10+2, Building =90 meter	90	meter	214.98	Rs. Two hundred fourteen and paise ninety eight only.
51	D.S.R 18.8		Providing and fixing Chlorinated Polyvinyl Chloride (CPVC) pipes, having thermal stability for hot & cold water supply including all CPVC plain & brass threaded fittings including fixing the pipe with clamps at 1.00 'm spacing. This includes joining of pipes & fittings with one step CPVC solvent cement and the cost of cutting chases and making good the same including testing of joints complete as per direction of E/I Concealed work including cutting chases and making good the wall etc.				
		D.S.R 18.8.1	15 mm nominal outer dia Pipes 10+2, Building =100 meter	100	metre	220.84	Rs. Two hundred twenty and paise eighty four only.


गोपनीय दस्तावेज़


Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Enl

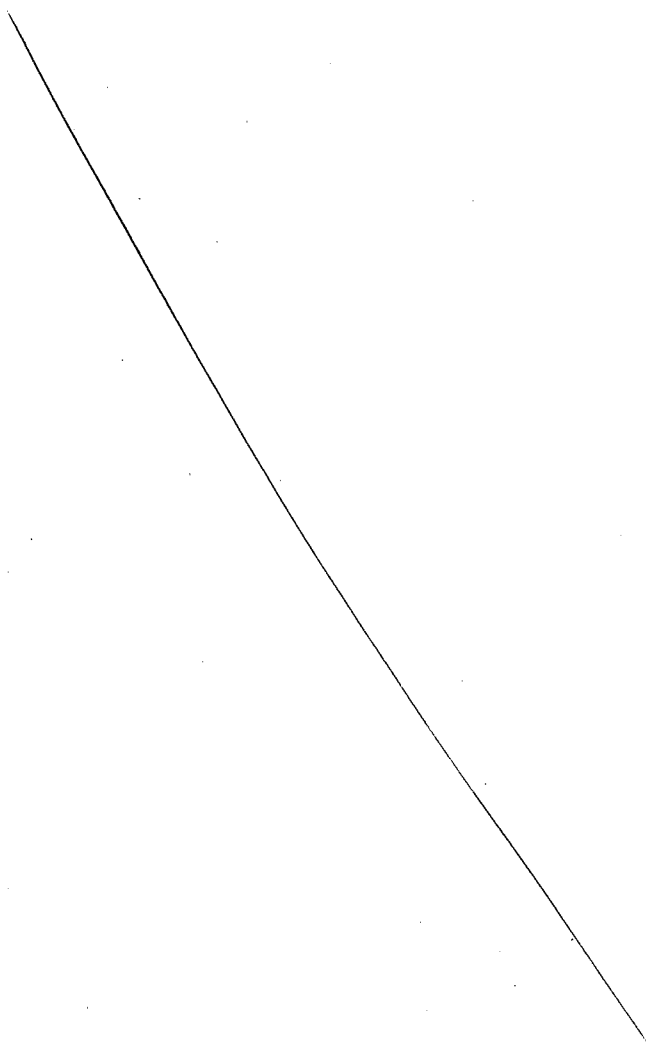

52	D.S.R 18.9		Providing and fixing Chlorinated Polyvinyl Chloride (CPVC) pipes, having thermal stability for hot & cold water supply including all CPVC plain & brass threaded fittings This includes jointing of pipes & fittings with one step CPVC solvent cement ,trenching ,refilling & testing of joints complete as per direction of Engineer in Charge.				
		D.S.R 18.9.3	25 mm nominal outer dia Pipes 10+2, Building =25 meter	25	metre	187.00	Rs. One hundred eighty seven only.
53	D.S.R 18.48		Providing and placing on terrace (at all floor levels) polyethylene water storage tank, ISI : 12701 marked, with cover and suitable locking arrangement and making necessary holes for inlet, outlet and overflow pipes but without fittings and the base support for tank. 10+2, Building =6000 per litre	6000	per litre	6.16	Rs. Six and paise sixteen only.
54	D.S.R 18.49		Providing and fixing C.P. brass bib cock of approved quality conforming to IS:8931				
		D.S.R 18.49.1	15 mm nominal bore 10+2, Building =10 Each	10	Each	401.48	Rs. Four hundred one and paise forty eight only.
55	D.S.R 18.52		Providing and fixing C.P. brass stop cock (concealed) of standard design and of approved make conforming to IS:8931.				
		D.S.R 18.52.1	15 mm nominal bore 10+2, Building =24 Each	24	Each	430.82	Rs. Four hundred thirty and paise eighty two only.
56	D.S.R 19.2		Providing and laying cement concrete 1:5:10 (1 cement : 5 coarse sand : 10 graded stone aggregate 40 mm nominal size) all-round S.W. pipes including bed concrete as per standard design :				
		D.S.R 19.2.1	100 mm diameter S.W. pipe 10+2, Building =30 meter	30	meter	501.87	Rs. Five hundred one and paise eighty seven only.
57	D.S.R 19.6		Providing and laying non-pressure NP2 class (light duty) R.C.C. pipes with collars jointed with stiff mixture of cement mortar in the proportion of 1:2 (1 cement : 2 fine sand) including testing of joints etc. complete :				
		D.S.R 19.6.1	100 mm dia. R.C.C. pipe 10+2, Building =10 meter	10	meter	220.53	Rs. Two hundred twenty and paise fifty three only.
58	D.S.R 19.27		Constructing brick masonry road gully chamber 50x45x60 cm with bricks in cement mortar 1:4 (1cement : 4 coarse sand) including 500x450 mm pre-cast R.C.C. horizontal grating with frame complete as per standard design :				
		D.S.R 19.27.1	With common burnt clay F.P.S. (non modular) bricks of class designation 7.5 10+2, Building =4 Each	4	Each	3225.44	Rs. Three thousand two hundred twenty five and paise forty four only.


 Chief Engineer
 B.S.E.I.D.C. Ltd, Patna
 Rm



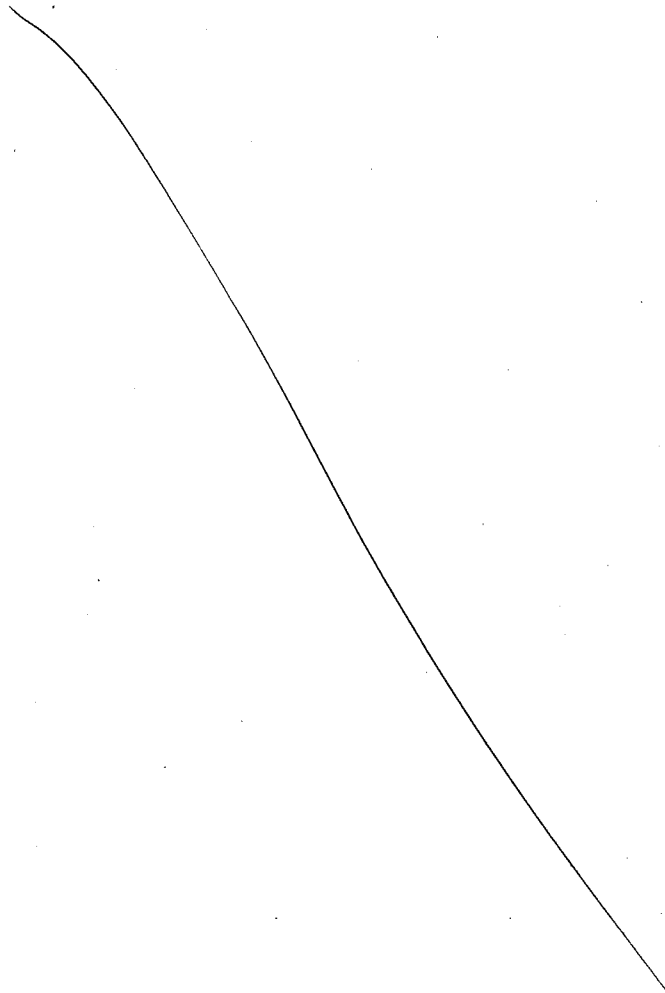

59	D.S.R 19.30		Constructing brick masonry chamber for underground C.I. inspection chamber and bends with bricks in cement mortar 1:4 (1 cement : 4 coarse sand) C.I. cover with frame (light duty) 455x610 mm internal dimensions, total weight of cover with frame to be not less than 38kg (weight of cover 23 kg and weight of frame 15 kg), R.C.C. top slab with 1:2:4 mix (1 cement : 2 coarse sand : 4 graded stone aggregate 20 mm nominal size), foundation concrete 1:5:10 (1 cement : 5 fine sand : 10 graded stone aggregate 40 mm nominal size), inside plastering 12 mm thick with cement mortar 1:3 (1 cement : 3 coarse sand), finished smooth with a floating coat of neat cement on walls and bed concrete etc. complete as per standard				
		D.S.R 19.30.1.1	Inside dimensions 455x610 mm and 45 cm deep for single pipe line : With common burnt clay F.P.S. (non modular) bricks of class designation 7.5 10+2, Building =4 Each	4	Each	3956.83	Rs. Three thousand nine hundred fifty six and paise eighty three only.
60	D.S.R 19.32		Making soak pit 2.5 m diameter 3.0 metre deep with 45 x 45 cm dry brick honey comb shaft with bricks and S.W. drain pipe 100 mm diameter, 1.8 m long complete as per standard design.				
		D.S.R 19.32.1	With common burnt clay F.P.S. (non modular) bricks of class designation 7.5 10+2, Building =1 Each	1	Each	15380.43	Rs. Fifteen thousand three hundred eighty and paise forty three only.
61	D.S.R 19.34		Providing and fixing S.W. intercepting trap in manholes with stiff mixture of cement mortar 1:1 (1 cement : 1 fine sand) including testing of joints etc.				
		D.S.R 19.34.1	100 mm dia 10+2, Building =4 Each	4	Each	251.04	Rs. Two hundred fifty one and paise four only.
62			Construction of 125mm x 40mm x 90m Tube well 10+2, Building =1 Each	1	Each	60,058.46	Rs. Sixty thousand fifty eight and paise forty six only.
63		Code no. 1352	i) C.I. cover and frame 300 x 300 mm inside Septic Tank=1 Each	1.00	Each	301.24	Rs. Three hundred one and paise twenty four only.
64		Code no. 1621	(ii) S.C.I. plain bend 100 mm dia Septic Tank=1 Each	1.00	Each	225.94	Rs. Two hundred twenty five and paise ninety four only.
65		Code no. 7087	(iii) S.C.I. Tee 150 mm dia Septic Tank=1 Each	1.00	Each	543.31	Rs. Five hundred forty three and paise thirty one only.
						Total = (B)	431,259.12
			Electrical Works (1% labour cess has been added on current SOR as labour cess is not included in current SOR).				

[Signature]
25-6-2014

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

[Signature]

अभिप्रेत किया है

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

66	1.8		Wiring for light point / fan point / exhaust fan point / call bell point with 1.5 sq.mm FR PVC insulated copper conductor single core cable in surface / recessed medium class PVC conduit, with piano type switch, phenolic laminated sheet, suitable size M.S. box and earthing the point with 1.5 sq.mm. FR PVC insulated copper conductor single core cable etc. as required.				
		1.8.3	Group C 10+2, Building = 302Nos	302	Nos.	625.19	Rs. Six hundred twenty five and paise nineteen only.
67	1.11		Wiring for twin control light point with 1.5 sq.mm FR PVC insulated copper conductor single core cable in surface / recessed medium class PVC conduit, 2 way modular switch, modular plate, suitable GI. Box and earthing the point with 1.5 sq. mm. FR PVC insulated copper conductor single core cable etc as required. 10+2, Building = 4 point	4	point	717.10	Rs. Seven hundred seventeen and paise ten only.
68	1.12		Wiring for light/ power plug with 2x4 sq.mm FR PVC insulated copper conductor single core cable in surface/ recessed medium class PVC conduit along with 1 No 4 sq. mm FR PVC insulated copper conductor single core cable for loop earthing as required. 10+2, Building = 350 meter	350	meter	163.62	Rs. One hundred sixty three and paise sixty two only.
69	1.14		Wiring for circuit / submain wiring alongwith earth wire with the following sizes of FR PVC insulated copper conductor, single core cable in surface / recessed medium class PVC conduit as required.				
		1.14.3	2 x 4 sq.mm + 1 x 4 sq. mm earth wire 10+2, Building = 350 meter	350	meter	163.62	Rs. One hundred sixty three and paise sixty
		1.14.9	4 x 6 sq.mm + 2 x 6 sq. mm earth wire 10+2, Building = 60 meter	60	meter	361.58	Rs. Three hundred sixty one and paise fifty eight only.
70	1.18		Supplying and drawing following pair 0.5 sq.mm. FR PVC insulated annealed copper conductor, unarmored telephone cable in the existing surface/ recessed steel/ PVC conduit as required.				
		1.18.1	1Pair 10+2, Building = 50 meter	50	meter	11.11	Rs. Eleven and paise eleven only.
71	1.19		Supplying and drawing co-axial TV cable RG-6 grade, 0.7 mm solid copper conductor PE insulated, shielded with fine tinned copper braid and protected with PVC sheath in the existing surface / recessed steel / PVC conduit as required. 10+2, Building = 50 meter	50	meter	22.22	Rs. Twenty two and paise twenty two only.
72	1.24		Supplying and fixing following modular switch/ socket on the existing modular plate & switch box including connections but excluding modular plate etc. as required.				
		1.24.3	15/16 amp switch 10+2, Building = 52 Each	52	Each	110.09	Rs. One hundred ten and paise nine only.

3107/2022

B.S.E.I.D.C. Ltd, Patna

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

		1.24.4	3 pin 5/6 amp socket outlet. 10+2, Building = 34 Each	34	Each	96.96	Rs. Ninety six and paise ninety six only.
		1.24.6	Telephone socket outlet 10+2, Building =4 Each	4	Each	89.89	Rs. Eighty nine and paise eighty nine only.
		1.24.7	TV antenna socket outlet 10+2, Building =11 Each	11	Each	93.93	Rs. Ninety three and paise ninety three only.
73	1.29		Supplying and fixing metal box of 150mm x 75mm x 60mm deep (nominal size) on surface on in recess with suitable size of phenolic laminated sheet cover in front including providing and fixing 3 pin 5/6 amps socket outlet and 5/6 amps piano type switch, connection, painting etc. as required. (For light plugs to be used in non residential buildings). 10+2, Building =100 Each	100	Each	153.52	Rs. One hundred fifty three and paise fifty two only.
74	2.8		Supplying and fixing following way prewired vertical type TP&N MCB distribution board of steel sheet for 415 volts on surface / recess complete with loose wire box, terminal connectors for all incoming and outgoing circuits, duly prewired with suitable size of FR PVC insulated copper conductor for upto the terminal blocks, tinned copper bus bar, neutral link, earth bar, din bar, detachable gland plate, interconnections, powder painted including earthing etc. as required. (But without				
		2.8.2	6 way (4 + 18), Single door 10+2, Building =2 Each	2	Each	7226.55	Rs. Seven thousand two hundred twenty six and paise fifty five
75	3.2		Supplying, installing, testing and commissioning of following capacity TPN tap off box made of 1.6mm thick sheet steel enclosure duly painted with powder coating on exinsing rising mains complete with PPN disconnector FSU AND HRC fuses, connections, earthing etc as required.				
		3.2.2	32 amps TPN 10+2, Building =2 Each	2	Each	5974.15	Rs. Five thousand nine hundred seventy four and paise fifteen only.
		3.2.3	63 amps TPN 10+2, Building =1 Each	1	Each	6706.4	Rs. Six thousand seven hundred six and paise forty only.
		3.2.4	100 amps TPN 10+2, Building =1 Each	1	Each	7725.49	Rs. Seven thousand seven hundred twenty five and paise forty nine only.
76	5.6		Earthing with copper earth plate 600mm x 600mm x 3mm thick including accessories, and providing masonry enclosure with cover plate having locking arrangement and watering pipe of 2.7	1	Nos.	8644.59	Rs. Eight thousand six hundred forty four and paise fifty nine only.
77	2349		Straight through cable jointing kit with cast resin compound with ferrules for 3.5 x 25 sq.mm. 1.1 KV grade cable. 10+2, Building =1 Set	1	set.	972.48	Rs. Nine hundred seventy two and paise forty eight only.
						TOTAL=	405,787.55
			Fire Fighting (1% labour cess has been added on current SOR as labour cess is not included in current SOR).				

31/01/2018

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

Chief Engineer
B.S.E.I.D.C. Ltd, Patna


78	DGS&D		Supply, & Installation of ABC Fire Extinguisher for fire fighting work. 10+2, Building = 10 Nos.	10	Nos.	7549.8	Rs. Seven thousand five hundred forty nine and paise eighty only.
						TOTAL = (D)	75497.50
			Carriage cost of materials (1% labour cess has been added on current SOR as labour cess is not included in current SOR)				
79	Lead in Km		Type of materials				
	5		Cement, Lead = 5 Kms (P)	177.403	MT.	199.48	Rs. One hundred ninety nine and paise forty eight only.
	14		Coarse Sand, Lead = Ave. 73Kms (P) (Source - Dehri)	303.976	cum	957.00	Rs. Nine hundred fifty seven only.
	3		Local Sand, Lead = 3 Kms (2P+1K)	422.892	cum	192.30	Rs. One hundred ninety two and paise thirty only.
	118		Stone Chips, Lead = 1US+4P+156R+11PKms (P) (Source - Manpur)	338.120	cum	1218.34	Rs. One thousand two hundred eighteen and paise thirty four only.
	8		Brick, Lead = 8 Kms (7P+1K)	165.186	Thous and	562.93	Rs. Five hundred sixty two and paise ninety three only.
	5		Steel, Lead = 5 Kms (P)	33.452	MT.	199.48	Rs. One hundred ninety nine and paise forty eight only.
						TOTAL = (E)	919,222.51
80			ADD EXTRA COST OF MATERIAL FOR PATNA (RURAL) COMM. W.R.T GAYA AS PER SOR BCD + NEW RATE W.R.T. TO OLD RATE +15% CP AND OVER HEAD				
			Bricks	165.186	Thous and	235.40	Rs. Two hundred thirty five and paise forty only.
			Cement	177.403	MT.	841.07	Rs. Eight hundred forty one and paise seven only.
						TOTAL =	188,093.13
				Total Cost in Rs.			10,505,390.77
Group No. : - S.S.S-153							
Sl.	District	Name of School					Amount
1	KAIMUR	10 + 2 SCHOOL, KASER					10,505,390.77
2		10 + 2 SCHOOL, SINDHI					10,505,390.77
Total Cost in 'Rs'						21,010,781.53	
Say 'Rs'						21,010,782.00	

Tender approved in favour of Ajay Kumar Singh. @ 1.01% (One Point Zero One Percent) below BOQ rates i.e total amount comes to Rs.2,07,98,573=00 (Rupees Two Core Seven Lacs Ninety Eight Thousand Five Hundred Seventy Three Only)

310742012 RSE

Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Rm


Chief Engineer
B.S.E.I.D.C. Ltd, Patna



GOVERNMENT OF BIHAR

STANDARD BIDDING DOCUMENT
PROCUREMENT
OF
CIVIL WORKS


(Seal & Signature of Tenderer)


25-6-2014
Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Ramb

**BIHAR STATE EDUCATIONAL
INFRASTRUCTURE DEVELOPMENT CORPORATION
LTD.**

(Seal & Signature of Tenderer)

31/04/2014

25-6-2014

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

Patna

STANDARD BIDDING DOCUMENT

PROCUREMENT OF CIVIL WORKS


(Seal & Signature of Tenderer)


Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Pmb

BIHAR STATE EDUCATIONAL INFRASTRUCTURE DEVELOPMENT CORPORATION LTD.
(A Govt. Of Bihar Undertaking)

Shiksha Bhawan, Bihar Rastrabhasa Parishad Campus
Acharya Shiv Pujan Sahay Path, Saidpur, PATNA-800004.

NATIONAL COMPETITIVE BIDDING
(CIVIL WORKS)

1. NAME OF WORK : Construction of Senior Secondary Schools, in Bihar.

<u>Gr. No.</u>	<u>District</u>	<u>Name of School</u>
SSS-153	KAIMUR	10 + 2 SCHOOL, KASER
		10 + 2 SCHOOL, SINDHI

2. PERIOD OF CONSTRUCTION : 15 Months.
3. DATE OF ISSUE OF NOTICE INVITING BID : 12.12.2013
4. PERIOD AND PLACE OF SALE : FROM : 20-12-2013 To 04-01-2014, 15.00 Hours
OF BID DOCUMENT on Website : www.eproc.bihar.gov.in
5. TIME, DATE AND PLACE OF. : TIME : 14:30 HOURS, Date : 24-12-2013, in the
office of PRE- BID MEETING Managing Director, BSEIDC, Patna.
6. LAST DATE AND TIME FOR : DATE : 06-01-2014, TIME; 15:00 HOURS
RECEIPT OF BIDS on Website : www.eproc.bihar.gov.in
7. *TIME AND DATE OF OPENING : DATE : 08-01-2014, TIME: 16:30 HOURS
TECHNICAL BIDS on Website : www.eproc.bihar.gov.in
8. *TIME AND DATE OF OPENING : DATE : 18-01-2014, TIME: 16:00 HOURS
FINANCIAL BIDS on Website ; www.eproc.bihar.gov.in
9. PLACE OF OPENING OF BIDS : THROUGH WEBSITE Only www.eproc.bihar.gov.in
10. PERIOD OF BID VALIDITY : 120 Days.
11. OFFICER INVITING BIDS : Managing Director, BSEIDC, Patna.
- *Should be the same as for the deadline for receipt of bids or promptly thereafter.**

(Seal & Signature of Tenderer)

[Handwritten Signature]

[Handwritten Signature]
25-6-2014

Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Rous

INVITATION FOR BID
(IFB)

अजय कुमार सिंह
(Seal & Signature of Tenderer)

25-6-2014
Chief Engineer
B.S.E.I.D.C. Ltd, Patna
For

बिहार राज्य शैक्षणिक आधारभूत संरचना विकास निगम लिमिटेड

(बिहार सरकार का एक उपक्रम)

शिक्षा भवन, बिहार राष्ट्रभाषा परिषद कैम्पस, आचार्य शिवपुजन सहाय पथ, सैदपुर, पटना-800004 (दूरभाष:-0612-2910314)

निविदा आमंत्रण सूचना संख्या-36 वर्ष 2013-14

प्रतिशत मद दर निविदा

(केवल ई-टेंडरिंग पद्धति के अनुसार वेबसाइट www.eproc.bihar.gov.in पर)

1. बिहार राज्य के अन्तर्गत विभिन्न जिलों में "पंचायत स्तर पर उच्च माध्यमिक विद्यालय" के भवन निर्माण कार्य हेतु निम्नांकित निविदायें आमंत्रित की जाती हैं। कोई भी संवेदक जो केन्द्रीय/राज्य सरकार/सार्वजनिक क्षेत्रों में निबंधित हो, निविदा में भाग ले सकते हैं परन्तु इस निगम का रजिस्ट्रेशन कराना, उक्त कार्य का लेटर ऑफ एक्सेप्टेंस प्राप्त होने के बाद अनिवार्य होगा।

क्र म	गुप संख्या	जिला का नाम	विद्यालय का नाम	प्राक्कलित राशि (लाख रु०)	अग्रधन की राशि (लाख रु०)	परिमाण विपत्र की राशि(रु०)	कार्य समाप्ति की अवधि
1	SSS-1	पूर्वी चंपारण	1 उत्कर्मित मध्य. विद्यालय, खैरी जमुनिया	328.40	6.57	26,900.00	15 माह
			2 उत्कर्मित मध्य विद्यालय, बैरिया				
			3 मध्य विद्यालय, रामकरण पकड़ी				
2	SSS-2	पूर्वी चंपारण	1 मध्य विद्यालय, सपट्टी	218.19	4.37	15,650.00	15 माह
			2 उ०मध्य विद्या० भगत टोला, मोहबबत छपरा				
3	SSS-3	पूर्वी चंपारण	1 मध्य विद्यालय, रामजी टोला	326.11	6.53	26,900.00	15 माह
			2 मध्य विद्यालय, पट्टी, (महात्मा)				
			3 उत्कर्मित मध्य विद्यालय, कररिया जागीर				
4	SSS-4	पूर्वी चंपारण	1 मध्य विद्यालय, राजेपुर, नवादा	218.70	4.38	15,650.00	15 माह
			2 मध्य विद्यालय, धनौजी				
5	SSS-5	पूर्वी चंपारण	1 मध्य विद्यालय, मुरला	111.41	2.23	15,650.00	15 माह
6	SSS-6	पूर्वी चंपारण	1 मध्य विद्यालय, उज्जैन लोहियार	109.83	2.20	15,650.00	15 माह
7	SSS-7	पूर्वी चंपारण	1 उत्कर्मित मध्य विद्यालय, हथियाही	105.25	2.11	15,650.00	15 माह
8	SSS-8	पूर्वी चंपारण	1 उत्कर्मित मध्य विद्यालय, श्यामपुर	109.98	2.20	15,650.00	15 माह
9	SSS-9	पूर्वी चंपारण	1 मध्य विद्यालय, मझौलिया	109.10	2.19	15,650.00	15 माह
10	SSS-10	पूर्वी चंपारण	1 मध्य विद्यालय, हराजघाट	110.03	2.21	15,650.00	15 माह
11	SSS-11	पूर्वी चंपारण	1 उत्कर्मित मध्य विद्यालय, मच्छहाँ	108.82	2.18	15,650.00	15 माह
12	SSS-12	पूर्वी चंपारण	1 मध्य विद्यालय, रमसिरियाँ	219.01	4.39	15,650.00	15 माह
			2 मध्य विद्यालय, झखरा				
13	SSS-13	पूर्वी चंपारण	1 मध्य विद्यालय, तेलहारा कला	110.53	2.22	15,650.00	15 माह
14	SSS-14	पूर्वी चंपारण	1 उत्कर्मित मध्य विद्यालय, बरवा	335.31	6.71	26,900.00	15 माह
			2 उत्कर्मित मध्य विद्यालय, लक्ष्मीपुर				
			3 मध्य विद्यालय, भवानीपुर बाजार				
15	SSS-15	पूर्वी चंपारण	1 मध्य विद्यालय, रायकरिया	109.85	2.20	15,650.00	15 माह
16	SSS-16	पूर्वी चंपारण	1 मध्य विद्यालय, विशुनपुर बसंत	329.08	6.59	26,900.00	15 माह
			2 मध्य विद्यालय टेवसा				
			3 मध्य विद्यालय, परसौनी कोठी				
17	SSS-17	पूर्वी चंपारण	1 मध्य विद्यालय, जोकियारी	112.06	2.25	15,650.00	15 माह
18	SSS-18	पूर्वी चंपारण	1 उत्कर्मित मध्य विद्यालय गौरिया	219.20	4.39	15,650.00	15 माह
			2 उत्कर्मित मध्य विद्यालय, अजगरवा हिन्दी				

(Seal & Signature of Tenderer)

(Handwritten Signature)


(Handwritten Signature)

6

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

19	SSS-19	पूर्वी चंपारण	1	मध्य विद्यालय, रघुनाथपुर	109.21	2.19	15,650.00	15 माह
20	SSS-20	पश्चिम चंपारण	1	मध्य विद्यालय, महुआ	1014.79	20.15	26,900.00	15 माह
			2	मध्य विद्यालय, बोरवल				
			3	उत्क्रमित मध्य विद्यालय बेलवा चखनी				
			4	उत्क्रमित मध्य विद्यालय, नौतनवा				
			5	मध्य विद्यालय, सिधाव				
			6	उत्क्रमित मध्य विद्यालय, मिश्रौली				
			7	उत्क्रमित मध्य विद्यालय रमवलिया				
			8	मध्य विद्यालय, महुआर				
			9	उत्क्रमित मध्य विद्यालय मच्छरगावा,				
21	SSS-21	पश्चिम चंपारण	1	उत्क्रमित मध्य विद्यालय जुड़ा पकड़ी	787.01	15.75	26,900.00	15 माह
			2	उत्क्रमित मध्य विद्यालय डुमरी				
			3	मध्य विद्यालय, शिवपुर कॉलनी				
			4	मध्य विद्यालय, बी०एम०सी० फूलकोल				
			5	मध्य विद्यालय, भावल				
			6	मध्य विद्यालय, मुड़ेरा				
			7	मध्य विद्यालय बड़गो				
			8	उत्क्रमित मध्य विद्यालय जुड़ा पकड़ी				
			9	उत्क्रमित मध्य विद्यालय डुमरी				
22	SSS-22	पश्चिम चंपारण	1	उत्क्रमित मध्य विद्यालय बैठनिया	447.52	9.00	26,900.00	15 माह
			2	मध्य विद्यालय, मठिया वृत्त बैठनिया				
			3	उत्क्रमित मध्य विद्यालय, परसा बाबूटोला				
			4	मध्य विद्यालय, सेनुअरिया				
23	SSS-23	पश्चिम चंपारण	1	मध्य विद्यालय, मनवा परसी	446.42	9.00	26,900.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, बनवरिया				
			3	मध्य विद्यालय, राजपुर मदान				
			4	उत्क्रमित मध्य विद्यालय चगौना				
24	SSS-24	पश्चिम चंपारण	1	मध्य विद्यालय, बिनही	226.23	4.53	15,650.00	15 माह
			2	मध्य विद्यालय, खैरवा				
25	SSS-25	पश्चिम चंपारण	1	मध्य विद्यालय, हौदा डुमरा	562.82	11.26	26,900.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, भित्तिहरवा				
			3	उत्क्रमित मध्य विद्यालय, डरौल				
			4	उत्क्रमित मध्य विद्यालय, बखरी				
			5	मध्य विद्यालय, धमौरा				
26	SSS-26	पश्चिम चंपारण	1	उत्क्रमित मध्य विद्यालय, बासोपट्टी	221.83	4.44	15,650.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, दुधिअवा				
27	SSS-27	पश्चिम चंपारण	1	उत्क्रमित मध्य विद्यालय, कोवाहा	551.94	11.04	26,900.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, हीरा पाकड़				
			3	उत्क्रमित मध्य विद्यालय, भरपटिया				
			4	उत्क्रमित मध्य विद्यालय सबैया काला				
			5	उत्क्रमित मध्य विद्यालय, मोहली सुग्गा				
28	SSS-28	पश्चिम चंपारण	1	उ०मध्य विद्यालय, तधवानन्दपुर लखनी बाजार	330.94	6.62	26,900.00	15 माह
			2	उत्क्रमित मध्य विद्यालय ज्ञानीजी का टोला				
			3	उत्क्रमित मध्य विद्यालय बलुआ रमपुरवा				
29	SSS-29	पश्चिम चंपारण	1	मध्य विद्यालय, चन्द्रहाँ	112.43	2.25	15,650.00	15 माह
30	SSS-30	पश्चिम चंपारण	1	उत्क्रमित मध्य विद्यालय सियारही	549.94	11.00	26,900.00	15 माह
			2	आदर्श मध्य विद्यालय, महुआहाँ				
			3	मध्य विद्यालय, डबरिया				
			4	उत्क्रमित मध्य विद्यालय, शिवराजपुर				
			5	उत्क्रमित मध्य विद्यालय, लक्ष्मीपुर दुबोलिया				
			2	मध्य विद्यालय, धनौजी				

(Seal & Signature of Tenderer)



 Chief Engineer
 B.S.E.I.D.C. Ltd, Patna

31	SSS-31	पश्चिम चंपारण	1	मध्य विद्यालय, सिंगाछापर	220.35	4.41	15,650.00	15 माह
			2	मध्य विद्यालय, शेखौना				
32	SSS-32	पश्चिम चंपारण	1	मध्य विद्यालय, सिरिसिया	112.28	2.25	15,650.00	15 माह
33	SSS-33	पश्चिम चंपारण	1	मध्य विद्यालय, धनहा	230.29	4.61	15,650.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, तनकूहा				
34	SSS-34	पश्चिम चंपारण	1	मध्य विद्यालय, बनकटवा	111.53	2.24	15,650.00	15 माह
35	SSS-35	सीतामढ़ी	1	मध्य विद्यालय, महेशा 1	217.84	4.36	15,650.00	15 माह
			2	मध्य विद्यालय, बगाही				
36	SSS-36	सीतामढ़ी	1	मध्य विद्यालय, हरबेल	442.74	8.86	26,900.00	15 माह
			2	मध्य विद्यालय, रनौली				
			3	मध्य विद्यालय, यमुना बरही				
			4	मध्य विद्यालय, हरपुर बलहा				
37	SSS-37	सीतामढ़ी	1	मध्य विद्यालय, बसेपुर	109.69	2.20	15,650.00	15 माह
38	SSS-38	सीतामढ़ी	1	मध्य विद्यालय, डुमरा	327.74	6.56	26,900.00	15 माह
			2	मध्य विद्यालय, दमामी मठ				
			3	मध्य विद्यालय, मधकौल				
39	SSS-39	सीतामढ़ी	1	मध्य विद्यालय, धनगेर	109.09	2.19	15,650.00	15 माह
40	SSS-40	सीतामढ़ी	1	मध्य विद्यालय, बुलाकीपुर	439.01	8.79	26,900.00	15 माह
			2	मध्य विद्यालय, उसरहिया				
			3	मध्य विद्यालय, दोधरा				
			4	मध्य विद्यालय, पौसा				
41	SSS-41	सीतामढ़ी	1	मध्य विद्यालय, बसहीया हिन्दी	221.66	4.44	15,650.00	15 माह
			2	मध्य विद्यालय, मरपा कचौर				
42	SSS-42	सीतामढ़ी	1	मध्य विद्यालय, कोरियाही	221.32	4.43	15,650.00	15 माह
			2	मध्य विद्यालय, बखरी				
43	SSS-43	मुजफ्फरपुर	1	उत्क्रमित मध्य विद्यालय, घोसरामा कोठी	437.38	8.75	26,900.00	15 माह
			2	मध्य विद्यालय, बनगही				
			3	मध्य विद्यालय, रतनमनिया				
			4	उत्क्रमित मध्य विद्यालय, बंगरा				
44	SSS-44	मुजफ्फरपुर	1	मध्य विद्यालय, धरभरा	107.95	2.16	15,650.00	15 माह
45	SSS-45	मुजफ्फरपुर	1	मध्य विद्यालय, वाजितपुर	216.48	4.33	15,650.00	15 माह
			2	मध्य विद्यालय, अतहर				
46	SSS-46	मुजफ्फरपुर	1	मध्य विद्यालय, बररिया	538.14	10.77	26,900.00	15 माह
			2	मध्य विद्यालय, मुस्तफापुर				
			3	उत्क्रमित मध्य विद्यालय, मधुबन				
			4	मध्य विद्यालय, कपलपुरा				
			5	मध्य विद्यालय, श्यामपुर भोजा				
47	SSS-47	मुजफ्फरपुर	1	उत्क्रमित मध्य विद्यालय, कोठियापुर	214.97	4.30	15,650.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, रतनपुरा				
48	SSS-48	मुजफ्फरपुर	1	मध्य विद्यालय, बंगरा	1071.95	20.72	26,900.00	15 माह
			2	मध्य विद्यालय, तेलिया				
			3	मध्य विद्यालय, करमचन्द रामपुर बलरा				
			4	मध्य विद्यालय, फतेहपुर				
			5	मध्य विद्यालय, चढुआ				
			6	मध्य विद्यालय, किशुनपुर, मधुबन				
			7	मध्य विद्यालय, अमरख				
			8	मध्य विद्यालय, मरिचा				
			9	मध्य विद्यालय, सिलौट				
			10	मध्य विद्यालय, मोरिनिरक उर्वू				

(Seal & Signature of Tenderer)




8

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

49	SSS-49	मुजफ्फरपुर	1	मध्य विद्यालय, मकशुदपुर	431.81	8.64	26,900.00	15 माह
			2	मध्य विद्यालय, खरिका				
			3	मध्य विद्यालय, कोदहरिया				
			4	मध्य विद्यालय, सिवायपट्टी				
50	SSS-50	मुजफ्फरपुर	1	मध्य विद्यालय, मोरसंडी	322.17	6.45	26,900.00	15 माह
			2	मध्य विद्यालय, अंजनाकोट				
			3	मध्य विद्यालय, धुमनगर				
51	SSS-51	मुजफ्फरपुर	1	उत्क्रमित मध्य विद्यालय, गवसारा	212.61	4.26	15,650.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, बथना राम				
52	SSS-52	मुजफ्फरपुर	1	मध्य विद्यालय, बलुआ	432.38	8.65	26,900.00	15 माह
			2	मध्य विद्यालय, टिटरा विशुनपुर				
			3	उत्क्रमित मध्य विद्यालय, मुशहरा लौतन				
			4	मध्य विद्यालय, विद्याझांप				
53	SSS-53	मुजफ्फरपुर	1	मध्य विद्यालय, पकड़ी स्माईल	426.65	8.54	26,900.00	15 माह
			2	मध्य विद्यालय, खबरा				
			3	मध्य विद्यालय, प्रहलादपुर				
			4	उत्क्रमित मध्य विद्यालय, मुसहरी फार्म				
54	SSS-54	मुजफ्फरपुर	1	मध्य विद्यालय, रामचन्द्रपुर	321.71	6.44	26,900.00	15 माह
			2	मध्य विद्यालय, सलहपुर				
			3	मध्य विद्यालय, सखहरा				
55	SSS-55	मुजफ्फरपुर	1	मध्य विद्यालय, लक्ष्मीपुर	107.99	2.16	15,650.00	15 माह
56	SSS-56	मुजफ्फरपुर	1	उत्क्रमित मध्य विद्यालय, महमदापुर बनवारी	975.54	19.52	26,900.00	15 माह
			2	मध्य विद्यालय, मथुरापुर, गोवर्धनपुर				
			3	मध्य विद्यालय, गनियारी				
			4	मध्य विद्यालय, महसी				
			5	मध्य विद्यालय, सिमरी				
			6	मध्य विद्यालय, हरिपुर कृष्ण				
			7	उत्क्रमित मध्य विद्यालय, रहिमपुर रसका उर्दू				
			8	मध्य विद्यालय, सरमस्तपुर				
			9	मध्य विद्यालय, पचडही				
57	SSS-57	मुजफ्फरपुर	1	उत्क्रमित मध्य विद्यालय, वासुदेव	427.74	8.56	26,900.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, विष्णुपुर बसैथा				
			3	उत्क्रमित मध्य विद्यालय, गौरीगावा				
			4	मध्य विद्यालय, धुबीयाही रामकृष्ण				
58	SSS-58	मुजफ्फरपुर	1	मध्य विद्यालय, औराई हिन्दी	542.43	10.85	26,900.00	15 माह
			2	मध्य विद्यालय, शंभुता				
			3	मध्य विद्यालय, भरथुआ				
			4	मध्य विद्यालय, भदई				
			5	मध्य विद्यालय, अमनौर				
59	SSS-59	मुजफ्फरपुर	1	मध्य विद्यालय, बुशहरा मन	106.52	2.14	15,650.00	15 माह
60	SSS-60	शिवहर	1	मध्य विद्यालय, औरा	437.67	8.76	26,900.00	15 माह
			2	मध्य विद्यालय, मुसहरी				
			3	मध्य विद्यालय, छत्तीनी				
			4	मध्य विद्यालय, मगुराहा				
61	SSS-61	शिवहर	1	मध्य विद्यालय, सुंदरपुर खरौना	110.75	2.22	15,650.00	15 माह
62	SSS-62	वैशाली	1	उत्क्रमित मध्य विद्यालय, परमानंदपुर	531.77	10.64	26,900.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, शाहपुर चकुम्भर				
			3	उत्क्रमित मध्य विद्यालय, हरपुर गंगाराम				
			4	राजकीय मध्य विद्यालय, चकउमर				
			5	उत्क्रमित मध्य विद्यालय, पकड़ी				

(Seal & Signature of Tenderer)



Chief Engineer
B.S.E.I.D.C. Ltd, Patna

63	SSS-63	वैशाली	1	मध्य विद्यालय मजलिसपुर	107.28	2.15	15,650.00	15 माह
64	SSS-64	वैशाली	1	मध्य विद्यालय, बाजितपुर, कर्तार	432.88	8.66	26,900.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, मोहम्मदपुर जुम्मान				
			3	मध्य विद्यालय, पहाड़पुर				
			4	मध्य विद्यालय, बलिगाँव				
65	SSS-65	वैशाली	1	मध्य विद्यालय, बलाढ़	432.59	8.66	26,900.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, मौदह चातुर				
			3	मध्य विद्यालय, पातेपुर				
			4	उत्क्रमित मध्य विद्यालय, परतारा				
66	SSS-66	वैशाली	1	उत्क्रमित मध्य विद्यालय, बेलसर हाट	106.78	2.14	15,650.00	15 माह
67	SSS-67	वैशाली	1	चक्रसिंगार मध्य विद्यालय	214.77	4.30	15,650.00	15 माह
			2	चौदपुरा मध्य विद्यालय				
68	SSS-68	वैशाली	1	उत्क्रमित मध्य विद्यालय, गौसपुर	212.57	4.26	15,650.00	15 माह
			2	मध्य विद्यालय बनघाड़ा				
69	SSS-69	वैशाली	1	उत्क्रमित मध्य विद्यालय, ममरेजपुर कन्या	213.20	4.27	15,650.00	15 माह
			2	मध्य विद्यालय, उफरौल				
70	SSS-70	वैशाली	1	मध्य विद्यालय, जतकौली	638.72	12.78	26,900.00	15 माह
			2	मध्य विद्यालय, बरटिया मझौली				
			3	मध्य विद्यालय चकअल्हदाद परिसर				
			4	उत्क्रमित मध्य विद्यालय, हुसैनपुर				
			5	उत्क्रमित मध्य विद्यालय, खजुअता				
			6	मध्य विद्यालय, दाउदनगर परिसर				
71	SSS-71	वैशाली	1	उत्क्रमित मध्य विद्यालय, सोहरथी	107.39	2.15	15,650.00	15 माह
72	SSS-72	वैशाली	1	उत्क्रमित मध्य विद्यालय, जगोडीह हरिजन	106.07	2.13	15,650.00	15 माह
73	SSS-73	पूर्णियाँ	1	नौबत लाल मण्डि कुकरौन-2	325.36	6.51	26,900.00	15 माह
			2	मध्य विद्यालय, रंगपुरा				
			3	आम मध्य विद्यालय, नीरपुर				
74	SSS-74	पूर्णियाँ	1	मध्य विद्यालय, गहिलस्थान	766.44	15.33	26,900.00	15 माह
			2	मध्य विद्यालय, चिकनी पटराहा				
			3	मध्य विद्यालय, गुलाबटोल मल्लडीहा				
			4	मध्य विद्यालय, भतसारा				
			5	मध्य विद्यालय, सुखसेना				
			6	मध्य विद्यालय, निपनियाँ				
			7	मध्य विद्यालय, सहसौल				
75	SSS-75	पूर्णियाँ	1	मध्य विद्यालय, गंगौली	764.93	15.30	26,900.00	15 माह
			2	मध्य विद्यालय, जियनगंज मध्य				
			3	मध्य विद्यालय, काझी				
			4	मध्य विद्यालय, हरिपुरमादी				
			5	मध्य विद्यालय, देवोत्तर				
			6	मध्य विद्यालय, बोराही				
			7	मध्य विद्यालय, रामपुर तिलक पूर्व				
76	SSS-76	पूर्णियाँ	1	मध्य विद्यालय, लालगंज	107.55	2.16	15,650.00	15 माह
77	SSS-77	पूर्णियाँ	1	आम मध्य विद्यालय, हसैली खुँडी	108.53	2.18	15,650.00	15 माह
78	SSS-78	अररिया	1	उत्क्रमित मध्य विद्यालय, बिकनी	225.10	4.51	15,650.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, होरिया				
79	SSS-79	अररिया	1	मध्य विद्यालय, डेनिया	112.71	2.26	15,650.00	15 माह
80	SSS-80	अररिया	1	उत्क्रमित मध्य विद्यालय, सिरसिया कला	111.50	2.23	15,650.00	15 माह
81	SSS-81	अररिया	1	मध्य विद्यालय, दर्मगंज	332.40	6.75	26,900.00	15 माह
			2	मध्य विद्यालय, फुलसरा				
			3	मध्य विद्यालय, डाला				

(Seal & Signature of Tenderer)




25-6-2014

Chief Engineer

B.S.E.I.D.C. Ltd, Patna

Rmk

82	SSS-82	अररिया	1	मध्य विद्यालय, लालपुर महुआ	328.47	6.57	26,900.00	15 माह
			2	मध्य विद्यालय, बड़हारा				
			3	कन्या मध्य विद्यालय, पोठिया				
83	SSS-84	अररिया	1	मध्य विद्यालय, मौजहा	221.27	4.43	15,650.00	15 माह
			2	मध्य विद्यालय, मधुलता				
84	SSS-85	अररिया	1	उत्क्रमित मध्य विद्यालय गौरिया	559.20	11.19	26,900.00	15 माह
			2	मध्य विद्यालय, परवाहा हरिजन				
			3	मध्य विद्यालय, बसगड़ा रामपुर				
			4	मध्य विद्यालय, बारा				
			5	मध्य विद्यालय, भागपरभाहा				
85	SSS-86	अररिया	1	मध्य विद्यालय, दोमोहना 2	109.56	2.20	15,650.00	15 माह
86	SSS-87	अररिया	1	मध्य विद्यालय, साहेबगंज	451.24	9.03	26,900.00	15 माह
			2	मध्य विद्यालय, डुमरबन्ना				
			3	मध्य विद्यालय, गढ़गामा				
			4	मध्य विद्यालय, भवानीपुर				
87	SSS-88	अररिया	1	मध्य विद्यालय, बेलवात	332.98	6.66	26,900.00	15 माह
			2	मध्य विद्यालय, कुसियारगंज				
			3	उत्क्रमित मध्य विद्यालय, तिरहुतबिष्टा				
88	SSS-89	कटिहार	1	मध्य विद्यालय, छोहार	214.70	4.30	15,650.00	15 माह
			2	मध्य विद्यालय, मलहरिया				
89	SSS-90	कटिहार	1	मध्य विद्यालय, कटरिया	214.68	4.30	15,650.00	15 माह
			2	मध्य विद्यालय, जरलाही				
90	SSS-91	कटिहार	1	मध्य विद्यालय, नेपहा	216.75	4.34	15,650.00	15 माह
			2	मध्य विद्यालय, टिकैली				
91	SSS-92	किशनगंज	1	उत्क्रमित मध्य विद्यालय, लोधा	339.89	6.80	26,900.00	15 माह
			2	मध्य विद्यालय, बेहुलदंगी				
			3	उत्क्रमित मध्य विद्यालय, पंचगाछी				
92	SSS-93	किशनगंज	1	उत्क्रमित मध्य विद्यालय, लौचा	222.58	4.46	15,650.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, मंडलटोला डोहर				
93	SSS-94	किशनगंज	1	उत्क्रमित मध्य विद्यालय, बालानगर	111.36	2.23	15,650.00	15 माह
94	SSS-95	किशनगंज	1	मध्य विद्यालय, पनीसाल	110.65	2.22	15,650.00	15 माह
95	SSS-96	किशनगंज	1	मध्य विद्यालय, जालुचौक	337.85	6.76	26,900.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, सोनापुर				
			3	मध्य विद्यालय, बेलगाछी वीरपुर				
96	SSS-97	किशनगंज	1	उत्क्रमित मध्य विद्यालय, आदिवासी टोला भोरहा	230.08	4.61	15,650.00	15 माह
			2	मध्य विद्यालय, भोजपुर, बलवा				
97	SSS-98	पटना	1	मध्य विद्यालय, राघोपुर, बिहटा, पटना	105.51	2.12	15,650.00	15 माह
98	SSS-99	पटना	1	उत्क्रमित मध्य विद्यालय, बरियारपुर	106.32	2.13	15,650.00	15 माह
99	SSS-100	नालन्दा	1	मध्य विद्यालय, कोबिल	208.37	4.17	15,650.00	15 माह
			2	मध्य विद्यालय, चौरमा				
100	SSS-101	नालन्दा	1	उत्क्रमित मध्य विद्यालय, हवेली	104.25	2.09	15,650.00	15 माह
101	SSS-102	नालन्दा	1	उत्क्रमित मध्य विद्यालय, हरगाँव	314.06	6.29	26,900.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, सकरौल				
			3	उत्क्रमित मध्य विद्यालय, परौहा				
102	SSS-103	नालन्दा	1	मध्य विद्यालय, कपसिआवन	209.37	4.19	15,650.00	15 माह

(Seal & Signature of Tenderer)

अमित कुमार सिंह

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

11

10	SSS-104	नालन्दा	1	उर्दू मध्य विद्यालय, सोबईत	520.78	10.42	26,900.00	15 माह
			2	मध्य विद्यालय, चौदी माँउ				
			3	मध्य विद्यालय, कुल				
			4	उत्क्रमित मध्य विद्यालय, पांकी				
			5	उत्क्रमित मध्य विद्यालय, जयकिशुन बिगहा				
10.1	SSS-105	नालन्दा	1	मध्य विद्यालय, आदमपुर	208.16	4.17	15,650.00	15 माह
			2	मध्य विद्यालय, चौरसुआ				
10.3	SSS-106	नालन्दा	1	मध्य विद्यालय, नेहुसा	105.36	2.11	15,650.00	15 माह
10.6	SSS-107	नालन्दा	1	उ०आ०मध्य विद्यालय, मई	104.52	2.10	15,650.00	15 माह
10.7	SSS-108	नालन्दा	1	मध्य विद्यालय, मोड़तलाव	210.57	4.22	15,650.00	15 माह
			2	मध्य विद्यालय, कथौली				
10.1	SSS-109	नालन्दा	1	मध्य विद्यालय, काजीचक	210.42	4.21	15,650.00	15 माह
			2	मध्य विद्यालय, मलावन				
10.9	SSS-120	नालन्दा	1	मध्य विद्यालय, ममुरादाबाद	209.96	4.20	15,650.00	15 माह
			2	मध्य विद्यालय, सरदारविगहा				
11.1	SSS-121	नालन्दा	1	उर्दू मध्य विद्यालय, उगावन	521.31	10.43	26,900.00	15 माह
				उत्क्रमित मध्य विद्यालय, ओइयाब				
				मध्य विद्यालय, खेतलपुरा				
				मध्य विद्यालय, जाना				
				मध्य विद्यालय, औन्डा				
11.1	SSS-122	भोजपुर	1	मध्य विद्यालय, नथमलपुर	103.58	2.08	15,650.00	15 माह
11.2	SSS-123	भोजपुर	1	उत्क्रमित मध्य विद्यालय, वीरपुर	208.81	4.18	15,650.00	15 माह
			2	प्रायोगिक मध्य विद्यालय, बिहियाँ				
11.3	SSS-124	भोजपुर	1	उत्क्रमित मध्य विद्यालय, एयार	210.14	4.21	15,650.00	15 माह
			2	मध्य विद्यालय, लहराबाद				
11.4	SSS-125	भोजपुर	1	मध्य विद्यालय, चचार	104.91	2.10	15,650.00	15 माह
11.5	SSS-126	भोजपुर	1	मध्य विद्यालय, लहंग डुमरिया	104.55	2.10	15,650.00	15 माह
11.6	SSS-127	भोजपुर	1	उत्क्रमित मध्य विद्यालय, खलीसा	309.13	6.19	26,900.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, बामपौली				
			3	उत्क्रमित मध्य विद्यालय, वीरमपुर				
11.7	SSS-128	भोजपुर	1	मध्य विद्यालय, चंदा	208.58	4.18	15,650.00	15 माह
			2	मध्य विद्यालय, बेरई				
11.8	SSS-129	भोजपुर	1	उत्क्रमित मध्य विद्यालय, दाँवा	209.45	4.19	15,650.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, बैरही				
11.9	SSS-130	भोजपुर	1	मध्य विद्यालय, खजुरियाँ	205.53	4.12	15,650.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, लक्ष्मणपुर				
12.0	SSS-131	रोहतास	1	मध्य विद्यालय, मनियारी	208.93	4.18	15,650.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, रूपैठा				
12.1	SSS-132	रोहतास	1	उत्क्रमित मध्य विद्यालय, लहेरी	209.97	4.20	15,650.00	15 माह
			2	मध्य विद्यालय, कुरुसा				
12.2	SSS-133	रोहतास	1	मध्य विद्यालय, मुहम्मदपुर	414.24	8.29	26,900.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, गोतहर				
			3	उत्क्रमित मध्य विद्यालय, सेमरी				
			4	मध्य विद्यालय, थनुआँ				
12.3	SSS-134	रोहतास	1	उत्क्रमित मध्य विद्यालय, भडकुडिया	206.54	4.14	15,650.00	15 माह
			2	मध्य विद्यालय, दुर्गापुर				
12.4	SSS-135	रोहतास	1	मध्य विद्यालय, वेलवैया	419.01	8.39	26,900.00	15 माह
			2	मध्य विद्यालय, बराडीकला				
			3	मध्य विद्यालय, मेदनीपुर				
			4	उत्क्रमित मध्य विद्यालय, खलसापुर				
12.5	SSS-136	रोहतास	1	मध्य विद्यालय, सेवही	103.43	2.07	15,650.00	15 माह
12.6	SSS-137	रोहतास	1	मध्य विद्यालय, भदोखरा	103.43	2.07	15,650.00	15 माह

(Seal & Signature of Tenderer)



Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Rmt

127	SSS-138	रोहतास	1	उत्क्रमित मध्य विद्यालय, दवनपुर	308.31	6.17	26,900.00	15 माह
			2	मध्य विद्यालय, दरिगांव				
			3	मध्य विद्यालय, गोटपा				
128	SSS-139	रोहतास	1	मध्य विद्यालय, भैसही	309.40	6.19	26,900.00	15 माह
			2	मध्य विद्यालय, नौगाई				
			3	मध्य विद्यालय, पतियाद				
129	SSS-140	रोहतास	1	मध्य विद्यालय, भुडकुडिया	209.19	4.19	15,650.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, गणेशपुर				
130	SSS-141	रोहतास	1	मध्य विद्यालय, मढियाँ	103.58	2.08	15,650.00	15 माह
131	SSS-142	रोहतास	1	उत्क्रमित मध्य विद्यालय, भवनाथपुर	106.15	2.13	15,650.00	15 माह
132	SSS-143	रोहतास	1	उत्क्रमित मध्य विद्यालय, सलैया	205.83	4.12	15,650.00	15 माह
			2	मध्य विद्यालय, कौपा				
133	SSS-144	बक्सर	1	मध्य विद्यालय, बिझौरा	211.32	4.23	15,650.00	15 माह
			2	मध्य विद्यालय, बैरी				
134	SSS-145	बक्सर	1	मध्य विद्यालय, बोक्सा	210.92	4.22	15,650.00	15 माह
			2	मध्य विद्यालय, जासो				
135	SSS-146	बक्सर	1	ह0उ0 मध्य विद्यालय, रघुनाथपुर	212.63	4.26	15,650.00	15 माह
			2	मध्य विद्यालय, बरादी				
136	SSS-147	बक्सर	1	क0 मध्य विद्यालय, दुल्लहपुर	317.85	6.36	26,900.00	15 माह
			2	मध्य विद्यालय, छोटका सिंहनपुरा				
			3	मध्य विद्यालय, एकौना				
137	SSS-148	बक्सर	1	मध्य विद्यालय, मंगराव	106.38	2.13	15,650.00	15 माह
138	SSS-149	बक्सर	1	मध्य विद्यालय, पवनी	317.65	6.36	26,900.00	15 माह
			2	मध्य विद्यालय, सगरा				
			3	मध्य विद्यालय, चुन्नी				
139	SSS-150	बक्सर	1	मध्य विद्यालय, भदार	211.67	4.24	15,650.00	15 माह
			2	मध्य विद्यालय, गोविन्दपुर				
140	SSS-151	कैमूर	1	उत्क्रमित मध्य विद्यालय, दादर	315.37	6.31	26,900.00	15 माह
			2	मध्य विद्यालय, भरखर				
			3	उत्क्रमित मध्य विद्यालय, अमेठ				
141	SSS-152	कैमूर	1	मध्य विद्यालय, भेकास	104.49	2.09	15,650.00	15 माह
142	SSS-153	कैमूर	1	उत्क्रमित मध्य विद्यालय, कसेर	210.11	4.21	15,650.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, सिंधी				
143	SSS-154	कैमूर	1	उत्क्रमित मध्य विद्यालय, गोरा	106.08	2.13	15,650.00	15 माह
144	SSS-155	कैमूर	1	मध्य विद्यालय, भारारी	106.27	2.13	15,650.00	15 माह
145	SSS-156	कैमूर	1	मध्य विद्यालय, बढौना	105.13	2.11	15,650.00	15 माह
146	SSS-157	कैमूर	1	उत्क्रमित मध्य विद्यालय, चफना	216.41	4.33	15,650.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, न्यू				
147	SSS-158	मुंगेर	1	मध्य विद्यालय, समदा हथिया	420.22	8.41	26,900.00	15 माह
			2	मध्य विद्यालय, लडुई				
			3	मध्य विद्यालय, कन्दनी				
			4	मध्य विद्यालय, अग्रहण				
148	SSS-159	मुंगेर	1	मध्य विद्यालय, चन्दनियाँ	106.58	2.14	15,650.00	15 माह
149	SSS-160	मुंगेर	1	मध्य विद्यालय, बिहमा	316.55	6.34	26,900.00	15 माह
			2	मध्य विद्यालय, रामपुर				
			3	मध्य विद्यालय, खुटिया				
150	SSS-161	मुंगेर	1	मध्य विद्यालय, बोचाही	104.22	2.09	15,650.00	15 माह
151	SSS-162	मुंगेर	1	मध्य विद्यालय, मासुमगंज	105.10	2.11	15,650.00	15 माह
152	SSS-163	मुंगेर	1	मध्य विद्यालय, भुना	211.80	4.24	15,650.00	15 माह
			2	मध्य विद्यालय, धौरी				
153	SSS-164	शेखपुरा	1	उत्क्रमित मध्य विद्यालय, करकी	311.86	6.24	26,900.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, बेलछी				
			3	उत्क्रमित मध्य विद्यालय, वरुणा				
154	SSS-165	शेखपुरा	1	मध्य विद्यालय, छतियारा	104.20	2.09	15,650.00	15 माह

(Seal & Signature of Tenderer)



Chief Engineer
B.S.E.I.D.C. Ltd, Patna

153	SSS-166	शेखपुरा	1	मध्य विद्यालय, बैरिया बीघा	103.69	2.08	15,650.00	15 माह
153	SSS-167	वेगूसराय	1	उत्क्रमित मध्य विद्यालय, मसुराज	214.48	4.29	15,650.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, मुशहरी				
15	SSS-168	वेगूसराय	1	मध्य विद्यालय, बखरी	214.48	4.29	15,650.00	15 माह
			2	मध्य विद्यालय, चक्करभीड़, नदौल				
153	SSS-169	वेगूसराय	1	मध्य विद्यालय, मिर्जापुर चौद	520.63	10.42	26,900.00	15 माह
			2	मध्य विद्यालय, भवनगामा				
			3	उत्क्रमित मध्य विद्यालय, चकीया पुनर्वास				
			4	उत्क्रमित मध्य विद्यालय, असुरारी				
			5	मध्य विद्यालय, केशवे				
159	SSS-170	वेगूसराय	1	मध्य विद्यालय, पपरौर	103.94	2.08	15,650.00	15 माह
160	SSS-171	वेगूसराय	1	उत्क्रमित मध्य विद्यालय, कुसमौत	104.70	2.10	15,650.00	15 माह
161	SSS-172	वेगूसराय	1	मध्य विद्यालय, दरियापुर	210.48	4.21	15,650.00	15 माह
			2	मध्य विद्यालय, गोदरगामा				
162	SSS-173	वेगूसराय	1	मध्य विद्यालय, ताजपुर	104.62	2.10	15,650.00	15 माह
163	SSS-174	वेगूसराय	1	मध्य विद्यालय, सादपुर	534.25	10.69	26,900.00	15 माह
			2	मध्य विद्यालय, रहुआ				
			3	मध्य विद्यालय, रसलपुर				
			4	मध्य विद्यालय, दीहा				
			5	मध्य विद्यालय, रघुनाथपुर				
164	SSS-175	वेगूसराय	1	उत्क्रमित मध्य विद्यालय, नया टोला, कल्याणपुर	323.47	6.47	26,900.00	15 माह
			2	मध्य विद्यालय, राजोपुर				
			3	मध्य विद्यालय, सिसौनी				
165	SSS-176	वेगूसराय	1	मध्य विद्यालय, अकाहा रामपुर	312.97	6.26	26,900.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, ओझा टोल				
			3	मध्य विद्यालय, पिढौली				
166	SSS-177	वेगूसराय	1	उत्क्रमित मध्य विद्यालय, चकमुजफ्फर	209.47	4.19	15,650.00	15 माह
			2	कन्या मध्य विद्यालय, पहसरा				
167	SSS-178	वेगूसराय	1	मध्य विद्यालय, मछराहा, रजौर	320.87	6.42	26,900.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, कोरियमा				
			3	उत्क्रमित मध्य विद्यालय, प्राणपुर हिन्दी				
168	SSS-179	लखीसराय	1	मध्य विद्यालय, प्रतापपुर	206.21	4.13	15,650.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, लक्ष्मीपुर, सहजादपुर				
169	SSS-180	लखीसराय	1	मध्य विद्यालय, घोघी बरियारपुर	311.03	6.23	26,900.00	15 माह
			2	मध्य विद्यालय, नवकाडीह उरैन				
			3	मध्य विद्यालय, कजरा				
170	SSS-181	लखीसराय	1	उत्क्रमित मध्य विद्यालय, तियाचक	206.35	4.13	15,650.00	15 माह
			2	मध्य विद्यालय, भांदर				
171	SSS-182	लखीसराय	1	मध्य विद्यालय, बन्नु बगीचा	206.92	4.14	15,650.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, बसुआचक्र				
172	SSS-183	लखीसराय	1	उत्क्रमित मध्य विद्यालय, खगौर	102.53	2.06	15,650.00	15 माह
173	SSS-184	जमुई	1	मध्य विद्यालय, रूपावेल	417.75	8.36	26,900.00	15 माह
			2	मध्य विद्यालय, धरमपुर				
			3	उत्क्रमित मध्य विद्यालय, टिहियादिनारी				
			4	मध्य विद्यालय, कैड़ाकादो				
174	SSS-185	जमुई	1	मध्य विद्यालय, पैरगाहा	317.07	6.35	26,900.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, सुन्दरी टांड				
			3	मध्य विद्यालय, चैन				
175	SSS-186	जमुई	1	मध्य विद्यालय, लाखेय	208.66	4.18	15,650.00	15 माह
			2	मध्य विद्यालय, पंचेश्वरी				

(Seal & Signature of Tenderer)



Chief Engineer
B.S.E.I.D.C. Ltd, Patna

176	SSS-187	जमुई	1	मध्य विद्यालय, सबलबीघा	208.47	4.17	15,650.00	15 माह
			2	मध्य विद्यालय, नवकाडीह				
177	SSS-188	जमुई	1	मध्य विद्यालय, धमनाडीह	873.92	17.48	26,900.00	15 माह
			2	मध्य विद्यालय, सिमरा				
			3	मध्य विद्यालय, दरवा				
			4	मध्य विद्यालय, मरही बसबुटिया				
			5	मध्य विद्यालय, पांडेडीह				
			6	मध्य विद्यालय, ठाढ़ी				
			7	मध्य विद्यालय, माधोपुर				
			8	मध्य विद्यालय, सिमरिया				
178	SSS-189	जमुई	1	मध्य विद्यालय, प्रतापपुर	103.51	2.08	15,650.00	15 माह
179	SSS-190	जमुई	1	उत्क्रमित मध्य विद्यालय, सिंधिया	104.90	2.10	15,650.00	15 माह
180	SSS-191	खगड़िया	1	मध्य विद्यालय, बोबिल फुलवरिया	435.30	8.71	26,900.00	15 माह
			2	मध्य विद्यालय, माली				
			3	मध्य विद्यालय, सकरोहर				
			4	मध्य विद्यालय, पचौत				
181	SSS-192	खगड़िया	1	मध्य विद्यालय, अमनी	106.17	2.13	15,650.00	15 माह
182	SSS-193	खगड़िया	1	मध्य विद्यालय, रोहियार	106.85	2.14	15,650.00	15 माह
183	SSS-194	दरभंगा	1	मध्य विद्यालय, घनश्यामपुर	111.07	2.23	15,650.00	15 माह
184	SSS-195	दरभंगा	1	उत्क्रमित मध्य विद्यालय, उसरी	661.00	13.22	26,900.00	15 माह
			2	मध्य विद्यालय, हरौली				
			3	मध्य विद्यालय, औराही				
			4	मध्य विद्यालय, हरिनगर				
			5	मध्य विद्यालय, घोरदोर				
			6	मध्य विद्यालय, बरगौंव				
185	SSS-196	दरभंगा	1	मध्य विद्यालय, शिवनगर	438.19	8.77	26,900.00	15 माह
			2	मध्य विद्यालय, अम्बाबिजुलिया				
			3	मध्य विद्यालय, लदहो				
			4	मध्य विद्यालय, साहो				
186	SSS-197	दरभंगा	1	उत्क्रमित मध्य विद्यालय, रामपुर	109.10	2.19	15,650.00	15 माह
187	SSS-198	मधुबनी	1	मध्य विद्यालय, चिकना	340.65	6.82	26,900.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, केवटना				
			3	उत्क्रमित मध्य विद्यालय, बसुआरा				
188	SSS-199	मधुबनी	1	मध्य विद्यालय, नहरी	339.68	6.80	26,900.00	15 माह
			2	मध्य विद्यालय, अंधारवन				
			3	मध्य विद्यालय, सिकटियाही				
189	SSS-200	मधुबनी	1	उत्क्रमित मध्य विद्यालय, कुसमार	557.96	11.16	26,900.00	15 माह
			2	मध्य विद्यालय, कसमा मरार				
			3	उत्क्रमित मध्य विद्यालय, छपराढ़ी				
			4	मध्य विद्यालय, रसीदपुर				
			5	उत्क्रमित मध्य विद्यालय, इनरवा पूरब				
190	SSS-201	मधुबनी	1	मध्य विद्यालय, सिमरा	332.21	6.65	26,900.00	15 माह
			2	मध्य विद्यालय, सिङ्खरिया				
			3	मध्य विद्यालय, अड़रिया संग्राम				
191	SSS-202	मधुबनी	1	मध्य विद्यालय, कुल्हड़िया	337.09	6.75	26,900.00	15 माह
			2	मध्य विद्यालय, विकमशेर				
			3	उत्क्रमित मध्य विद्यालय, बलानशेरपुरब				
192	SSS-203	मधुबनी	1	उत्क्रमित मध्य विद्यालय, कौआहा	565.95	11.32	26,900.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, चन्दन कसेरा				
			3	मध्य विद्यालय, गौसनगर				
			4	उत्क्रमित मध्य विद्यालय, महथौर				
			5	मध्य विद्यालय, घोड़बंकी				
193	SSS-204	मधुबनी	1	मध्य विद्यालय, जरैल	106.38		15,650.00	15 माह



(Seal & Signature of Tenderer)



Chief Engineer
B.S.E.I.D.C. Ltd, Patna

193	SSS-205	मधुबनी	1	मध्य विद्यालय, पोखरौनी	452.14	9.05	26,900.00	15 माह
			2	मध्य विद्यालय, बिहारी				
			3	उत्क्रमित मध्य विद्यालय, औरा				
			4	उत्क्रमित मध्य विद्यालय, केरबा				
194	SSS-206	मधुबनी	1	उत्क्रमित मध्य विद्यालय, बकुआ	449.51	9.00	26,900.00	15 माह
			2	मध्य विद्यालय, दालख				
			3	मध्य विद्यालय, टेंगराहा				
			4	उत्क्रमित मध्य विद्यालय, परबलपुर				
195	SSS-207	मधुबनी	1	उत्क्रमित मध्य विद्यालय, रामपुर	113.49	2.27	15,650.00	15 माह
197	SSS-208	मधुबनी	1	मध्य विद्यालय, भौर	334.39	6.69	26,900.00	15 माह
			2	मध्य विद्यालय, नवहथ				
			3	मध्य विद्यालय, भवानीपुर				
198	SSS-209	मधुबनी	1	उत्क्रमित मध्य विद्यालय, माड़र	444.88	8.90	26,900.00	15 माह
			2	मध्य विद्यालय, बलिया				
			3	मध्य विद्यालय, इजरा				
			4	उत्क्रमित मध्य विद्यालय, नीमा				
199	SSS-210	मधुबनी	1	उत्क्रमित मध्य विद्यालय, रही पूरब	666.63	13.34	26,900.00	15 माह
			2	मध्य विद्यालय, सुगौना पोखर अ0जा0				
			3	मध्य विद्यालय, सिमरी				
			4	उत्क्रमित मध्य विद्यालय, बड़हारा				
			5	मध्य विद्यालय, जहरमोहरा				
			6	उत्क्रमित मध्य विद्यालय, राधोपुर				
200	SSS-211	मधुबनी	1	मध्य विद्यालय, अमौजा	339.70	6.80	26,900.00	15 माह
			2	मध्य विद्यालय, महथौर खुर्द				
			3	मध्य विद्यालय, सिजौलिया, गोठ				
201	SSS-212	मधुबनी	1	मध्य विद्यालय, कुवाढ़	112.92	2.26	15,650.00	15 माह
202	SSS-213	मधुबनी	1	मध्य विद्यालय, मदनपट्टी	112.25	2.25	15,650.00	15 माह
203	SSS-214	मधुबनी	1	मध्य विद्यालय, भरफोडी	802.14	16.05	26,900.00	15 माह
			2	मध्य विद्यालय, नरेन्द्रपुर				
			3	उत्क्रमित मध्य विद्यालय, करियौत				
			4	उत्क्रमित मध्य विद्यालय, नरही				
			5	मध्य विद्यालय, बेलही कचनरवा				
			6	उत्क्रमित मध्य विद्यालय, कुरीवन				
			7	उत्क्रमित मध्य विद्यालय, थरुआरी				
204	SSS-215	मधुबनी	1	मध्य विद्यालय, एकहरी	459.22	9.19	26,900.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, भगवतीपुर				
			3	मध्य विद्यालय, कुमरखत				
			4	मध्य विद्यालय, सिंधप परसाही				
205	SSS-216	समस्तीपुर	1	उत्क्रमित मध्य विद्यालय, मसीना	324.64	6.50	26,900.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, बथनाहा				
			3	मध्य विद्यालय, भानपुर				
206	SSS-217	समस्तीपुर	1	उत्क्रमित मध्य विद्यालय, धोलीयाही	107.25	2.15	15,650.00	15 माह
207	SSS-218	समस्तीपुर	1	मध्य विद्यालय धर्मपुर बंदे	107.63	2.16	15,650.00	15 माह
208	SSS-219	समस्तीपुर	1	उत्क्रमित मध्य विद्यालय, जन्दाहा	108.17	2.17	15,650.00	15 माह
209	SSS-220	समस्तीपुर	1	उत्क्रमित मध्य विद्यालय, परहट	218.21	4.37	15,650.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, नीरपुर भररिया				
210	SSS-221	समस्तीपुर	1	आदर्श राजकीय मध्य विद्यालय, काँचा	214.36	4.29	15,650.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, सोठगामा				
211	SSS-222	समस्तीपुर	1	मध्य विद्यालय, कल्याणपुर	107.54	2.16	15,650.00	15 माह
212	SSS-223	समस्तीपुर	1	उत्क्रमित मध्य विद्यालय, देवघा	217.56	4.36	15,650.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, हसनपुर				

(Seal & Signature of Tenderer)





16




213	SSS-224	समस्तीपुर	1	उत्क्रमित मध्य विद्यालय, गोविन्दपुर	107.71	2.16	15,650.00	15 माह
214	SSS-225	समस्तीपुर	1	उत्क्रमित मध्य विद्यालय, महुली	430.84	8.62	26,900.00	15 माह
			2	मध्य विद्यालय, पंचगामा				
			3	उत्क्रमित मध्य विद्यालय, भटोट				
			4	उत्क्रमित मध्य विद्यालय, पीटधादोभी				
215	SSS-226	समस्तीपुर	1	मध्य विद्यालय, शंभुपट्टी	428.15	8.57	26,900.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, बाजितपुर				
			3	मध्य विद्यालय धूरलख				
			4	उत्क्रमित मध्य विद्यालय, सिलौट				
216	SSS-227	समस्तीपुर	1	उत्क्रमित मध्य विद्यालय, रसलपुर	321.51	6.44	26,900.00	15 माह
			2	राजकीय मध्य विद्यालय, अख्तियारपुर				
			3	उत्क्रमित मध्य विद्यालय, नौआचक				
217	SSS-228	समस्तीपुर	1	उत्क्रमित मध्य विद्यालय, परोरिया	107.54	2.16	15,650.00	15 माह
218	SSS-229	समस्तीपुर	1	उत्क्रमित मध्य विद्यालय, हजपुरवा	107.18	2.15	15,650.00	15 माह
219	SSS-230	भागलपुर	1	मध्य विद्यालय, अलालपुर	209.89	4.20	15,650.00	15 माह
			2	मध्य विद्यालय, बगडी				
220	SSS-231	भागलपुर	1	मध्य विद्यालय, रामनगर	210.17	4.21	15,650.00	15 माह
			2	मध्य विद्यालय, मोती टोला				
221	SSS-232	भागलपुर	1	मध्य विद्यालय, कटोरिया	103.88	2.08	15,650.00	15 माह
222	SSS-233	भागलपुर	1	मध्य विद्यालय, औलियाबाद	106.37	2.13	15,650.00	15 माह
223	SSS-234	भागलपुर	1	मध्य विद्यालय, बसंतपुर	415.75	8.32	26,900.00	15 माह
			2	मध्य विद्यालय, दउवा				
			3	मध्य विद्यालय, ज्ञानवती टपुआ				
			4	मध्य विद्यालय, परशुरामपुर				
224	SSS-235	भागलपुर	1	मध्य विद्यालय, भवानीपुर टोला	211.53	4.24	15,650.00	15 माह
			2	मध्य विद्यालय, बनिया				
225	SSS-236	भागलपुर	1	मध्य विद्यालय, वासुदेवपुर	317.04	6.35	26,900.00	15 माह
			2	मध्य विद्यालय, पंचरुखी				
			3	मध्य विद्यालय, भंडारवन				
226	SSS-237	भागलपुर	1	मध्य विद्यालय, बैजनाथपुर	104.44	2.09	15,650.00	15 माह
227	SSS-238	भागलपुर	1	मध्य विद्यालय, तेलौधा	104.06	2.09	15,650.00	15 माह
228	SSS-239	भागलपुर	1	मध्य विद्यालय, विशनपुर	104.28	2.09	15,650.00	15 माह
229	SSS-240	भागलपुर	1	मध्य विद्यालय, रायपुर	319.01	6.39	26,900.00	15 माह
			2	मध्य विद्यालय, भवानीपुर				
			3	कन्या मध्य विद्यालय, मथुरापुर				
230	SSS-241	भागलपुर	1	मध्य विद्यालय, जगतपुर	210.53	4.22	15,650.00	15 माह
			2	मध्य विद्यालय, खैरपुर				
231	SSS-242	भागलपुर	1	मध्य विद्यालय, मकन्दपुर	105.23	2.11	15,650.00	15 माह
232	SSS-243	भागलपुर	1	मध्य विद्यालय, पचगछिया	208.09	4.17	15,650.00	15 माह
			2	मध्य विद्यालय, डिमहा				
233	SSS-244	भागलपुर	1	मध्य विद्यालय, विशनपुर जिच्छे	626.70	12.54	26,900.00	15 माह
			2	मध्य विद्यालय, सोनूडीह				
			3	मध्य विद्यालय, मोहनपुर				
			4	मध्य विद्यालय, गंगाकरहरिया				
			5	मध्य विद्यालय, मुक्तापुर				
			6	मध्य विद्यालय, काशील				
234	SSS-245	भागलपुर	1	मध्य विद्यालय, अरसी मकैता	312.61	6.26	26,900.00	15 माह
			2	मध्य विद्यालय, चन्दाडीह				
			3	मध्य विद्यालय, मथुरापुर				
235	SSS-246	बांका	1	प्रो० मध्य विद्यालय, अमरपुर	105.34	2.11	15,650.00	15 माह
236	SSS-247	बांका	1	प्रो० मध्य विद्यालय, महुआ	104.91	2.10	15,650.00	15 माह
237	SSS-248	बांका	1	प्रो० मध्य विद्यालय, बभनगामा	209.98	4.20	15,650.00	15 माह
			2	प्रो० मध्य विद्यालय, झपनियां				


(Seal & Signature of Tenderer)



Chief Engineer
B.S.E.I.D.C. Ltd, Patna

233	SSS-249	बांका	1	मध्य विद्यालय, श्रीनगर	108.09	2.17	15,650.00	
233	SSS-250	बांका	1	मध्य विद्यालय, इनारावरण	215.33	4.31	15,650.00	15 माह
			2	प्रो० मध्य विद्यालय, छाताकुरुम				
240	SSS-251	बांका	1	प्रो० मध्य विद्यालय, अलीपुर धनियां	209.00	4.18	15,650.00	15 माह
			2	मध्य विद्यालय, लशकरी				
241	SSS-252	बांका	1	मध्य विद्यालय, कोडिया इनारावरण	429.27	8.59	26,900.00	15 माह
			2	प्रो० मध्य विद्यालय, धावा कन्या				
			3	प्रो० मध्य विद्यालय, सादपुर				
			4	मध्य विद्यालय, धनकुडिया				
242	SSS-253	बांका	1	प्रो० मध्य विद्यालय, मैनामा	210.39	4.21	15,650.00	15 माह
			2	मध्य विद्यालय, गरीबपुर (उर्दू)				
243	SSS-254	गया	1	मध्य विद्यालय, वंशी	418.32	8.37	26,900.00	15 माह
			2	मध्य विद्यालय, विराज				
			3	मध्य विद्यालय, झिकटियाकला				
			4	मध्य विद्यालय, वसेता				
244	SSS-255	गया	1	उर्दू मध्य विद्यालय, वंडी	103.96	2.08	15,650.00	15 माह
245	SSS-256	गया	1	मध्य विद्यालय, रौशनगंज	102.68	2.06	15,650.00	15 माह
246	SSS-257	गया	1	मध्य विद्यालय, लुटुआ	206.22	4.13	15,650.00	15 माह
			2	मध्य विद्यालय, मोनेया				
247	SSS-258	गया	1	मध्य विद्यालय, दिवनियां	208.04	4.17	15,650.00	15 माह
			2	मध्य विद्यालय, नवाडीह				
248	SSS-259	गया	1	मध्य विद्यालय, जमड़ी	408.89	8.18	26,900.00	15 माह
			2	मध्य विद्यालय, पररिया				
			3	मध्य विद्यालय, मोचारिम				
			4	मध्य विद्यालय, शेरवारा				
249	SSS-260	गया	1	मध्य विद्यालय, विशुनपुर	103.37	2.07	15,650.00	15 माह
250	SSS-261	गया	1	मध्य विद्यालय, जेठुआडाहा	206.84	4.14	15,650.00	15 माह
			2	मध्य विद्यालय, खुडुआ				
251	SSS-262	गया	1	मध्य विद्यालय, गेरे	205.11	4.11	15,650.00	15 माह
			2	मध्य विद्यालय, भोरे				
252	SSS-263	गया	1	मध्य विद्यालय, सरिया	102.85	2.06	15,650.00	15 माह
253	SSS-264	गया	1	मध्य विद्यालय, उचिरमा	307.28	6.15	26,900.00	15 माह
			2	मध्य विद्यालय, मोहनपुर				
			3	मध्य विद्यालय, कचौड़ी				
254	SSS-265	गया	1	मध्य विद्यालय, बरहा	209.37	4.19	15,650.00	15 माह
			2	मध्य विद्यालय, हेसरा रामपुर				
255	SSS-266	गया	1	मध्य विद्यालय, सलैयाकला	103.36	2.07	15,650.00	15 माह
256	SSS-267	गया	1	ग्राम-केवाली, थाना सं०-197	307.30	6.15	26,900.00	15 माह
			2	मध्य विद्यालय, कोरमां				
			3	ग्राम-धुर्वे थाना सं०-177				
257	SSS-268	गया	1	मध्य विद्यालय, श्यामकला	204.74	4.10	15,650.00	15 माह
			2	मध्य विद्यालय, निमा बुद्धौल				
258	SSS-269	गया	1	मध्य विद्यालय, बलबीधा	102.78	2.06	15,650.00	15 माह
259	SSS-270	गया	1	मध्य विद्यालय, नौवागढ़	206.78	4.14	15,650.00	15 माह
			2	मध्य विद्यालय, भेटौरा				
260	SSS-271	गया	1	मध्य विद्यालय, शेरपुर	409.65	8.20	26,900.00	15 माह
			2	मध्य विद्यालय, नौडिहा				
			3	मध्य विद्यालय, विरहिमा				
			4	मध्य विद्यालय, काज				
261	SSS-272	नवादा	1	उत्क्रमित मध्य विद्यालय, पवाई	203.70	4.08	15,650.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, अकरि				

(Seal & Signature of Tenderer)

 Chief Engineer
 B.S.E.I.D.C. Ltd, Patna

262	SSS-273	नवादा	1	उत्क्रमित मध्य विद्यालय, एकनार	101.62	2.04	15,650.00	15 माह
			1	उत्क्रमित मध्य विद्यालय, कोलडिहा				
263	SSS-274	नवादा	2	मध्य विद्यालय, खनपुरा	309.53	6.20	26,900.00	15 माह
			3	मध्य विद्यालय, अकम्बा				
264	SSS-275	नवादा	1	मध्य विद्यालय, केशौरी	101.80	2.04	15,650.00	15 माह
265	SSS-276	नवादा	1	मध्य विद्यालय, कुंज	102.21	2.05	15,650.00	15 माह
			1	उत्क्रमित मध्य विद्यालय, धामुचक				
266	SSS-277	नवादा	2	मध्य विद्यालय, चपरा	206.72	4.14	15,650.00	15 माह
267	SSS-278	नवादा	1	मध्य विद्यालय, थेरा	101.74	2.04	15,650.00	15 माह
			1	उत्क्रमित मध्य विद्यालय, बरबत्ता				
268	SSS-279	नवादा	2	उत्क्रमित मध्य विद्यालय, दाईबिगहा	203.81	4.08	15,650.00	15 माह
269	SSS-280	नवादा	1	उत्क्रमित मध्य विद्यालय, पछिया डीह	101.67	2.04	15,650.00	15 माह
			1	उत्क्रमित मध्य विद्यालय, फरहा				
			2	उत्क्रमित मध्य विद्यालय, तेलभद्रो				
270	SSS-281	नवादा	3	मध्य विद्यालय, भनेल	513.18	10.27	26,900.00	15 माह
			4	उत्क्रमित मध्य विद्यालय, फुलमा				
			5	उत्क्रमित मध्य विद्यालय, पसिया				
			1	उत्क्रमित मध्य विद्यालय, तेतरिया				
271	SSS-282	नवादा	2	मध्य विद्यालय, बुधवाड़ा	208.27	4.17	15,650.00	15 माह
			1	मध्य विद्यालय, खजुरी				
272	SSS-283	अरवल	2	मध्य विद्यालय, आधारचक	204.41	4.09	15,650.00	15 माह
			1	मध्य विद्यालय, उसरी				
273	SSS-284	अरवल	2	मध्य विद्यालय, बलिदाद	205.66	4.12	15,650.00	15 माह
274	SSS-285	अरवल	1	उत्क्रमित मध्य विद्यालय, कैथोलीदीपुर	101.87	2.04	15,650.00	15 माह
275	SSS-286	अरवल	1	मध्य विद्यालय, पोन्दिल	102.28	2.05	15,650.00	15 माह
276	SSS-287	अरवल	1	मध्य विद्यालय, रामपुर चौम	101.96	2.04	15,650.00	15 माह
			1	मध्य विद्यालय, कदोखरी				
277	SSS-288	औरंगाबाद	2	मध्य विद्यालय, पिठनुआ	205.43	4.11	15,650.00	15 माह
			1	मध्य विद्यालय, चौखडा				
			2	मध्य विद्यालय, किशुनपुर				
278	SSS-289	औरंगाबाद	3	मध्य विद्यालय, बैजाबिगहा	725.98	14.52	26,900.00	15 माह
			4	मध्य विद्यालय, बैराव				
			5	मध्य विद्यालय, घेउरा				
			6	मध्य विद्यालय, पोला गोरडीहा				
			7	मध्य विद्यालय, पीपरा बगाही				
			1	मध्य विद्यालय, सरावक				
279	SSS-290	औरंगाबाद	2	मध्य विद्यालय, पखनौर	206.09	4.13	15,650.00	15 माह
280	SSS-291	औरंगाबाद	1	मध्य विद्यालय, नारायणपुर	102.77	2.06	15,650.00	15 माह
			1	मध्य विद्यालय, बरंडा रामपुर				
281	SSS-292	औरंगाबाद	2	मध्य विद्यालय, कटैया	309.39	6.19	26,900.00	15 माह
			3	मध्य विद्यालय, बेला				
			1	मध्य विद्यालय, रामनगर				
282	SSS-293	औरंगाबाद	2	मध्य विद्यालय, मझीआव	417.45	8.35	26,900.00	15 माह
			3	मध्य विद्यालय, कंकर				
			4	मध्य विद्यालय, बेलाई				
283	SSS-294	औरंगाबाद	1	मध्य विद्यालय, बभन्डी	102.34	2.05	15,650.00	15 माह
			1	मध्य विद्यालय, घाटो				
284	SSS-295	औरंगाबाद	2	मध्य विद्यालय, शेखपुरा	204.57	4.10	15,650.00	15 माह
285	SSS-296	औरंगाबाद	1	मध्य विद्यालय, तुरता	104.08	2.09	15,650.00	15 माह
			1	उत्क्रमित मध्य विद्यालय, देवधरा				
286	SSS-297	जहानाबाद	2	उत्क्रमित मध्य विद्यालय, उत्तरसेरथु	204.22	4.09	15,650.00	15 माह
287	SSS-298	जहानाबाद	1	उत्क्रमित मध्य विद्यालय, उदू मलाठी	102.60	2.06	15,650.00	15 माह
288	SSS-299	जहानाबाद	1	मध्य विद्यालय, वैना	101.83	2.04	15,650.00	15 माह

(Seal & Signature of Tenderer)



Chief Engineer
B.S.E.I.D.C. Ltd, Patna

28	SSS-300	जहानाबाद	1	मध्य विद्यालय, केउर	102.47	2.05	15,650.00	15 माह
29	SSS-301	जहानाबाद	1	मध्य विद्यालय, घेजन	408.76	8.18	26,900.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, पंडौल				
			3	उत्क्रमित मध्य विद्यालय, जहांगीरपुर				
			4	उत्क्रमित मध्य विद्यालय, बढेता				
291	SSS-302	जहानाबाद	1	उत्क्रमित मध्य विद्यालय, धुरिया	102.04	2.05	15,650.00	15 माह
292	SSS-303	सहरसा	1	मध्य विद्यालय, पारसबन्नी	109.52	2.20	15,650.00	15 माह
293	SSS-304	सहरसा	1	मध्य विद्यालय, सुलिन्दाबाद	110.01	2.21	15,650.00	15 माह
294	SSS-305	सहरसा	1	मध्य विद्यालय, कन्दाहा	441.01	8.83	26,900.00	15 माह
			2	मध्य विद्यालय, थनवार				
			3	मध्य विद्यालय, तेलहर				
			4	मध्य विद्यालय, मंगरौनी				
295	SSS-306	सहरसा	1	मध्य विद्यालय, वेलवारा	110.44	2.21	15,650.00	15 माह
296	SSS-307	सहरसा	1	मध्य विद्यालय, कथडुमर	109.38	2.19	15,650.00	15 माह
297	SSS-308	सहरसा	1	मध्य विद्यालय, किशनपुर	220.38	4.41	15,650.00	15 माह
			2	मध्य विद्यालय, पस्तपर				
298	SSS-309	सहरसा	1	मध्य विद्यालय, गोदराम	438.57	8.78	26,900.00	15 माह
			2	मध्य विद्यालय, कोपा				
			3	मध्य विद्यालय, खजुराहा				
			4	मध्य विद्यालय, आरसी				
299	SSS-310	सहरसा	1	मध्य विद्यालय, बिहरा	110.56	2.22	15,650.00	15 माह
300	SSS-311	सहरसा	1	मध्य विद्यालय, अलनी	220.70	4.42	15,650.00	15 माह
			2	मध्य विद्यालय, खोचरदेवा				
301	SSS-312	सहरसा	1	कन्या मध्य विद्यालय, कासिमपुर	111.20	2.23	15,650.00	15 माह
302	SSS-313	सुपौल	1	मध्य विद्यालय, बनैलीपट्टी	920.32	18.41	26,900.00	15 माह
			2	मध्य विद्यालय, समदा				
			3	मध्य विद्यालय, निर्मली				
			4	मध्य विद्यालय, दादा				
			5	मध्य विद्यालय, हदयनगर				
			6	मध्य विद्यालय, पटेरवा				
			7	मध्य विद्यालय, परसा उर्दू				
			8	मध्य विद्यालय, विशनपुर चौधरी				
303	SSS-314	सुपौल	1	मध्य विद्यालय, टेकुना	113.98	2.28	15,650.00	15 माह
304	SSS-315	सुपौल	1	मध्य विद्यालय, गोनहा	563.29	11.27	26,900.00	15 माह
			2	मध्य विद्यालय, परसाही हाट				
			3	मध्य विद्यालय, पाण्डेयपट्टी				
			4	मध्य विद्यालय, मिरजावा				
			5	मध्य विद्यालय, मौन				
305	SSS-316	सुपौल	1	मध्य विद्यालय, कमलदहा	113.01	2.27	15,650.00	15 माह
306	SSS-317	सुपौल	1	मध्य विद्यालय, बसुली	112.37	2.25	15,650.00	15 माह
307	SSS-318	सुपौल	1	मध्य विद्यालय, रामपुरकला	698.88	13.98	26,900.00	15 माह
			2	मध्य विद्यालय, कारियापट्टी देवीपुर				
			3	मध्य विद्यालय, हुलास				
			4	मध्य विद्यालय, बौराहा, हिन्दी				
			5	मध्य विद्यालय, मोतिपुर				
			6	रामनाथ मध्य विद्यालय, गौसपुर				
308	SSS-319	सुपौल	1	मध्य विद्यालय, पिपराखुर्द	227.07	4.55	15,650.00	15 माह
			2	मध्य विद्यालय, झल्ला डुमरी				
309	SSS-320	सुपौल	1	मध्य विद्यालय, लालगंज	113.92	2.28	15,650.00	15 माह
310	SSS-321	सुपौल	1	मध्य विद्यालय, बैरौ	333.66	6.68	26,900.00	15 माह
			2	कन्या मध्य विद्यालय, बाड़ा				
			3	मुरली मनोहर मध्य विद्यालय, बरैल				

(Seal & Signature of Tenderer)



Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Bt

311	SSS-322	सुपौल	1	मध्य विद्यालय, रतनसार	567.02	11.35	26,900.00	15 माह
			2	मध्य विद्यालय, कटही				
			3	मध्य विद्यालय, गिरिधरपट्टी				
			4	मध्य विद्यालय, महदीपुर				
			5	मध्य विद्यालय, शेखटोला लक्ष्मीनियां				
312	SSS-323	मधेपुरा	1	मध्य विद्यालय, बेलारी	683.22	13.67	26,900.00	15 माह
			2	मध्य विद्यालय, रघुनिया				
			3	मध्य विद्यालय, रीता				
			4	उत्क्रमित मध्य विद्यालय, खूँटहा रजै				
			5	उत्क्रमित मध्य विद्यालय, इसरायन गोठ				
			6	उत्क्रमित मध्य विद्यालय, सुन्दरनगर (अ0जा0)				
313	SSS-324	मधेपुरा	1	मध्य विद्यालय, तिनकोनमा	221.29	4.43	15,650.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, रजनी मिल्लिक				
314	SSS-325	मधेपुरा	1	मध्य विद्यालय, रतनपट्टी, भेलाही	332.80	6.66	26,900.00	15 माह
			2	मध्य विद्यालय, जीतापुर				
			3	मध्य विद्यालय, दिग्घी				
315	SSS-326	मधेपुरा	1	मध्य विद्यालय, कठौतिया	332.51	6.66	26,900.00	15 माह
			2	मध्य विद्यालय, लक्ष्मीपुर				
			3	उत्क्रमित मध्य विद्यालय, रामगंज				
316	SSS-327	मधेपुरा	1	मध्य विद्यालय, तरहा डंडारी	443.36	8.87	26,900.00	15 माह
			2	मध्य विद्यालय, सबैला				
			3	उत्क्रमित मध्य विद्यालय, मानपुर				
			4	मध्य विद्यालय, पटोरी				
317	SSS-328	मधेपुरा	1	कबीर गंगा मध्य विद्यालय, बीड़ीरणपाल	221.20	4.43	15,650.00	15 माह
			2	मध्य विद्यालय, मंजौरा				
318	SSS-329	मधेपुरा	1	मध्य विद्यालय, विषपट्टी	334.29	6.69	26,900.00	15 माह
			2	मध्य विद्यालय, हरिहरपुर बजराहा				
			3	मध्य विद्यालय, कपसिया				
319	SSS-330	मधेपुरा	1	मध्य विद्यालय, शाहपुर	332.41	6.65	26,900.00	15 माह
			2	मध्य विद्यालय, टेमाभेला				
			3	मध्य विद्यालय, खोखसी बाड़ा, रामगंज				
320	SSS-331	सारण	1	मध्य विद्यालय, कोठैयाँ	213.66	4.28	15,650.00	15 माह
			2	मध्य विद्यालय, अनवल				
321	SSS-332	सारण	1	मध्य विद्यालय, बसाढ़ी	536.83	10.74	26,900.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, उमधा				
			3	कन्या मध्य विद्यालय, शेरपुर				
			4	उत्क्रमित मध्य विद्यालय, उदयपुरा				
			5	उत्क्रमित मध्य विद्यालय, बलवन टोला				
322	SSS-333	सारण	1	मध्य विद्यालय, हरपुर फरिदन	213.37	4.27	15,650.00	15 माह
			2	मध्य विद्यालय, सरैया बसंत				
323	SSS-334	सारण	1	उत्क्रमित मध्य विद्यालय, गौसपुर	216.20	4.33	15,650.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, नौतन				
324	SSS-335	सारण	1	उत्क्रमित मध्य विद्यालय, करही	214.98	4.30	15,650.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, पिपड़ा				
325	SSS-336	सारण	1	मध्य विद्यालय, सिसवाँ	106.73	2.14	15,650.00	15 माह
326	SSS-337	सारण	1	मध्य विद्यालय, भेल्दी	105.27	2.11	15,650.00	15 माह
327	SSS-338	सारण	1	मध्य विद्यालय, मुबारकपुर	106.12	2.13	15,650.00	15 माह
328	SSS-339	सारण	1	मध्य विद्यालय, गंडामन	107.11	2.15	15,650.00	15 माह

(Seal & Signature of Tenderer)



Chief Engineer
B.S.E.I.D.C. Ltd, Patna

329	SSS-340	सीवान	1	उत्क्रमित मध्य विद्यालय, डटवॉ	106.51	2.14	15,650.00	15 माह
330	SSS-341	गोपालगंज	1	मध्य विद्यालय, धरहरा मेला	330.68	6.62	26,900.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, पकड़ी डीह				
			3	मध्य विद्यालय, रसौती				
331	SSS-342	गोपालगंज	1	मध्य विद्यालय, तेलिया बौध	216.53	4.34	15,650.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, मधु सरेया				
332	SSS-343	गोपालगंज	1	उत्क्रमित मध्य विद्यालय, सोनबरसा	215.99	4.32	15,650.00	15 माह
			2	मध्य विद्यालय, कल्याणपुर				
333	SSS-344	गोपालगंज	1	उत्क्रमित मध्य विद्यालय, वेलसड	432.83	8.66	26,900.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, खजुरिया बालक				
			3	मध्य विद्यालय, माडनपुर				
			4	उत्क्रमित मध्य विद्यालय, नेउरी				
334	SSS-345	गोपालगंज	1	मध्य विद्यालय, कुसहॉ	665.15	13.31	26,900.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, महारादेउर				
			3	मध्य विद्यालय, जिगना दूबे				
			4	मध्य विद्यालय, सिसई				
			5	मध्य विद्यालय, लामीचौर				
			6	मध्य विद्यालय, वनकटा जागीरदारी				
335	SSS-346	गोपालगंज	1	उत्क्रमित मध्य विद्यालय, बुधसी	325.86	6.52	26,900.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, बुधिया				
			3	मध्य विद्यालय, झझवॉ				
336	SSS-347	गोपालगंज	1	उत्क्रमित मध्य विद्यालय, बंसतछापरा	216.78	4.34	15,650.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, मडवा				
337	SSS-348	गोपालगंज	1	उत्क्रमित मध्य विद्यालय, भोजछापरा	328.80	6.58	26,900.00	15 माह
			2	मध्य विद्यालय, विशम्भरपुर				
			3	उत्क्रमित मध्य विद्यालय, वृत्तभामी टोला				
338	SSS-349	गोपालगंज	1	उत्क्रमित मध्य विद्यालय, मानिकपुर कन्या	216.24	4.33	15,650.00	15 माह
			2	उत्क्रमित मध्य विद्यालय, खैरटिया राम नगर				
339	SSS-350	गोपालगंज	1	मध्य विद्यालय, सेमराव	216.22	4.33	15,650.00	15 माह
			2	मध्य विद्यालय, चैनपुर				
340	SSS-351	गोपालगंज	1	उत्क्रमित मध्य विद्यालय, मगहॉ	326.91	6.54	26,900.00	15 माह
			2	मध्य विद्यालय, माडीपुर				
			3	उत्क्रमित मध्य विद्यालय, संग्रामपुर गोपाल				
341	SSS-352	गोपालगंज	1	उत्क्रमित मध्य विद्यालय, मुडा मकसूदपुर	109.20	2.19	15,650.00	15 माह
342	SSS-353	गोपालगंज	1	उत्क्रमित मध्य विद्यालय, पिपरही	109.69	2.20	15,650.00	15 माह
343	SSS-354	गोपालगंज	1	मध्य विद्यालय, सुअरहॉ हंकारपुर	110.40	2.21	15,650.00	15 माह

नोट:-1. निविदाकार एक या अधिक ग्रुप में अलग-अलग निविदा डाल सकते हैं।

2. प्राक्कलित राशि घट या बढ़ सकती है एवं तदनुसार अग्रधन की राशि घट या बढ़ सकती है।

- (2) विज्ञापन निर्गत करने की तिथि :- दिनांक:- 12-12-2013
- (3) परिमाण विपत्र प्राप्त करने(डाउनलोड) की अवधि एवं समय :- दिनांक:- 20-12-2013 से 04-01-2014 15:00 घंटा
(वेबसाइट: www.eproc.bihar.gov.in पर)
- (4) प्री बिड मीटिंग का समय, स्थान एवं तिथि :- दिनांक:- 24.12.2013 14:30 घंटा प्रबंध निदेशक का कार्यालय,
बिहार राज्य शैक्षणिक आधारभूत संरचना विकास निगम, पटना।
- (5) निविदा प्राप्ति(अपलोड) की अंतिम तिथि एवं समय :- दिनांक:- 06-01-2014 समय-15:00 घंटा
- (6) टेक्निकल बिड खोलने की तिथि एवं समय :- दिनांक:- 08-01-2014 समय- 16:30 घंटा
(वेबसाइट:- www.eproc.bihar.gov.in पर)
- (7) वित्तीय बिड खोलने की तिथि एवं समय :- दिनांक:- 18-01-2014 समय- 16:00 घंटा

(Seal & Signature of Tenderer)

उजियुमर सिंह

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

- (8) निविदा खोलने का स्थान :— वेबसाइट—www.eproc.bihar.gov.in पर
- (9) निविदा की वैधता की अवधि :— 120 दिन
- (10) ई-टेन्डरिंग की प्रक्रिया में भाग लेने हेतु संवेदकों को पंजीकृत होना होगा, जिससे कि उन्हें उपयोगकर्ता का नाम (user ID) पासवर्ड (Password) अंकीय हस्ताक्षर (Digital Signature) निर्गत की जायेगी। यह उन्हें वेबसाइट www.eproc.bihar.gov.in से डाउनलोड करने/टेन्डर की प्रक्रिया में भाग लेने की योग्यता प्रदान करेगा।
- (11) ई-निविदा पत्र वेबसाइट www.eproc.bihar.gov.in से प्राप्त किया जा सकता है। संवेदक द्वारा सिर्फ उपर्युक्त वेबसाइट से ही परिमाण विपत्र प्राप्त करने के उपरांत वेबसाइट पर ही इलेक्ट्रॉनिक निविदा पत्र को भरकर भेजना है। अन्य सभी महत्वपूर्ण कागजात/बैंक ड्राफ्ट/अग्रधन की राशि/सभी प्रमाण पत्र जो निविदा के लिए आवश्यक है को स्कैन कर ई-निविदा के साथ संलग्न करना अनिवार्य है।
- (12) परिमाण विपत्र के दर से कम दर उद्धृत करने पर बीड डाक्यूमेंट की शर्तों एवं सरकारी निर्णयानुसार अतिरिक्त Performance Guarantee एकरारनामा के पूर्व जमा करना होगा।
- (13) (क) प्रत्येक परिमाण विपत्र का मूल्य जो प्रत्येक निविदा के सामने उपर कण्डिका (1) में अंकित है (जो लौटाया नहीं जाएगा) किसी भी राष्ट्रीयकृत बैंक द्वारा निर्गत एवं BIHAR STATE EDUCATIONAL INFRASTRUCTURE DEVELOPMENT CORPORATION LTD. के नाम से एवं पटना में भुगतये हो, स्वीकार किया जायेगा। मूल बैंक ड्राफ्ट "बिहार राज्य शैक्षणिक आधारभूत संरचना विकास निगम लिमिटेड" पटना के कार्यालय में दिनांक 08-01-2014 के 16:00 घंटे तक स्वयं/निबंधित डाक /स्पीड पोस्ट द्वारा निश्चित रूप से जमा किया जाना है। ऐसा नहीं करने पर निविदा मान्य नहीं होगा।
- (ख) वांछित अग्रधन की राशि राष्ट्रीय बचत पत्र/डाकघर सावधि जमा 3 वर्षीय या 5 वर्षीय पासबुक जो बिहार राज्य से क्रय या जमा किया हो, प्रबंध निदेशक, BSEIDC Ltd., पटना के नाम प्रतिज्ञित (Pledged) हो अथवा बिहार वित्त नियमावली के अनुसार BSEIDC Ltd. के नाम से पटना में भुगतये एकाउन्ट पेयी डिमाण्ड ड्राफ्ट, फिक्सड डिपोजिट रिसिप्ट, बैकर्स चेक अथवा बैंक गारन्टी जो बिड के मान्य अवधि तक के लिए बिहार अवस्थित किसी राष्ट्रीयकृत/अनुसूचित बैंक से निर्गत हो (अगर बिहार प्रान्त के बाहर के बैंक से निर्गत बैंक गारन्टी दिया जाता है तो एकरारनामा के पूर्व इसे बिहार अवस्थित किसी बैंक से निर्गत किया जाना होगा) के रूप में प्रबंध निदेशक का कार्यालय, बिहार राज्य शैक्षणिक आधारभूत संरचना विकास निगम लिमिटेड, पटना में दिनांक 08-01-2014 के 16:00 घंटे तक स्वयं/निबंधित डाक /स्पीड पोस्ट द्वारा निश्चित रूप से जमा किया जाना आवश्यक है। ऐसा नहीं करने पर निविदा मान्य नहीं होगा।
- (14) निविदाकारों द्वारा इस्तेमाल किये जा रहे इन्टरनेट सर्विस में किसी प्रकार का व्यवधान उत्पन्न होने पर कोई भी दावा मान्य नहीं होगा। निविदाकारों को सलाह दी जाती है कि अपने निविदा को समय रहते उपर्युक्त वेबसाइट पर अपलोड कर लें। ताकि अंतिम समय में होनेवाले किसी प्रकार के व्यवधान से बच सकें।
- (15) किसी भी प्रकार की जानकारी अथवा शुद्धि पत्र को वेबसाइट www.eproc.bihar.gov.in पर प्रकाशित किया जायेगा। बिना कारण बताये निविदा या उसके अंश को अस्वीकृत करने/रद्द करने का अधिकार सक्षम पदाधिकारी को सुरक्षित है।
- (16) विशेष जानकारी हेतु अधोहस्ताक्षरी के कार्यालय में कार्य अवधि में सम्पर्क किया जा सकता है। ई-टेन्डरिंग की प्रक्रिया से संबंधित किसी भी प्रकार की जानकारी/सूचना हेतु सहायता कक्ष, ई-टेन्डरिंग कक्ष, प्रथम तल्ला, M/22, बैंक ऑफ इण्डिया भवन, रोड नं० 25, श्री कृष्णा नगर, पटना-800001, दूरभाष सं०, 0612-2523006/9939035696.

प्रबंध निदेशक

(Seal & Signature of Tenderer)


अजय कुमार सिंह

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

Rr

SECTION 1
INSTRUCTION TO BIDDERS
(ITB)


Seal and Signature of Tenderer


Official Stamp
B.S.E.I.D.C. Ltd, Patna
Pmk.

Section 1 : Instructions to Bidders

Table of Contents

Page No.					
A.	General	Page No	D	Submission of Bids	Page No
	1. Scope of Bid	10		19. Sealing and Marking of Bids	17
	2. Source of Funds	10		20. Deadline for Submission of Bids	18
	3. Eligible Bidders	10		21. Late Bids	18
	4. Qualification of the Bidder	10	E	Bid Opening and Evaluation	
	5. One Bid per Bidder	13		22. Bid Opening	18
	6. Cost of Bidding	13		23. Process to be Confidential	19
	7. Site Visit	13		24. Clarification of Financial Bids	19
B.	Bidding Documents	14		25. Examination of Bids and Determination of Responsiveness	19
	8. Content of Bidding Documents	14		26. Correction of Errors	19
	9. Clarifications of Bidding Documents	14		27. Evaluation and Comparison of Financial Bids	20
	10. Amendment of Bidding Documents	14	F.	Award of Contract	
C.	Preparation of Bids			28. Award Criteria	20
	11. Language of Bid	15		29. Employer's Right to Accept any Bid and to Reject any or all Bids	20
	12. Documents Comprising the Bid	15		30. Notification of Award and Signing of Agreement	20
	13. Bid Prices	15		31. Performance Security	21
	14. Currencies of Bid and Payment	16		32. Advance Payment and Security	21
	15. Bid Validity	16		33. Corrupt or Fraudulent Practices	21
	16. Bid Security	16	G.	Appendix to I TB	22
	17. Alternative Proposals by Bidders	17	H.	Annexure – I	24
	18. Format and Signing of Bid	17		Annexure - II	25

[Signature]
Seal and Signature of Tenderer

[Signature]
25-6-2014
Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Pmt

GENERAL

1. Scope of Bid

- 1.1 The Employer (named in Appendix to ITB) invites bids for the construction of works (as defined in these documents and referred to as "the works") detailed in the table given in IFB. The bidders may submit bids for any or all of the works detailed in the table given in IFB.
- 1.2 The successful bidder will be expected to complete the works by the intended completion date specified in the Contract data.
- 1.3 Throughout these bidding documents, the terms 'bid' and 'tender' and their derivatives (bidder / tenderer, bid/tender, bidding/tendering, etc.) are synonymous.
- 1.4 **Administrative authority shall decide that this agreement would be either PERCENTAGE RATE OR ITEM RATE and accordingly the non-relevant sections of this document must be crossed.**

2. Sources of Funds

- 2.1 The expenditure on this project will be met as decided by the Competent Authority.


3. Eligible Bidders

- 3.1 This *Invitation for Bids* is open to all bidders.
- 3.2 All bidders shall provide in Section 2, Forms of Bid and Qualification Information, a statement that the Bidder is neither associated, nor has been associated, directly or indirectly, with the Consultant; Engineer-in-Charge or any other entity that has prepared the design, specifications, and other documents for the Project or being proposed as Project Manager for the Contract or involved in supervision of the contract. A firm that has been engaged by the Employer to provide consulting services for the preparation or supervision of the works, and any of its affiliates shall not be eligible to bid.
- 3.3 Bidders shall not be under a declaration of ineligibility for delay, failure or corrupt and fraudulent practices by any of the State Govt. or Central Govt. or Public Undertaking or any Autonomous Body.

4. Qualification of the Bidder

- 4.1 All bidders shall provide in Section 2, Forms of Bid and Qualification Information, a preliminary description of the proposed work method and schedule, including drawings and charts indicating miles stones to complete the project on time.
- 4.2 All bidders shall also furnish the following information in Section 2:
 - (i) Evidence of access to or availability of credit facilities (minimum 10% of estimated cost) certified by the bankers.
 - (ii) Undertaking that bidder would be able to invest a minimum of cost upto 25% of the contract value of work, during implementation of contract.
 - (iii) Proposals, if any, for sub contracting of elements of work, costing more than 10% of the bid amount. (for all contracts over Rs. 5 crore)
 - (iv) Power of attorney, if any.
- 4.3 If the Employer has not undertaken prequalification of potential bidders, all bidders shall include the following information and documents with their bids in Section 2:
 - (a) copies of original documents defining the constitution or legal status, place of registration, and principal place of business; written power of attorney of the signatory of the Bid to commit the Bidder;
 - (b) total monetary value of construction work performed for each of the last five years;
 - (c) experience in works of a similar nature and size for each of the last five years, and details of works underway or contractually committed; and clients who may be contacted for further information on those contracts;
 - (d) major items of construction equipment proposed to carry out the Contract or evidence of arrangement; of possessing them on hire/ lease/ buying as defined therein;
 - (e) qualifications and experience of key site management and technical personnel proposed for contract;
 - (f) reports on the financial standing of the Bidder, such as profit and loss statements and auditor's reports for the past five years;


Seal and Signature of Tenderer


Chief Engineer
BSEIDC, Ltd, Patna
PMB

- (g) evidence of access to line(s) of credit and availability of other financial resources facilities (10% of contract value), certified by the Bankers (Not more than 3 months old)
- (h) undertaking that the bidder will be able to invest a minimum cash up to 25% of contract value of work, during implementation of work.
- (i) authority to seek references from the Bidder's bankers;
- (j) information regarding any litigation, current or during the last five years, in which the Bidder is involved, the parties concerned and dispute amount;
- (k) proposals for subcontracting components of the Works amounting to more than 10% of the Bid Price (for each, the qualifications and experience of the identified sub-contractor in the relevant field should be annexed); *(for all contracts over Rs. 5 Crore)*
- (l) the proposed methodology and programme of construction, backed with equipment planning and deployment, duly supported with broad calculations and quality control procedures proposed to be adopted, justifying their capability of execution and completion of the work as per technical specifications within the stipulated period of completion as per milestones *(for all contracts over Rs. 5 Crore)*


4.4 Bids from Joint ventures are not acceptable.*

- 4.5** (A) A.To qualify for award of the contract, each bidder in its name should have in the last five years and current financial year will also be considered as referred to in Appendix :-
- (a) Achieved in any one year a minimum annual financial turnover (in all classes of civil engineering construction works only) volume of construction work of at least the amount equal to the 50 % (fifty percent) estimated cost of works for which bid has been invited. The turn over will be indexed at the rate of 8% for a year.
- (b) Satisfactorily completed as a prime contractor (or as a nominated subcontractor, where the subcontract involved execution of all main items of work described in the bid document, provided further that all other qualification criteria are satisfied) at least one similar work of value not less than amount indicated in Appendix *(usually not less than 25% (twenty five percent) of estimated value of contract)*;
- (c) executed in any one year, the minimum quantities of the following items of work as indicated in Appendix.
- | | |
|-----------------------|------------|
| - R.C.C. and P.C.C. | 393.00 cum |
| - Brick work quantity | 334.00 cum |

(usually 50% of the expected peak rate of construction)

* To be deleted for projects costing Rs. 10 crores or more

** Also, see section 5, the special condition of contract


Seal and Signature of Tenderer


Chief Engineer
B.S.E.I.D.C. Ltd, Patna

B. Each bidder should further demonstrate :

- (a) availability (either owned or leased or by procurement against mobilization advances) of the following key and critical equipment for this work:

Based on the studies, carried out by the Engineer the minimum suggested major equipment to attain the completion of works in accordance with the prescribed construction schedule are shown in the Annexure-I.

Availability of the testing equipment required for establishing field laboratory to perform mandatory tests e.g. those stated in Appendix to ITB.

The bidders should, however, undertake their own studies and furnish with their bid, a detailed construction planning and methodology supported with layout and necessary drawings and calculations (detailed) as stated in clause 4.3(1) above to allow the employer to review their proposals. The numbers, types and capacities of each plant/equipment shall be shown in the proposals along with the cycle time for each operation for the given production capacity to match the requirements.

NOTE : (To be included for bids valued over Rs 5 Crore)

- (b) availability for this work of personnel with adequate experience as required; as per Annexure-II.
- (c) liquid assets and/or availability of credit facilities of no less than amount indicated in Appendix
(Credit lines/letter of credit/certificates from Banks for meeting the funds requirement etc.- usually the equivalent of the estimated cash flow for 3 months in peak construction period.)
- C. To qualify for a package of contracts made up of this and other contracts for which bids are invited in the IFB, the bidder must demonstrate having experience and resources sufficient to meet the aggregate of the qualifying criteria for the individual contracts.**

- 4.6 Sub-contractors' experience and resources shall not be taken into account in determining the bidder's compliance with the qualifying criteria except to the extent stated in 4.5(A) above.

- 4.7 Bidders who meet the minimum qualification criteria will be qualified only if their available bid capacity is more than the total bid value. The available bid capacity will be calculated as under :

$$\text{Assessed Available Bid capacity} = (A * N * 3 - B)$$

Where

A = Maximum value of civil engineering works executed in any one year during the last five years (updated to the price level of the year indicated in Appendix) taking into account the completed as well as works in progress.

N = Number of years prescribed for completion of the works for which bids are invited.

B = Value (updated to the price level of the year indicated in Appendix) of existing commitments and on-going works to be completed during the next..... years (period of completion of the works for which bids are invited)

Note : The statements showing the value of existing commitments and on-going works as well as the stipulated period of completion remaining for each of the works listed should be countersigned by the Engineer in charge, not below the rank of an Executive Engineer or equivalent.

- 4.8 Even though the bidders meet the above qualifying criteria, they are subject to be disqualified if they have:

- made misleading or false representations in the forms, statements and attachments submitted in proof of the qualification requirements; and/or


Seal and Signature of Tenderer


Chief Engineer
B.S.E.I.D.C. Ltd, Patna
B&S

- have record of poor performance such as abandoning the works, not properly completing the contract, inordinate delays in completion, litigation history, or financial failures etc; and/or

- participated in the previous bidding for the same work and had quoted unreasonably high bid prices and could not furnish rational justification to the employer.

5. One Bid per Bidder

- 5.1 Each bidder shall submit only one bid for any work or one package or group. A bidder who submits or participates in more than one Bid (other than as a subcontractor or in cases of alternatives that have been permitted or requested) will cause all the proposals with the Bidder's participation to be disqualified.

6. Cost of Bidding

- 6.1 The bidder shall bear all costs associated with the preparation and submission of his Bid, and the Employer will in no case be responsible and liable for those costs.

In case of cancellation of tender, cost of bidding document will be charged each times.

7. Site Visit

- 7.1 The Bidder, at the Bidder's own responsibility and risk must visit and examine the Site of Works and its surroundings and obtain all information that may be necessary for preparing the Bid and entering into a contract for construction of the Works. The costs of visiting the Site shall be at the Bidder's own expense.

- 7.2 Tender documents are not transferable.


Seal and Signature of Tenderer


Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Pmt

B.BIDDING DOCUMENTS

8. Content of Bidding Documents

8.1 The set of bidding documents comprises the documents listed below and addenda issued in accordance with Clause 10;

Section	Particulars	Volume No.
	Invitation for Bids	
1	Instructions to Bidders	I
2	Qualifications of Bidders	
3	Conditions of Contracts	
4	Contract Data	
5	Special condition of Contract	II
6	Technical Specifications	III
7	Bill of Quantities	
8	Securities and other forms	
9	Drawings	IV
10	Documents to be furnished by bidder	V

8.2 One copy of each of the volumes I, II, III and IV will be issued to the bidder Documents to be furnished by the bidder in compliance to section 2 will be prepared by him and furnished as Volume- V in two parts (refer clause 12).

8.3 The bidder is expected to examine carefully all instructions, conditions of contract, contract data, forms, terms, technical specifications, bill of quantities, forms, Annexes and drawings in the Bid Document. Failure to comply with the requirements of Bid Documents shall be at the bidder's own risk. Pursuant to clause 25 hereof, bids which are not substantially responsive to the requirements of the Bid Documents shall be rejected.

9.1 Pre-bid meeting

9.1.1 The bidder or his official representative is invited to attend a pre-bid meeting which will take place at the address, venue, time and date as indicated in appendix.

9.1.2 The purpose of the meeting will be to clarify issues and to answer questions on any matter that may be raised at that stage.

9.1.3 The bidder is requested to submit any questions in writing or by fax to reach the Employer not later than one week before the meeting.


9.1.4 Minutes of the meeting, including the text of the questions raised (without identifying the source of enquiry) and the responses given will be transmitted without delay to all purchasers of the bidding documents. Any modification of the bidding documents listed in Sub-Clause 8.1 which may become necessary as a result of the pre-bid meeting shall be made the Employer exclusively through the issue of an Addendum pursuant to Clause 10 and not through the minutes of the pre-bid meeting. All bidders have to collect any addendum on next working day of pre-bid meeting. The bidder shall receive the minutes of the meeting on the next working day of the pre-bid meeting.

9.1.5 Non-attendance at the pre-bid meeting will not be a cause for disqualification of a bidder.

10. Amendment of Bidding Documents

Seal and Signature of Tenderer




Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Rmb

- 10.1 Before the deadline for submission of bids, the Employer may modify the bidding documents by issuing addendum.
- 10.2 Any addendum thus issued shall be part of the bidding documents and shall be collected by all the purchasers of the bidding documents. Prospective bidders shall acknowledge receipt of each addendum in writing or by cable to the Employer. The Employer will assume no responsibility for postal delays.
- 10.3 To give prospective bidders reasonable time in which to take an addendum into account in preparing their bids, the Employer may, at his discretion, extend as necessary the deadline for submission of bids, in accordance with Sub-Clause 20.2 below.

C. PREPARATION OF BIDS

11. Language of the Bid

- 11.1 All documents relating to the bid shall be in English / Hindi.

12. Documents Comprising the Bid

- 12.1 The bid to be submitted by the bidder as Volume V of the bid document (refer Clause 8.1) shall be in two separate parts;

Part I shall be named "Technical Bid" and shall comprise

- (i) Earnest money in the form specified in Section 8
- (ii) Qualification Information and supporting documents as specified in Section- 2
- (iii) Certificates, undertakings, affidavits as specified in Section 2
- (iv) Any other information pursuant to Clause 4.2 of these instructions
- (v) Undertaking that the bid shall remain valid for the period specified in Clause 15.1
- (vi) An affidavit affirming the information he has furnished in the bidding document is correct to the best of his knowledge and belief.

Part II shall be named "Financial Bid" and shall comprise



- (i) Form of Bid as specified in Section 6
 - (ii) Priced Bill of Quantities for items specified in Section 7
- 12.2 Each part will be separately sealed and marked in accordance with the Sealing and Marking Instructions in Clause 19.
- 12.3 Following documents, which are not submitted with the bid, will be deemed to be part of the bid.

Section	Particulars	Volume No.
	Invitation for Bids (IFB)	
1	Instructions to Bidders	Volume I
3	Conditions of Contract	
4	Contract Data	
5	Specifications	Volume II
8	Drawings	Volume IV

13. Bid Prices


Seal and Signature of Tenderer:




Chief Engineer
B.S.E.I.D.C. Ltd, Patna


- 13.1 The contractor shall bid for the whole work as described in Sub-Clause 1.1 based on the priced Bill of Quantities submitted by the Bidder.
- 13.1.1 The bidder shall adopt the percentage rate method or item rate method as specified in the appendix to ITB; only the same option is allowed to all the bidders. Percentage rate method requires the bidder to quote a percentage above/below/ at par of the schedule of rates specified in the appendix to ITB.
- Item rate method requires to quote rates and prices and line item total (both in figures and words) for all items of the Works described in the Bill of Quantities along with total bid price both in figures and words). *Items for which no rate or price is entered by the bidder will not be paid for by the Employer when executed and shall be deemed covered by the other rates and prices in the Bill of Quantities.* Corrections, if any, shall be made by crossing out, initialing, dating and rewriting.
- 13.1.2 All duties, taxes, and other levies payable by the contractor under the contract or for any other cause shall be included in the rates, prices and total Bid Price submitted by the Bidder.
- 13.2 The rates and prices quoted by the bidder are subject to adjustment during the performance of the Contract in accordance with the provisions clause 10CA & 10CC clause Conditions of Contract.
- 13.3 The rate should include the cost of all seen and unseen expenditure. No claim, whatsoever, will be entertained due to non-inclusion of any such event necessary for the completion of the item of work.
- 14. Currencies of Bid and Payment**
- 14.1 The units rates and the prices shall be quoted by the bidder entirely in Indian Rupees. All payments shall be made in Indian Rupees.
- 15. Bid Validity**
- 15.1 Bids shall remain valid for a period not less than 120 days after the deadline date for bid submission specified in Clause 20.A bid valid for a shorter period shall be rejected by the Employer as non-responsive. In case of discrepancy in bid validity period between that given in the undertaking pursuant to Clause 12.1 (v) and the Form of Bid submitted by the bidder, the latter shall be deemed to stand corrected in accordance with the former and the bidder has to provide for any additional security that is required.
- 15.2 In exceptional circumstances, prior to expiry of the original time limit, the Employer may request that the bidders may extend the period of validity for a specified additional period. The request and the bidders' responses shall be made in writing or by cable. A bidder may refuse the request without forfeiting his bid security. A bidder agreeing to the request will not be required or permitted to modify his bid.
- 16. Earnest Money**
- 16.1 The Bidder shall furnish, as part of his Bid, a Bid security in the amount as shown in column 4 of the table of IFB for this particular work. This bid security shall be in favour of Employer, and shall be in the following form of Unconditional bank guarantee from any nationalized scheduled Indian bank issued within the state in the format given in Vol. III (If issued from any bank outside state it will have to be converted to any bank within the state before executing the agreement).
- 16.2 Unconditional bank guarantees issued as surety for the bid shall be valid for 45 days beyond the validity of the bid.
- 16.3 Any bid not accompanied by an acceptable Bid Security and not secured as indicated in Sub-Clauses 16.1 and 16.2 above shall be rejected by the Employer as non-responsive.
- 16.4 The Earnest money of unsuccessful bidders will be returned within 28 days of the end of the bid validity period specified in Sub-Clause 15.1.
- 16.5 The Earnest money of the successful bidder will be discharged when the bidder has signed the Agreement and furnished the required Performance Security.
- 16.6 The Earnest money may be forfeited
- (a) if the Bidder withdraws the Bid after Bid opening during the period of Bid validity;
- (b) if the Bidder does not accept the correction of the Bid Price, pursuant to Clause 26; or
- (c) in the case of a successful Bidder, if the Bidder fails within the specified time limit to

Seal and Signature of Tenderer




Ch. ...
B.S.E.I.D.C. Ltd, Patna
Rmt

- (i) sign the Agreement; or
- (ii) furnish the required Performance Security.

17. Alternative Proposals by Bidder

- 17.1 Bidders shall submit offers that fully comply with the requirements of the bidding documents, including the conditions of contract (including mobilisation advance or time for completion), basic technical design as indicated in the drawing and specifications. Conditional offer or alternative offers will not be considered further in the process of tender evaluation.
- 17.2 Conditional tender will be rejected forthwith.

18. Format and Signing of Bid

- 18.1 The Bidder shall submit one set of the Technical bid and two set of Financial bid (original & duplicate) comprising of the documents as described in clause 12 of ITB.
- 18.2 The Bid shall be typed or written in indelible ink and shall be signed by a person or persons duly authorized to sign on behalf of the Bidder, pursuant to Sub-Clause 4.3. All pages of the bid where entries or amendments have been made shall be initialed by the person or persons signing the bid and a certificate of corrections must be given by the employer.
- 18.3 The Bid shall contain no alterations or additions, except those to comply with instructions issued by the Employer, or as necessary to correct errors made by the bidder, in which case such corrections shall be initialed by the person or persons signing the bid.

D. SUBMISSION OF BIDS (Only on Website : www.eproc.bihar.gov.in)

(SI.No. 19 To 21.1, All Process shall be done through e-tendering Process)

19. Sealing and Marking of Bids.

- 19.1 The Bidder shall place three separate envelopes (called as inner envelopes) which shall be marked one as technical bid and two envelope as Financial bid in duplicate. Inside one outer envelope. The envelopes marked "Technical Bid" and "Financial Bid" will have additional markings as follows.

- Technical Bid : To be opened as per NIT (date of Technical Bid opening) in the presence of Evaluation Committee, or authorized person. (Only on Website : www.eproc.bihar.gov.in)
- Financial Bid: Not to be opened except with the approval of Evaluation Committee. (Only on Website : www.eproc.bihar.gov.in)


The contents of Technical and Financial Bids will be as specified in clause 12.1

- 19.2 The inner, outer and separate envelopes containing Technical and Financial Bids shall
- (a) be addressed to the Employer at the address given in Appendix
 - (b) bear the identification no of contract as indicated in Appendix.
 - (c) provide a warning not to open before the specified time and date for bid opening as specified in ITB.
- 19.3 In addition to the identification required in Sub-Clause 19.1 and 19.2, each of the envelopes shall indicate the name and address of the bidder to enable the bid to be returned unopened in case it is declared late, pursuant to Clause 21, or if Evaluation Committee declares the bid as non responsive pursuant to Clause 23.
- 19.4 If the outer envelope is not sealed and marked as above, the Employer will assume no responsibility for the misplacement or premature opening of the bid.

Seal and Signature of Tenderer



25-6-2014


Chief Engineer
B.S.E.I.D.C. Ltd, Patna


20. **Deadline for Submission of the Bids(Only on Website : www.eproc.bihar.gov.in)**
- 20.1 Complete Bids (including Technical and Financial) must be received by the Employer at the address specified above not later than the date indicated in appendix. In the event of the specified date for the submission of bids have declared a holiday for the Employer, the Bids will be received up to the appointed time on the next working day.
- 20.2 The Employer may extend the deadline for submission of bids by issuing an amendment in accordance with Clause 10, in which case all rights and obligations of the Employer and the bidders previously subject to the original deadline will then be subject to the new deadline.
21. **Late Bids**
- 21.1 Any Bid received by the Employer after the deadline prescribed in Clause 20 will be returned unopened to the bidder.

E. BID OPENING AND EVALUATION (Only on Website : www.eproc.bihar.gov.in)
(Sl.No. 22 To 27.5, All Process shall be done through e-tendering Process)

22. **Bid Opening**
- 22.1 The Employer or their authorized representative will open all the Bids received (except those received late), in the presence of the Bidders or their representatives who choose to attend at time, date and the place specified in Appendix in the manner specified in Clause 20 and 22.3. In the event of the specified date of Bid opening being declared a holiday for the Employer, the Bids will be opened at the appointed time and location on the next working day. Even in the case of absence of the bidder at the time of opening of bids, department will proceed a head with the opening.
- 22.2 If any of the tenderers or their agents are not present at the time of opening, the employer will open the tender in their absence and prepare a statement and that will be binding on the absent tenderers.
- 22.3 The envelope containing "Technical Bid" shall be opened. The amount, form and validity of the Earnest money furnished with each bid will be announced. If the bid security furnished does not conform to the amount and validity period as specified in the Invitation for Bid (ref. Column 4 and paragraph 3), and has not been furnished in the form specified in Clause 16, the remaining technical bid and the sealed financial bid will be returned to the bidder.
- 22.4 (i) Subject to confirmation of the bid security by the issuing Bank, the bids accompanied with valid security will be taken up for evaluation with respect to the Qualification Information and other information furnished in Part I of the bid pursuant to Clause 12.1.
- (ii) After receipt of confirmation of the bid security, the bidder will be asked in writing (usually within 10 days of opening of the Technical Bid) to clarify or modify his technical bid, if necessary, with respect to any rectifiable defects.
- (iii) The bidders will respond in not more than 7 days of issue of the clarification letter.
- (iv) Immediately (usually within 3 to 4 days), on receipt of these clarifications the Evaluation Committee will finalize the list of responsive bidders whose financial bids are eligible for consideration.
- 22.5 At the time of opening of "Financial Bid", the names of the bidders found responsive in accordance with Clause 23.4(iv) will be announced. The bids of only these bidders will be opened. The remaining bids will be returned to the bidders unopened. The responsive Bidders' names, the Bid prices, the total amount of each bid, any discounts, Bid Modifications and withdrawals, and such other details as the Employer may consider appropriate, will be announced by the Employer at the opening. Any Bid price or discount, which is not read out and recorded will not be taken into account in Bid Evaluation.
- 22.6 In case bids are invited in more than one package, the order for opening of the "Financial Bid" shall be that in which they appear in the "Invitation For Bid".

Seal and Signature of Tenderer





34

Chief Engineer
BSEIDC, Ltd, Patna



- 22.7 The Employer shall prepare minutes of the Bid opening, including the information disclosed to those present in accordance with Sub-Clause 22.5
- 23. Process to be Confidential**
- 23.1 Information relating to the examination, clarification, evaluation and comparison of Bids and recommendations for the award of a contract shall not be disclosed to Bidders or any other persons not officially concerned with such process until the award to the successful Bidder has been announced. Any effort by a Bidder to influence the Employer's processing of Bids or award decisions may result in the rejection of his Bid.
- 24. Clarification of Financial Bids**
- 24.1 To assist in the examination, evaluation and comparison of Bids, the Employer may, at his discretion, ask any Bidder for clarification of his Bid, including breakdowns of unit rates. The request for clarification and the response shall be sought, offered or permitted except as required to confirm the correction of arithmetic errors discovered by the Employer in the evaluation of the Bids in accordance with Clause 26.
- 24.2 Subject to sub-clause 24.1, no Bidder shall contact the Employer on any matter relating to his bid from the time of the bid opening to the time the contract is awarded. If the Bidder wishes to bring additional information to the notice of the Employer, it should do so in writing.
- 24.3 Any effort by the Bidder to influence the Employer in the Employer's bid evaluation, bid comparison or contract award decisions may result in the rejection of the Bidders' bid.
- 25. Examination of Bids and Determination of Responsiveness**
- 25.1 During detailed evaluation of "Technical Bids", the Employer will determine whether each Bid (a) meets the eligibility criteria defined in Clause 3 and 4; (b) has been properly signed; (c) is accompanied by the required securities and; (d) is substantially responsive to the requirements of the Bidding documents. During the detailed evaluation of the "Financial Bid", the responsiveness of the bids will be further determined with respect to the remaining bid conditions, i.e., priced bill of quantities, technical specifications, and drawings.
- 25.2 A substantially responsive "Financial Bid" is one which conforms to all the terms, conditions and specifications of the Bidding documents, without material deviation or reservation. A material deviation or reservation is one (a) which affects in any substantial way the scope, quality or performance of the Works; (b) which limits in any substantial way, inconsistent with the Bidding documents, the Employer's rights or the Bidder's obligations under the Contract; or (c) whose rectification would affect unfairly the competitive position of other Bidders presenting substantially responsive Bids.
- 25.3 If a "Financial Bid" is not substantially responsive, it will be rejected by the Employer, and may not subsequently be made responsive by correction or withdrawal of the non-conforming deviation or reservation.
- 26. Correction of Errors**
- 26.1 "Financial Bids" determined to be substantially responsive will be checked by the Employer for any arithmetic errors. Errors will be corrected by the Employer as follows:
- (a) where there is a discrepancy between the rates in figures and in words, the rate in words will govern; and
- (b) where there is a discrepancy between the unit rate and the line item total resulting from multiplying the unit rate by the quantity, the unit rate as quoted will govern.
- 26.2 The amount stated in the "Financial Bid" will be corrected by the Employer in accordance with the above procedure and the bid amount adjusted with the concurrence of the Bidder in the following manner:
- (a) If the Bid price increases as a result of these corrections, the amount as stated in the bid will be the 'bid price' and the increase will be treated as rebate;
- (b) If the bid price decreases as a result of the corrections, the decreased amount will be treated as the 'bid price'

Seal and Signature of Tenderer



35


Chief Engineer
B.S.E.I.D.C. Ltd, Patna.

For

Such adjusted bid price shall be considered as binding upon the Bidder. If the Bidder does not accept the corrected amount the Bid will be rejected, and the Earnest money may be forfeited in accordance with Sub-Clause 16.6(b).

27. Evaluation and Comparison of Financial Bids

- 27.1** The Employer will evaluate and compare only the Bids determined to be substantially responsive in accordance with Sub-Clause 25.2.
- 27.2** In evaluating the Bids, the Employer will determine for each Bid the evaluated Bid Price by adjusting the Bid Price as follows:
- (a) making any correction for errors pursuant to Clause 26; or
 - (b) making an appropriate adjustments for any other acceptable variations, deviations.
- 27.3** The Employer reserves the right to accept or reject any variation or deviation. Variations and deviations and other factors, which are in excess of the requirements of the Bidding documents or otherwise result in unsolicited benefits for the Employer shall not be taken into account in Bid evaluation.
- 27.4** If the Bid of the successful Bidder is seriously unbalanced in relation to the Engineer's estimate of the cost of work to be performed under the contract, the Employer may require the Bidder to produce detailed price analyses for any or all items of the Bill of Quantities, to demonstrate the internal consistency of those prices with the construction methods and schedule proposed. After evaluation of the price analyses, the Employer may require that the amount of the performance security set forth in Clause 31 be increased at the expense of the successful Bidder to a level sufficient to protect the Employer against financial loss in the event of default of the successful Bidder under the Contract.
- 27.5** A bid, in the opinion of employee which contains several items in the Bill of Quantities which are unrealistically priced low and which cannot be substantiated satisfactorily by the bidder, may be rejected as non-responsive.

F. AWARD OF CONTRACT

28. Award Criteria

- 28.1** Subject to Clause 29, the Employer will award the Contract to the Bidder whose Bid has been determined
- (i) to be substantially responsive to the Bidding documents and who has offered the lowest evaluated Bid Price; and
 - (ii) to be within the available bid capacity adjusted to account for his bid price which is evaluated the lowest in any of the packages opened earlier than the one under consideration.

In no case, the contract shall be awarded to any bidder whose available bid capacity is less than the evaluated bid price, even if the said bid is the lowest evaluated bid. The contract will in such cases be awarded to the next lowest bidder at his evaluated bid price.

29. Employer's Right to Accept any Bid and to Reject any or all Bids


Notwithstanding Clause 28, the Employer reserves the right to accept or reject any Bid, and to cancel the Bidding process and reject all Bids, at any time prior to the award of Contract, without thereby incurring any liability to the affected Bidder or Bidders or any obligation to inform the affected Bidder or Bidders of the ground for the Employer's action.

30. Notification of Award and Signing of Agreement

- 30.1** The Bidder whose Bid has been accepted will be notified of the award by the Employer prior to expiration of the Bid validity period by cable, telex or facsimile confirmed by registered letter. This letter (hereinafter and in the *General Conditions of Contract* called the "Letter of Acceptance") will state the sum that the Employer will pay the Contractor in consideration of the execution, completion and maintenance of the Works by the Contractor as prescribed by the Contract (hereinafter and in the Contract called the "Contract Price").

Seal and Signature of Tenderer





Chief Engineer
B.S.E.I.D.C. Ltd, Patna


- 30.2 The notification of award will constitute the formation of the Contract, subject only to the furnishing of the performance security in accordance with the provisions of Clause 31.
- 30.3 The Agreement will incorporate all agreements between the Employer and the successful Bidder. It will be signed by the Employer and the successful Bidder, after the performance security is furnished.
- 31. Performance Security**
- 31.1 Within 10 (ten) days of receipt of the Letter of Acceptance, the successful Bidder shall deliver to the Employer a Performance Security in any of the forms given below for an amount equivalent 2% of the Contract price including earnest money plus additional security for unbalanced Bids in accordance with the Clause 29.5 of ITB and the provisions of Bihar Financial Rules.
- 31.2 If the performance security is provided by the successful Bidder in the form of an Bank Guarantee or fixed deposit receipts in the name of Employer, it shall be issued either (a) at the Bidder's option, by a Nationalized/ Scheduled Indian bank within state or (b) acceptable to the Employer.
- 31.3 Failure of the successful Bidder to comply with the requirements of Sub-Clause 31.1 shall constitute sufficient grounds for cancellation of the award and forfeiture of the Bid Security.
- 32. Advance Payment and Security**
- 32.1 The Employer will provide an Advance Payment on the Contract Price as stipulated in the General Conditions of Contract, subject to maximum amount, as stated in the Contract Data.
- 33. Corrupt or Fraudulent Practices**
- 33.1 The Employer will reject a proposal for award if it determines that the Bidder recommended for award has engaged in corrupt or fraudulent practices in competing for the contract in question and will declare the firm ineligible, either indefinitely or for a stated period of time, to be awarded a contract with this Corporation (BSEIDC) and any other agencies, if it at any time determines that the firm has engaged in corrupt or fraudulent practices in competing for the contractor, or in execution.
- 33.2 Furthermore, Bidders shall be aware of the provision stated in Sub-Clause and Sub-Clause 14 of the General Conditions of Contract.

Seal and Signature of Tenderer

[Handwritten Signature]

[Handwritten Signature]
25-6-2014
Chief Engineer
B.S.E.I.D.C. Ltd, Patna
[Handwritten Initials]

G. APPENDIX to ITB

Clause Reference with respect to Section-I.


1. Name of the Employer—Managing Director, BSEIDC, Patna. [Cl. 1.1]
2. The last five years means for this tender
2008 - 2009
2009 - 2010
2010 - 2011
2011 - 2012
2012 - 2013.
And financial year 2013-14 will also be considered.
3. The required annual financial turn over amount is Rs. 105.05 Lac (Rupees One Crore Five Lac Five Thousand Only) [Cl. 4.5 A(a)]
4. Required minimum value of one similar work is Rs. 52.53 Lac (Rupees Fifty Two Lac Fifty Three Thousand Only). [Cl. 4.5A(b)]
5. Required minimum quantities of work executed are:- as prescribed in the relevant clause. [Cl. 4.5A(c)]
6. The cost of electric work is :-
7. The cost of water supply/ sanitary works is :-
8. Liquid assets and/or availability of credit facilities is 10% of Estimated Cost. [Cl. 4.5B(c)]
9. Price level of the financial year _____ [Cl. 4.7)]
10. The pre-bid meeting will take place : As Per NIT. [Cl. 9.1.2]
11. The technical bid will be opened THROUGH WEBSITE Only
Website : www.eproc.bihar.gov.in


Seal and Signature of Tenderer


Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Rond

12. Address of the Employer : Managing Director, BSEIDC, Patna. [Cl. 4.5(a)]
13. Identification: [cl. 10.2(b)]
Bid for : Construction of Senior Secondary Schools in Bihar, Gr.No. :SSS-153
Bid reference No. : 36 , Year : 2013-14
Do not open before : As Per NIT
14. Bids may be submitted only in Percentage Rate Method.
15. Schedule of rate applicable for Percentage Rate Method is S.O.R., BCD, Effective from: 11.08.2013 & DSR (CIVIL&ELECTRICAL) 2012.
16. The bid should be submitted latest by Date : As Per NIT [Cl. 20.1(a)]
17. The bid will be opened through Web Site : [Cl. 23.1]
[/www.eproc.bihar.gov.in](http://www.eproc.bihar.gov.in)
18. The Cost of BOQ & Cost of Earnest money : As Per NIT. [Cl. 14.1]
19. Escalation factors (for the cost of works executed and financial figure to a common base value for works completed)
Year before Multiply factor
- | | |
|-------|------|
| One | 1.1 |
| Two. | 1.21 |
| Three | 1.33 |
| Four | 1.46 |
| Five | 1.61 |
20. Bids will be submitted in Percentage Rate .


Seal and Signature of Tenderer


Chief Engineer
B.S.E.I.D.C. Ltd, Patna

ANNEXURE-I

List of Key Plant & Equipment to be deployed on ROAD Work

[Reference Cl. 4.5 (B) (a)]



Sl.	Type of Equipment*	Max *** age as on (Years)	Road Contract Package Size **				
			Within one crore	Rs. 1- 5 Crores	Rs. 5- 30 Crores	Rs. 31-50 Crores	Above 50 Crores
1.	Motor Grader	5	As per the decision of Engineer-in-Charge concerned	1	1	3	5
2.	Dozer	5			1	1	2
3.	Front end Loader	5			1	2	3
4.	Smooth Wheeled Roller	5		1	2	2	3
5.	Vibratory Roller	5		1	1	1	2
6.	Fully Computerized Hot Mix Plant with Electronic Controls	5		1 (Min. 40-60 TPH capacity)	1 (Min 80-100 TPH capacity)	1 (Min 100-120 TPH capacity)	2
7.	Paver Finisher with Electronic Sensor	5		1 (Mechanical)	1	1	2
8.	Water Tanker	5		1	2	3	4
9.	Bitumen Sprayer	5-7		1	1	1	2
10.	Tandem Roller	5			1	2	2
11.	Concrete Mixes with Integral Weigh Batching facility	5		1 (Drum mixer)	1	1	1
12.	Concrete Batching and Mixing Plant (Minimum Capacity – 15m ³ /hour)	5			-	-	1
	Total -			8	13	18	29

* To be decided by Employer before floating the tender.

** On the basis of nature of Construction work list of key plant & Equipments will be decided.

*** Life of machine minus two years or 5 years on which ever is more.

Seal and Signature of Tenderer



 Chief Engineer
 B.S.E.I.D.C. Ltd, Patna
 Rnd

ANNEXURE – II

List of Key Personnel to be deployed on Contract Work

[Reference Cl. 4.5(B) (b)]

Sl. No.	Personnel*	Qualification	Contract Package Size						
			Rs. 5-30 Lacs	Rs. 30 Lacs to 70 Lacs	Rs. 70 Lacs to 2 Crores	Rs. 2-10 Crores	Rs. 10-30 Crores	Rs. 31-50 Crores	More than 50 Crores
1.	Project Manager	B.E. Civil + 10 Years Exp. (5 years as Manager) or retired E.E.					1 No.	1 No.	1 No.
2.	Site Engineer	B.E. Civil + 07 Years Exp. (3 years in Road Construction) or retired A.E.			1 No.	1 No.	1 No.	2 Nos	4 Nos.
3.	Plant Engineer	B.E. Mech./ Civil + 05 Years Exp. or Dip. Mech + 07 Years Exp. or Retired J.E.				1 No.	1 No.	1 No.	2 Nos.
4.	Quantity Surveyor	B.E. Civil + 05 Years Exp. or Dip. Civil + 07 Years Exp.						1 No.	2 Nos.
5.	Soil & Material Engineer	B.E. Civil + 07 Years Exp.						1 No.	2 Nos.
6.	Survey Engineer	B.E. Civil + 03 Years Exp. or Dip. Civil + 05 Years Exp.						1 No.	2 Nos.
7.	Site Supervisor or	Fresh Graduate in Civil or Diploma Civil + 03 Years Exp. or retired I.T.I Holder.		1 No.	1 No.	1 Nos.	2 Nos.	3 Nos.	4 Nos.
	Total			1	2	3	5	10	17

* The designation and no. of the personnel has to be decided by the Corporation as per the requirement

31/05/2014
Seal and Signature of Tenderer

Chief Engineer
B.S.E.I.D.C. Ltd, Patna
25-5-2014

SECTION 2
QUALIFICATION INFORMARION
(to be filled in by Bidder)

Seal and Signature of Tenderer

BIDDER SIGNATURE

[Signature]
25-6-2014
Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Rmb

QUALIFICATION INFORMATION

The information to be filled in by the Bidder in the following pages will be used for purposes of post qualification as provided for in Clause 4 of the Instructions to Bidders. This information will not be incorporated in the Contract.

1. For Individual Bidders . .
 - 1.1 Constitution or legal status of Bidder
(*Attach copy*)

Place of registration :

Principal place of business :

Power of attorney of signatory of Bid
(*Attach*)
 - 1.2 Total value of Civil Engineering construction work performed in the last five years**
(in Rs. Million)

Place of registration :

Principal place of business :

Power of attorney of signatory of Bid
(Attach)

1.2 Total value of Civil Engineering construction work performed in the last five years**
(in Rs. Million)

200	200	}	β
200	200		
200	200		
200	200		
200	201		

- 1.3.1 Work performed as prime contractor, work performed in the past as a nominated sub-contractor will also be considered provided the sub-contract involved execution of all main items of work described in the bid document, provided further that all other qualification criteria are satisfied (in the same name) on works of a similar nature over the last five years.**

[illegible]

* Attach certificate(s) from the Engineer(s)-in-Charge

**** Immediately preceding the financial year in which bids are received and current financial year will also be consider.**

*** Certificate issued of Central govt./ State govt./ Public undertaking (Nigam) .

β Attach certificate from Chartered Accountant.

~~25-8-2014~~

Seal and Signature of Tenderer

Chief Engineer 43
B.S.E.I.D.C. Ltd, Patna
End

1.3.2. Quantities of work executed as prime contractor, work performed in the past as a nominated sub-contractor will also be considered provided the sub-contract involved execution of all main items of work described in the bid document, provided further that all other qualification criteria are satisfied (in the same name and style) in the last five years : **

Year*	Name of the work	Name of the Employer*	Quantity of work performed (cum) @ Remarks						Remarks* (indicate contract Ref)
			Cement Concrete (including RCC & PCC)	Masonry	Earth works	WBM	WMM	Bituminous Work	
200__200__									
200__200__									
200__200__									
200__200__									
200__200__									

1.4 Information on Bid Capacity (works for which bids have been submitted and works which are yet to be completed) as on the date of this bid.

(A) Existing commitments and on-going works:

Description of works	Place & State	Contract No.	Name & Address of Employer	Value of Contract (Rs Cr)	Stipulated Period of Completion	Value of works* remaining to be completed (Rs Cr)	Anticipated date of completion
1	2	3	4	5	6	7	8

* Attach certificate(s) from the Engineer(s)-in-Charge

@ The item of work for which data is requested should tally with that specified in ITB clause 4.5A (c)

** Immediately preceding the financial year in which bids are received.

Delete, if prequalification has been carried out.

Handwritten signature and date: 25-6-2014

Seal and Signature of Tenderer
Handwritten signature

Chief Engineer 44
B.S.E.I.D.C. Ltd, Patna
Handwritten signature

Description of works	Place & State	Name & Address of Employer	Estimated value of works (Rs Cr)	Stipulated period of completion	Date when decision is expected	Remarks, if any
1	2	3	4	5	6	7

[illegible]

~~25-6-2014~~

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

8

1.6 Qualifications and experience of key personnel required for administration and execution of the Contract [Ref. Clause 4.5(B)(b)]. Attach biographical data. Refer also to Sub Clause 4.3 (e) of instructions to Bidders and Sub Clause 9.1 of the Conditions of Contract.

Position	Name	Qualification	Year of Experience (General)	Years of experience in the proposed position
Project Manager				
Etc.				

1.7 Proposed sub-contracts and firms involved. [Refer ITB Clause 4.3(k)]

Sanction of the works	Value of Sub-contract	Sub-contractor (Name & Address)	Experience in similar work
1	2	3	4

Attach copies of certificates on possession of valid license for executing water supply/ sanitary work/ building electrification works [Reference Clause 4.5(d) & Clause 4.5(e)]

***1.8** Financial reports for the last five years: balance sheets, profit and loss statements, auditors' reports (in case of companies/corporation), etc. List them below and attach copies.

* Delete, if prequalification has carried out

Seal and Signature of Tenderer

BOTV 3712 Rie

Chief Engineer 46
B.S.E.I.D.C. Ltd, Patna
25-6-2014
Rnd

1.11 Information on litigation history in which the Bidder is involved.

Other Party(ies)	Employer	Cause of Dispute	Amount involved	Remarks showing Present Status

2. Additional Requirements

*** (v) Copy of prequalification letter

~~APRO~~
25-6-2014

Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Pm8

**SAMPLE FORMAT FOR EVIDENCE OF ACCESS TO OR
AVAILABILITY OF CREDIT FACILITIES**

(CLAUSE 4.2 (i) OF ITB)

BANK CERTIFICATE

This is to certify that M/s. _____ is a reputed company with a good financial standing.

If the contract for the work, namely _____ is awarded to the above firm, we shall be able to provide overdraft/credit facilities to the extent of Rs. _____ to meet their working capital requirements for executing to the above contract during the contract period.


(Signature)

Name of Bank

Senior Bank Manager

Address of the Bank

(Seal & Signature of Tenderer)




Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Pmb

AFFIDAVIT

1. I, the undersigned, do hereby certify that all the statements made in the required attachments are true and correct.
2. The undersigned also hereby certifies that neither our firm M/s _____ has been blacklisted, nor has abandoned any work in any government department, India nor any contract awarded to us for such works have been rescinded, during last five years prior to the date of this bid.
3. The undersigned hereby authorises and request(s) any bank, person, firm or corporation to furnish pertinent information deemed necessary and requested by the Department to verify this statement or regarding my (our) competence and general reputation.
4. The undersigned understand and agrees that further qualifying information may be requested, and agrees to furnish any such information at the request of the Department Project implementing agency.
5. If the work is allotted to me or my firm, I/we will arrange the required fund and submit the work program for timely completion of the work.
6. I/we will invest a minimum of cost up to 25% of contract value of work during implementation of contract.

(Signed by an Authorized Officer of the Firm)

Title of Officer

Name of Firm


(Seal & Signature of Tenderer)


DATE
Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Rnt

UNDERTAKING

I, the undersigned do hereby undertake that our firm M/s _____
_____ would invest a minimum cash up to 25% of the value of the work
during implementation of the Contract.


(Signed by an Authorised Officer of the Firm)

Title of Officer

Name of Firm

DATE

(Seal & Signature of Tenderer)




Chief Engineer 50
B.S.E.I.D.C. Ltd, Patna


SECTION 3
GENERAL CONDITIONS OF CONTRACT


(Seal & Signature of Tenderer)


Chief Engineer
B.S.E.I.D.C. Ltd, Patna
P. 8

Table of Contents

Clause	Details	Page
	<u>General</u>	52
1	Performance guarantee	52
1A	Recovery of Security deposit	53
2	Compensation for delay (Liquidated Damage)	53
2A	Incentive for early completion	53
3	When contract can be determined / Rescinded	55
4	Contractor liable to pay compensation even if action not taken under clause 3	73
18	Contractor to supply tools & plants etc.	76
20	Min. Wages Act to be complied with	76
21	Work not to be sublet/ Action in case of insolvency	76
23	Changes in firm's constitution to be intimated	76
24	Approval of Engineer Incharge	77
32	Hire of Plant & Machinery	80
33	Employment of Technical Staff and employees	82
34	Levy/ Taxes payable by Contractor	84
37	Termination of Contract on death of contractor	84
38	If relation working in " corporation" then contractor not allowed to tender	85
39	No Gazetted Engineer to work as contractor within two years of retirement.	85
41	Release of Security Deposit.	86
46	Safety, Security and Protection of the Environment	87
50	Commencement of Works	87
	<u>Time Control</u>	
5	Time and Extension for delay	55
45	Cash flow estimate to be submitted.	86
	<u>Cost Control</u>	
5A	Minutes of Meeting	56
6	Measurement of work done	56
7	Payment on Intermediate certificate to be regarded as advances	57
9	Payment of final bill	59
9A	Payment of contractor's Bills to Banks	59
10B	Secured Advance on Non-Perishable materials/ Mobilisation Advance / Plant & Machinery & Shuttering material advance / Interest & Recovery.	62
10C	Payment on account of Increase in Prices / Wages due to Statutory	

(Seal & Signature of Tenderer)

[Handwritten Signature]

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

[Handwritten Signature]

	order(s)	
10CA	Payment on account of increase / decrease in prices of construction materials after receipt of tender.	64
10CC	Payment due to Increase / Decrease in Prices / Wages after receipt of tender for works (Time more than 18 eighteen months)	65
10D	Dismantled material Employer property.	68
12	Deviations / Excess item Variations / extent and pricing	69
12.2	Deviation, extra items and pricing	69
12.3	Deviation, Deviated quantities , pricing	69
13	Foreclosure of contract due to Abandonment or Reduction in scope of work.	70
14	Cancellation of contract in full or part.	70
15	Suspension of work	72
16	Action in case work not done as per specification	72
22	Compensation	76
25	Settlement of disputes & arbitration	77
27	Lumpsum Provisions in Tender	78
29	With holding and lien in respect of sums due from contractor	79
29A	Lien in respect of claims in other Contracts	79
35	Condition of reimbursement of lavy / taxes after receipt of the tender.	84
43	Contractor's Risks	86
44	Insurance	86
47	Cost of Samples	87
48	Cost of Tests	87
49	Cost of Tests not provided for	87

Finishing Control

8	Completion certificate and completion plan	58
8A	Contractor to keep site clean	59
8B	Completion plans to be submitted by the contractor	59
17	Contractor liable for damage, defects during maintenance period.	73
40	Return of materials and recovery of excess materials issued.	85
51	Substantial Completion of Parts	85

Quality Control

10	Materials supplied by Employer	59
10A	Materials to be provided by the contractor	61
11	Work to be executed in accordance with specification, drawings, orders etc.	68
26	Contractor to indemnity Corporation against Patent Rights.	78
28	Action where no Specifications are specified	78
42	Responsibility of technical staff and employees	86


 (Seal & Signature of Tenderer)

Chief Engineer
 B.S.E.I.D.C. Ltd, Patna

 25-6-2014

Other Condition & Control

18A	Recovery of compensation paid to workman	74
18B	Ensuring payment and amenities to workers if contractor fails	74
19	Labour laws to complied by the Contractor	74
19B	Payment of wages	75
30	Unfiltered water supply	80
31	Return of Surplus materials	80
26	Contractor to indemnity Corporation against patent Rights	78
28	Action where no specification are specified	78
38	Imprisonment of contractor	84
40	Return of materials and recovery for excess materials issued.	85
42	Responsibility of technical staff and employees.	86
52	Force majeure	88
53	Recovery	88

(Seal & Signature of Tenderer)

अजय कुमार सिंह


Chief Engineer
B.S.E.I.D.C. Ltd, Patna

25-6-2014
Pm8

GENERAL GUIDELINES

1. This book of "General Conditions of Contract" is applicable to both types of tenders i.e. "Percentage rate tenders" and "Item rate tenders". Accordingly alternative provisions for conditions Nos. 4, The appropriate alternatives will be applicable in specific cases depending on whether this is used for percentage rate tender (Form-) or item rate tender (Form -)
2. Form -, Schedules A to F, special conditions/ specifications and drawing only will be issued to intending bidders. The standard form shall form part of the agreement to be drawn and signed by both parties after acceptance of tender.
3. All blanks are confined to Notice Inviting Tender (Form -) and Schedules A to F.
4. Authority approving the Notice Inviting Tender (NIT) shall fill up all the blanks in Form -6 and in Schedules B to F before issue of Tender Papers.
5. The intending bidders will quote their rates in Schedule A.
6. The proforma for registers and Schedules A to F are only for information and guidance. These are not to be filled in the Standard Form. The Schedules with all blanks, duly filled shall be separately issued to all intending tenderers.


(Seal & Signature of Tenderer)


Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Rmd

BIHAR STATE EDUCATIONAL INFRASTRUCTURE DEVELOPMENT CORPORATION LTD.
(A Govt. Of Bihar UNDERTAKING)

Form-1

NOTICE INVITING TENDER

contractor State RCD/BCD/ other State P.W.D. & Central Government / PSU or any Agency of National / International
repute

I of Tender to any Contractor registered with Central Government/any State Government / State RCD/BCD or any PSU or an agency of International / National repute may be submitted without the registration with Corporation. However, registration with the Corporation will be essential after issue of L.O.A.

(b) submission of bid (In case of other State PWD/ CPWD/ any PSU eligible contractors or Agencies of National/ International repute following documents (from a to c) have to be submitted after issue of letter of acceptance).t / other State PWD / CPWD Contractor will provide definite proof from appropriate authority for tools & Plant and Undertaking to install it on works site after getting letter of acceptance

2. Agreement shall be drawn with the successful tenderer on prescribed Form No. BSEIDC-2/3. Tenderer shall quote his rates as per various terms and conditions of the said form which will form part of the agreement.
5. The time allowed for carrying out the work will be from the day after the date of written orders to commence the work or from the first date of handing over of the site, whichever is later, in accordance with the phasing, if any, indicated in the tender documents.
6. The site for the work is available.

OR

The site for the work shall be made available in parts as specified below :-

7. Receipt of applications for issue of forms will be stopped by 1500 Hrs. days before the date fixed for opening of tenders. Issue of tender forms will be stopped day before the date fixed for opening of tenders or as mentioned in press Notice.

Tender documents consisting of plans, specifications, the schedule of quantities of the various classes of work to be done and the set of terms & conditions of contract to be complied with by the contractor whose tender may be accepted and other necessary documents can be seen in the office of the between hours of 11.00 A.M. & 03.00 P.M. from to everyday except on Sunday and Public Holidays. Tender documents, excluding standard form, will be issued from his office during the hours specified above, on payment of the following :-

- i) Rs. in as cost of tender.
- ii) Earnest Money of Rs. as mentioned in Bihar Financial Rule . Nationalised/dinstate. (

8. Tenders, which should always be placed in sealed envelope, with the name of work and due date written on the envelopes, will be received by the Dated -----

(Seal & Signature of Tenderer)

Signature of Tenderer

Signature
25-6-2014
Chief Engineer⁵⁶
B.S.E.I.D.C. Ltd, Patna
Put

up to 03.00 P.M. on and will be opened by him or his authorized representative in his office on the same day at 03.30 P.M.

9. The Contractor shall be required to deposit an amount equal to 2% of the tendered value of the work as performance guarantee in the form as mentioned in Bihar Financial Rules. F, bank guarantee is acceptable.

10. The description of the work is as follows:-----
Copies of other drawings and documents pertaining to the works will be open for inspection by the tenderers at the office of the above-mentioned officer.

* as applicable

Tenderers are advised to inspect and examine the site and its surroundings and satisfy themselves before submitting their tenders as to the nature of the ground and sub-soil (so far as is practicable), the form and nature of the site, the means of access to the site the accommodation they may require and in general shall themselves obtain all necessary information as to risks, contingencies and other circumstances which may influence or affect their tender. A tenderer shall be deemed to have full knowledge of the site whether he inspects it or not and no extra charges consequent on any misunderstanding or otherwise shall be allowed. The tenderer shall be responsible for arranging and maintaining at his own cost all materials, tool & plants, water, electricity access, facilities for workers and all other services required for executing the work unless otherwise specifically provided for in the contract documents. Submission of a tender by a tenderer implies that he has read this notice and all other contract documents and has made himself aware of the scope and specifications of the work to be done and of conditions and rates at which stores, tools and plant, etc. will be issued to him by the Corporation and local conditions and other factors having a bearing on the execution of the work.

11. Canvassing whether directly or indirectly, in connection with tenders is strictly prohibited and the tenders submitted by such contractors who resort to canvassing will be liable to rejection.
12. The competent authority on behalf of the Corporation reserves to himself the right of accepting the whole or any part of the tender and the tenderer shall bound to perform the same at the rate quoted.
13. The contractor shall not be permitted to tender for works in the Corporation in which his near relative is posted as officer in any capacity. He shall also intimate the names of persons who are working with him in any capacity or are subsequently employed by him and who are near relatives to any gazetted officer in the Corporation. Any breach of this condition by the contractor would render him liable to be removed from the approved list of contractors of the corporation.
14. No Engineer of Gazetted rank or other Gazetted officer employed in Engineering or Administrative duties in an Engineering Department of the Government of Bihar is allowed to work as a contractor for a period of two years after his retirement from Government service, without the previous permission of the Government of Bihar in writing. This contract is liable to be cancelled if either the contractor or any of his employee is found any time to be such a person who had not obtained the permission to the Government of Bihar as aforesaid before submission of the tender or engagement in the contractors service.
15. The tender for the works shall remain open for acceptance for a period of days from the date of opening of tenders. If any tenderer withdraws his tender before the said period or issue of letter of acceptance, whichever is earlier, or makes any modifications in the terms and conditions of the tender which are not acceptable to the Corporation, then the Corporation shall, without prejudice to


(Seal & Signature of Tenderer)

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

any other right or remedy, be at liberty to forfeit % of the said earnest money as aforesaid. 6. The Corporation has right to cancel or postpone any work without giving any notice or clarification. 17. The Corporation may add or delete any of the condition required for execution of any work. 18. This Notice Inviting Tender shall form a part of the contract document. The Authority, shall the and of by the successful tenderer contractor.

Signature the Competent Authority
For & on behalf of the Corporation.

BIHAR STATE EDUCATIONAL INFRASTRUCTURE DEVELOPMENT CORPORATION LTD.
(A GOVT. OF BIHAR UNDERTAKING)

Form-2/3

Percentage Rate Tender & Contract for Works

(A) Tender for the work of :-

(i) To be submitted by

(ii) To be opened

Signature of officer issuing the documents

Designation

Date of issue

TENDER


I/We have read and examined the notice inviting tender, schedule, A,B,C,D,E & F. Specifications applicable, Drawings & Designs, General Rules and Directions, Conditions of Contract, clauses of contract, Special conditions, Schedule of Rate & other documents and Rules referred to in the conditions of contract and all other contents in the tender document for the work.

I/We hereby tender for the execution of the work specified for the Bihar State Educational Infrastructure Development Corporation Ltd.. within the time specified in Schedule 'F', viz., schedule of quantities and in accordance in all in respects with the specifications, designs, drawings and instructions in writing referred to in Rule-1 of General Rules and Directions and in Clause 11 of the Conditions of contract and with such materials as are provided for, by, and in respect in accordance with, such conditions so far as applicable.

We agree to keep the tender open for days from the due date of submission thereof and not to make any modifications in its terms and conditions.

A sum of Rs2,06,200.00 (Rupees Two Lacs Six Thousand Two Hundred Only) has been deposited guarantee of a Nationalised / scheduled bank as earnest money. If I/We fail to furnish the prescribed performance guarantee within prescribed period, I/we agree that the competent Authority of the

(Seal & Signature of Tenderer)



Chief Engineer
B.S.E.I.D.C. Ltd, Patna

58

Corporation or his successors in office shall without prejudice to any other right or remedy, be at liberty to forfeit the said earnest money absolutely. Further, if/we fail to commence work as specified, I/we agree that competent Authority of the corporation or his successors in office shall without prejudice to any other right or remedy available in law, be at liberty to forfeit the said earnest money and the performance guarantee absolutely, otherwise the said earnest money shall be retained by him towards security deposit to execute all the works referred to in the tender documents upon the terms and conditions contained or referred to therein and to carry out such deviations as may be ordered, up to maximum of the percentage mentioned in Schedule 'F' and those in excess of that limit at the rates to be determined in accordance with the provision contained in Clause 12.2 and 12.3 of the tender form.

I/We hereby declare that I/We shall treat the tender documents drawings and other records connected with the work as secret/confidential documents and shall not communicate information/derived therefrom to any person other than a person to whom I/We am/are authorized to communicate the same or use the information in any manner prejudicial to the safety of the Corporation.

Dated

Signature of Contractor
Postal Address

Witness :

Address :

Occupation :

ACCEPTANCE

The above tender (as modified by you as provided in the letters mentioned hereunder) is accepted by me for and on behalf of the Bihar State Educational Infrastructure Development Corporation Ltd for a sum of Rs.

The letters referred to below shall form part of this contract Agreement :-

- a)
- b)
- c)

For & on behalf of the Bihar State Educational Infrastructure Development Corporation Ltd.

Signature of the competent Authority.....

Designation of the competent Authority.....

Dated


(Seal & Signature of Tenderer)


Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Rm8



GOVERNMENT OF BIHAR
ALL WORKS DEPARTMENT

**General
Rules &
Directions**

1. All work proposed for execution by contract will be notified in a form of invitation to tender pasted in public places and signed by the officer inviting tender or by publication in News papers and the internet as the case may be.

This form will state the work to be carried out, as well as the date for submitting and opening tenders and the time allowed for carrying out the work, also the amount of earnest money to be deposited with the tender, and the amount of the security deposit to be deposited by the successful tenderer and the percentage, if any, to be deducted from bills. Copies of the specifications, designs and drawings and any other documents required in connection with the work signed for the purpose of identification by the officer inviting tender shall also be open for inspection by the contractor at the office of officer inviting tender during office hours.

2. In the event of the tender being submitted by a firm, it must be signed separately either by one or all the partners or person duly authorised by the partners, it must be signed on behalf of the firm by a person holding the requisite authorisations, such authorisations to be produced with the tender, and it must disclose that the firm is duly registered under the Indian Partnership Act, 1952.

3. Receipts for payment on account of work done, when executed by a firm, must also be signed by one or all the partners or a duly authorised signatory of the firm.

**Appl cable for
Item Rate
Tender only
(Form- 3)**

4. Any person who submits a tender shall fill up the usual printed form, stating at what rate he is willing to undertake each item of the work. Tenders, which propose any alteration in the work specified in the said form of invitation to tender, or in the time allowed for carrying out the work, or which contain any other conditions of any sort, will be liable to rejection. No single tender shall include more than one work, but contractors who wish to tender two or more works shall submit separate tenders for each; with the nature and number of works to which they refer on the envelope.

The rate(s) must be quoted in decimal coinage. Amounts must be quoted in full rupees by ignoring fifty paise and less and considering more than fifty paise as rupee one.

**Appl cable for
Percentage
Rate Tender
only
(Form- 2)**

- 4A. In case of Percentage Rate Tenders, tenderer shall fill up the usual printed form, stating at what percentage below/above (in figures as well as in words) the total estimated cost given in Schedule of Quantities at Schedule- A, he will be willing to execute the work. Tenders, which propose any alteration in the work specified in the said form of invitation tender, or in the time allowed for carrying out the work, or which contain any other conditions of any sort, will be liable to rejection. No single tender shall include more than one work but contractors who wish to tender for two or more works shall submit separate tender for each. Tender shall have the name and number of the works to which they refer, written on the envelope.

(Seal & Signature of Tenderer)

[Handwritten Signature]

[Handwritten Signature]
25-6-2014
Chief Engineer 60
B.S.E.I.D.C. Ltd, Patna
Enr

If for any special reasons, the contract provides for the payments for work done to be made at a specified percentage below or above the rates entered in the sanctioned estimate of the work (or the Scheduled of Rates), it should be stated in clear terms in the contract that the deductions or additions, as the case may be of the percentage, will be calculated on the gross, and not the net amounts of the bills for work done and in fixing the percentage it should be borne in mind that the calculations will be made.

5. The officer inviting tender or his duly authorized assistant, will open tenders in the presence of any intending contractors who may be present at the time, and will enter the amount of the several tenders in a comparative statement in a suitable form. In the event of a tender being accepted, a receipt for the earnest money forwarded therewith shall thereupon be given to the contractor who shall thereupon for the purpose of identification sign copies of the specifications and other documents mentioned in Rule-1. In the event of a tender being rejected, the earnest money forwarded with such unaccepted tender shall thereupon be returned to the contractor remitting the same, without any interest.
6. The officer inviting tenders shall have the right of rejecting all or any of the tenders and will not be bound to accept the lowest or any other tender.
7. The receipt of an accountant or clerk for any money paid by the contractor will not be considered as an acknowledgment or payment to the officer inviting tender and the contractors shall be responsible for seeing that he procures a receipt signed by the office inviting tender or a duly authorized person.
8. The memorandum of work tendered for and the schedule of materials to be supplied by the department and their issue-rates, shall be filled and completed in the office of the officer inviting tender before the tender form is issued. If a form is issued to an intending tenderer without having been so filled in and incomplete, he shall request the officer to have this done before he completes and delivers his tender.
9. For works of sensitive nature the tenderers shall sign a declaration under the Official Secrets Act 1923, for maintaining secrecy of the tender documents drawing or other records connected with the work given to them. The unsuccessful tenderers shall return all the drawing given to them.
10. In the case of Item Rate Tenders, only rates quoted shall be considered. Any tender containing percentage below/above the rates quoted is liable to be rejected. Rates quoted by the contractor in item rate tender in figures and words shall be accurately filled in so that there is no discrepancy if any discrepancy found or the rates which correspond with the amount worked out of an item is not worked out by the contractor or it does not correspond with the rates written either in figures or in words then the rates quoted by the contractor in words shall be taken as correct. Where the rate quoted by the contractor in figures and in words tally but the amount is not worked out correctly, the rates quoted by the contractor will unless otherwise proved be taken as correct and not the amount.
- 10A. In case of Percentage Rate Tenders only percentage quoted shall be considered. Any tender containing item rates is liable to be rejected. Percentage quoted by the contractor in percentage rate tender shall be accurately filled in figures and words, so that there is no discrepancy. However if the contractor has worked out the amount of the tender and if any discrepancy is found in the percentage quoted in words and figures, the percentage which corresponds with the amount worked out by the contractor shall, unless otherwise proved, be taken as correct. If the amount of the tender is not worked out by the contractor or it does not correspond with the percentage written either in figures or in words then the percentage quoted by the contractor in words shall be taken as correct. Where the percentage quoted by the contractor in figures and in words tally but the amount is not worked out correctly, the

Applicable for
Item Rate
Tender only
(Form- 3)

Applicable for
Percentage
Rate Tender
only (Form- 2)


(Seal & Signature of Tenderer)

Chief Engineer, 61
B.S.E.I.D.C. Ltd, Patna
For

percentage quoted by the contractor will, unless otherwise proved, be taken as correct and not the amount.

11. In the case of any tender where unit rates of any item/items appear unrealistic, such tender will be considered as unbalanced and in case the tenderer is unable to provide satisfactory explanation such a tender is liable to be disqualified and rejected.

Applicable for
Item Rate
Tender only
(Form- 3)

12. All rates shall be quoted on the tender form. The amount for each item should be worked out and requisite totals given. Special care should be taken to write the rates in figures as well as in words and the amount in figures only, in such a way that interpolation is not possible. The total amount should be written both in figures and in words. In case of figures, the word 'Rs' should be written before the figure of rupees and word 'P' after the decimal figures, e.g. 'Rs 2.15 P' and in case of words, the word, 'Rupees' should precede and the word 'Paise' should be written in the end. Unless the rate is in whole rupee and followed by the word 'only' it should invariably be up to two decimal places. While quoting the rate in schedule of quantities, the word 'only' should be written closely following the amount and it should not be written in the next line.

Applicable for
Percentage
Rate Tender
only (Form- 2)

- 12A. In Percentage Rate Tender, the tenderer shall quote percentage below/above (in figures as well as in words) at which he will be willing to execute the work. He shall also work out the total amount of his offer and the same should be written in figures as well as in words in such a way that no interpolation is possible. In case of figures, the word 'Rs' should be written before the figure of rupees and word P after the decimal figures, e.g. 'Rs 2.15 P' and in case of words, the word 'Rupees' should precede and the word 'paise' should be written at the end.

The Quoted rate less than x % below the BOQ cost will be unworkable and bid will be rejected where x = 15 %; if materials will not be issued by the employer. And if materials will be issued by the employer then

$$X = (A - B) / A \times 15 \%$$


Where A = BOQ Cost

B = Cost of materials stipulated to be issued by the employer.

Where the value of X will not be less than 10% in other words it will be within 10 to 15%

13. (i) The contractor whose tender is accepted, will be required to furnish performance guarantee of 2 (two percent) including earnest money of the tendered amount within specified period. This guarantee shall be in the form of or Bank guarantee from any Nationalised / schedule bank in the State for works of more than one crore.
- (ii) The contractor whose tender is accepted, will also be required to furnish by way of Security Deposit for the fulfillment of his contract, an amount equal to 8 % of the tendered value of the work. The security deposit will be collected by deductions from the running bills of the contractor at the rates mentioned above
14. On acceptance of the tender, the name of the accredited representative(s) of the contractor who would be responsible for taking instructions from the Engineer-in-Charge shall be communicated in writing to the Engineer-in-Charge.
15. Sales-tax, purchase tax, turnover tax, service tax, entry tax royalty or any other tax on material in respect of this contract shall be payable by the Contractor and Government will not entertain any claim whatsoever in respect of the same.
16. The contractor shall give a list of both gazetted and non-gazetted BSEIDC employees related to him posted in the division, if any.

(Seal & Signature of Tenderer)



Chief Engineer
B.S.E.I.D.C. Ltd, Patna

- 31674272018
(Seal & Signature of Tenderer)

Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Rons

- 63

CONDITIONS OF CONTRACT

- Definitions :**
1. The contract means the document forming the tender and acceptances thereof and the formal agreement executed between the competent authority on behalf of the Bihar State Educational Infrastructure Development Corporation Ltd. and the Contractor, together with the documents referred to therein including these conditions, the specifications, designs, drawings and instructions issued from time to time form one contract and shall be complementary to one another.
 2. In the contract, the following expressions shall, unless the context otherwise requires have the meanings, hereby respectively assigned to them :-
 - i) The expression works or work shall, unless there be something either in the subject or context repugnant to such construction, be construed and taken to mean the works by or by virtue of the contract contracted to be executed whether temporary or permanent, and whether original, altered, substituted or additional.
 - ii) The site shall mean the land/or other places on, into or through which work is to be executed under the contract or any adjacent land, path or street through which work is to be executed under the contract or any adjacent land, path or street which may be allotted or used for the purpose of carrying out the contract.
 - iii) The Contractor shall mean the individual, firm or company, whether incorporate or not, undertaking the works and shall include the legal personal representative of such individual or the persons composing such firm or company, or the successors of such firm or company and the permitted assignees of such individual, firm of company.
 - iv) The Engineer-in-Charge means the Engineer officer who shall supervise and be in-charge of the work and who shall sign the contract on behalf of the Bihar State Educational Infrastructure Development Corporation Ltd. as mentioned in Schedule 'F' hereunder.
 - v) Corporation shall mean the Bihar State Educational Infrastructure Development Corporation Ltd..
 - vi) Excepted Risk are risks due to riots (other than those on account of contractor employees); war (whether declared or not) invasion, act of foreign enemies, hostilities, civil war, rebellion revolution, insurrection, any act of Government, damages from aircraft, acts of God, such as earthquake, lightening and unprecedented floods, and other causes over which the contractor has no control and accepted as such by the Accepting Authority Provided that the contractor is also to show that he has taken all due precautions to avoid / un, minimise any adverse after / damage from the above or causes solely due to use or occupation by Government of the part of the works in respect of which a certificate of completion has been issued or a caused solely due to Government's faulty design of works.
 - vii) Bill of quantity means the price and completed Bill of Quantities forming part of the Bid.
 - viii) The Defect liability certificate is the certificate issued by Engineer-in-Charge after defect liability period has ended and upon correction of defects by the contractor.
 - ix) The defect liability period will be decided by the Corporation for different nature of works from date of completion of the work and must be mentioned in the agreement.
It will be decided by the Corporation for different nature of work from time to time as mentioned in contract Data.
 - x) The intended completion date is the time intended to complete the work by the contractor.

(Seal & Signature of Tenderer)

[Handwritten Signature]

[Handwritten Signature]
25-6-2014
Chief Engineer
B.S.E.I.D.C. Ltd, Patna
[Handwritten Initials]

- xi) The start date is given in the contract data. It is the date when the contractor shall commence execution of the works. It does not necessarily coincide with any of the site possession date.
- xii) A 'sub contractor' is a person or corporate body who has a contract with the contractor to carry out a part of the construction work in the contract, which includes work on the site.
- xiii) Temporary works are works designed, constructed, installed and removed by the contractor that are needed for construction or installation of the works.
- xiv) Market Rate shall be the rate as decided by the competent authority on the basis of the cost of materials and labour at the site where the work is to be executed plus the percentage mentioned in Schedule 'F' to cover, all overheads and profits.
- xv) Schedule(s) referred to in these conditions shall mean the relevant schedule(s) annexed to the tender papers or the standard Schedule of Government mentioned in Schedule 'F' hereunder, with the amendments thereto issued up to date of receipt of the tender.
- xvi) Corporation means Bihar State Educational Infrastructure Development Corporation Limited, which invite tenders on behalf of Competent Authority of Corporation as specified in schedule 'F'.
- xvii) Specifications means the specifications followed by relevant department of the Government of India / State Government.
- xviii) Tender value means the value of the entire work as stipulated in the letter award.

Scope and Performance

- 3. Where the context so requires, words imparting the singular only also include the plural and vice versa. Any reference to masculine gender shall whenever required include feminine gender and vice versa.
- 4. Heading and Marginal notes to these General Conditions of Contract shall not be deemed to form part thereof or be taken into consideration in the interpretation or construction thereof or of the contract.
- 5. The contractor shall be furnished, free of cost one certified copy of the contract documents except standard specifications, Schedule of Rates and such other printed and published documents, together with all drawings as may be forming part of the tender papers. None of these documents shall be used for any purpose other than that of this contract.

Works to be carried out :

The work to be carried out under the Contract shall, except as otherwise provided these conditions, include all labour, materials, tools, plants, equipment and transport which may be required in preparation of and for and in the full and entire execution and completion of the works. The descriptions given in the Schedule of Quantities (Schedule - A) shall unless otherwise stated, be held to include wastage on materials, carriage and cartage, carrying and return of empties, hoisting, setting, fitting and fixing in position and all other labours necessary in and for the full and entire execution and completion of the work as aforesaid in accordance with good practice and recognized principles.

Sufficiency of Tender

The contractor shall be deemed to have satisfied himself before tendering as to the correctness and sufficiency of his tender for the works and of the rates and prices quoted in the Schedule of Quantities, which rates and prices shall, except as otherwise provided, cover all his obligations under the Contract and all matters and things necessary for the proper completion and maintenance of the works.

Discrepancies and Adjustment of Errors

The several documents forming the contract are to be taken as mutually explanatory of one another, detailed drawings being followed in preference to small scale drawing and figured dimensions in preference to scale and special conditions in preference to General Conditions.


(Seal & Signature of Tenderer)


Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Rmt

- 8.1 In the case of discrepancy between the schedule of Quantities, the Specifications and/or the Drawings, the following order of preference shall be observed :-
- Description of Schedule of Quantities.
 - Particular Specification and Special Condition, if any
 - Drawings.
 - MORT & H specification.
 - Indian Standard Specifications of B.I.S.
- 8.2 If there are varying or conflicting provisions made in any one document forming part of the contract, the Accepting Authority shall be the deciding authority with regard to the intention of the document and his decision shall be final and binding on the contractor.
- 8.3 Any error in description, quantity or rate in Schedule of Quantities or any omission therefrom shall not vitiate the Contract or release the Contractor from the execution of the whole or any part of the works comprised therein according to drawings and specifications or from any of his obligations under the contract.
9. The successful tenderer/contractor, after submitting the performance guarantee i.e. within 7 days of receipt of letter of acceptance shall attend the office of the Engineer-in-Charge for authentication signing and completion of the contractor document and execute the agreement consisting of :-
- the notice inviting tender, all the documents including drawings, if any, forming the tender as issued at the time of invitation of tender and acceptance thereof together with any correspondence leading thereto.
 - Standard P.W.D. Form as mentioned in Schedule 'F' consisting of :
Various standard clauses with corrections up to the date stipulated in Schedule 'F' along with annexure thereto.
 - Drawing.

**Signing of
Contract**

(Seal & Signature of Tenderer)




25-6-2014
Chief Engineer 66
B.S.E.I.D.C. Ltd, Patna
Encl

CLAUSE OF CONTRACT

CLAUSE 1

Performance Guarantee

- (i) The contractor shall submit an irrevocable PERFORMANCE GUARANTEE of 2% (Two percent) of the tendered amount including earnest money in the shape as mentioned in the Bihar Financial Rules or Bank Guarantee (for work costing more than one crore) or any other deposits mentioned for his proper performance of the contract agreement, (not withstanding and/or without prejudice to any other provisions in the contract) within period specified in scheduled 'F' from the date of issue of letter of acceptance. This period can be further extended by the Engineer-in-Charge up to a maximum period as specified in schedule 'F' on written request of the contractor stating the reason for delays in procuring the Bank Guarantee, to the satisfaction of the Engineer-in-Charge. This guarantee shall be in the form of N.S.C. of Post Office/ Pledged in favour of department; D.D. of any Scheduled Bank or State Bank of India or Bank Guarantee (for work costing more than Rupees one Crore.
- (ii) The performance Guarantee shall be initially valid up to 28 days beyond the defect liability.
- (iii) The Engineer-in-Charge shall not make a claim under the Performance guarantee except for amounts to which the Corporation is entitled under the contract (notwithstanding and/or without prejudice to any other provisions in the contract agreement) in the event of:
 - (a) Failure by the contractor to extend the validity of the Performance Guarantee as described herein above, in which event the Engineer-in-Charge may claim the full amount of the Performance guarantee.
 - (b) Failure by the contractor to pay the Corporation any amount due, either as agreed by the contractor or determined under any of the Clauses/Conditions of the agreement, within 30 days of the service of notice to this effect by Engineer-in-Charge.
 - (c) Failure by the contractor to rectify any defects as defined in the defect liability clause in the schedule - F of contract data to the satisfaction of the Engineer incharge.
- (iv) In the event of the contract being determined or rescinded under provisions of any of the clause/condition of the agreement, the performance guarantee shall stand forfeited in full and shall be absolutely at the disposal of the Governor of Bihar.

CLAUSE 1 A

Recovery of Security Deposit

The person/persons whose tender(s) may be accepted (hereinafter called the contractor) shall permit the Corporation at the time of making any payment to him for work done under the contract to deduct a sum at 8 % (eight percent) from the gross amount of each running bill till full amount of security deposit 10% (ten percent) of agreement value or value of work (whichever is higher) is reached. If value of work exceeds the agreement value, security deposit (10%) will be recovered for the exceeded work.

All compensations or the other sums of money payable by the contractor under the terms of this contract may be deducted from, or paid by the sale of a sufficient part of his security deposit or from the interest arising there from, or from any sums which may be due to or may become due to the contractor by the Corporation on any account whatsoever and in the event of his Security Deposit being reduced by reason of any such deductions or sale as aforesaid, the contractor shall within 10 days make good in cash or fixed deposit receipt tendered by the State Bank of India or by Scheduled Banks or Government Securities (if deposited for more than 12 months) endorsed in favour of the Engineer-in-Charge, any sum or sums which may have been deducted from, or raised by sale of his security deposit


(Seal & Signature of Tenderer)

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

or any part thereof. The security deposit shall be collected from the running bills of the contractor at the rates mentioned above and the earnest money at the time of tenders will be treated a part of the Security Deposit.

CLAUSE 2

Compensation
for Delay
(Liquidated
Damage)

If the contractor fails to maintain the required progress in terms of clause 5 or to complete the work and clear the site on or before the contract or extended date of completion, he shall, without prejudice to any other right or remedy available under the law to the Government / Corporation on account of such breach, pay as agreed compensation the amount calculated at the rates stipulated below as the Superintending Engineer / Chief Consultant (Technical) (whose decision in writing shall be final and binding) may decide on the amount of tendered value of the work for every completed day/month (as applicable) that the progress remains below that specified in Clause 5 or that the work remains incomplete.

This will also apply to items or group of items for which a separate period of completion has been specified.

i) Compensation

for delay of work

@ 2 % per month of delay to be computed on per Day basis

Provided always that the total amount of compensation for delay to be paid under this condition shall not exceed 10% of the Tendered Value of work or to the Tendered Value of the item or group of items of work for which a separate period of completion is originally given.

The amount of compensation may be adjusted or set-off against any sum payable to the Contractor under this or any other contract with the Corporation. In case, the contractor does not achieve a particular milestone mentioned in schedule- F, or the rescheduled milestone(s) in terms of Clause 5.4, the amount shown against that milestone shall be withheld, to be adjusted against the compensation levied at the final grant of extension of time. Withholding of this amount on failure to achieve a milestone, shall be automatic without any notice to the contractor. However, if the contractor catches up with the progress of work on the subsequent milestone(s), the withheld amount shall be released. In case the contractor fails to make up for the delay in subsequent milestone(s), amount mentioned against each milestone missed subsequently also shall be withheld. However, no interest, whatsoever, shall be payable on such withheld amount.

CLAUSE 2A

Incentive
for Early
completion

In case, the contractor completes the work ahead of scheduled completion time, a bonus @ 1% (one percent) of the tendered value per month computed on per day basis, shall be payable the contractor, subject to a maximum limit of 5% (five percent) of the tendered value. The amount of bonus, if payable, shall be paid along with final bill after completion of work. Provided always that provision of the Clause 2A shall be applicable only when so provided in 'Schedule F'.

CLAUSE 3

When Contract
can be
Determined /
Rescinded

Subject to the other provisions contained in this clause the Engineer-In-Charge may, without prejudice to his any other rights or remedy against the contractor in respect of any delay inferior workmanship, any claims for damages and/or any other provisions of this contract or otherwise, and whether the date of completion has or has not elapsed, by notice in writing absolutely determine the contract in any of the following cases :

(Seal & Signature of Tenderer)



Chief Engineer
B.S.E.I.D.C. Ltd, Patna



- i) If the contractor having been given by the Engineer-in-Charge a notice in writing to rectify, reconstruct or replace any defective work or that the work is being performed in an inefficient or otherwise improper or unworkman like manner shall omit to comply with the requirement of such notice for a period of seven days thereafter.
- ii) If the contractor being a company shall pass a resolution or the court shall make an order that the company shall be wind up or if a receiver or a manager on behalf of a creditor shall be appointed or if circumstances shall arise which entitle the court or the creditor to appoint a receiver or a manager or which entitle the court to make a winding up order.
- iii) If the contractor has, without reasonable cause, suspended the progress of the work or has failed to proceed with the work with due diligence so that in the opinion of the Engineer-in-Charge (which shall be final and binding) he will be unable to secure completion of the work by the date of completion and continues to do so after a notice in writing of seven days from the Engineer-in-Charge.
- iv) If the contractor fails to complete the work within the stipulated date or items of work with individual date of completion, if any stipulated, on or before such date(s) of completion and does not complete them within the period specified in a notice given in writing in that behalf by the Engineer-in-Charge.
- v) If the contractor persistently neglects to carry out his obligations under the contract and/or commits default in complying with any of the terms and conditions of the contract and does not remedy it or take effective steps to remedy it within 7 days after a notice in writing is given to him in that behalf by the Engineer-in-Charge.
- vi) If the contractor commits any acts mentioned in Clause 21 hereof:
- vii) If the work is not started by the contractor within 1/8th of the stipulated time subject to the maximum of 45 days.

When the contractor has made himself liable for action under any of the cases aforesaid, the Engineer-in-Charge on behalf of the Corporation shall have powers:

- a) To determine or rescind the contract as aforesaid (of which termination or rescission notice in writing to the contractor under the hand of Engineer-in-Charge shall be conclusive evidence). Upon such determination or rescission the Earnest Money Deposit, Security Deposit already recovered and Performance Guarantee under the contract shall be liable to be forfeited and shall be absolutely at the disposal of the Corporation.
- b) After giving notice to the contractor to measure up the work of the contractor and to take such whole, or the balance or part thereof as shall be un-executed out of his hands and to give it to another contractor to complete the work. The contractor, whose contract is determined or rescinded as above, shall not be allowed to participate in the tendering process for the balance work.

In the event of above course(s) being adopted by the Engineer-in-Charge, the contractor shall have no claim to compensation for any loss sustained by him by reasons of his having purchased or procured any materials or entered into any engagements or made any advances on account or with a view to the execution of the work or the performance of the contract. And in case action is taken under any of the provision aforesaid the contractor shall not be entitled to recover or be paid any sum for any work thereof or actually performed under this contract unless and until the Engineer-in-Charge has certified in writing the performance of such work and the value payable in respect thereof and he shall only be entitled to be paid the value so certified.


(Seal & Signature of Tenderer)


Chief Engineer
B.S.E.I.D.C. Ltd, Patna

CLAUSE 3A

In case, the work cannot be started due to reasons not within the control of the contractor as decided by the Employer within 1/4th of the stipulated time for completion of work, either party may close the contract. In such eventuality, the Earnest Money deposit and the Performance Guarantee of the contractor shall be refunded, but no payment on account of interest, loss of profit or damages etc. shall be payable at all. the reasons shall be examined by the Superintending Engineer / Chief Consultant (Technical) and his decision shall be final and binding.

CLAUSE 4

Contractor liable to pay compensation even if action not taken under Clause 3

In any case in which any of the powers conferred upon the Engineer-in-Charge by Clause-3 thereof, shall have become exercisable and, the same are not exercised the non-exercise thereof shall not constitute a waiver of any of the conditions hereof and such powers shall notwithstanding be exercisable in the event of any future case of default by the contractor and the liability of the contractor for compensation shall remain unaffected. In the event of the Engineer-in-Charge putting in force all or any of the powers vested in him under the preceding clause he may, if he so desires after giving a notice in writing to the contractor, take possession of (or at the sole discretion of the Engineer-in-Charge which shall be final and binding on the contractor) use as on hire (the amount of the hire money being also in the final determination of the Engineer-in-Charge) all or any tools, plant, materials and stores, in or upon the works, or the site thereof belonging to the contractor, or procured by the contractor and intended to be used for the execution of the work. or any part thereof, paying or allowing for the same in account at the contract rates or, in the case of these not being applicable, at current market rates to be certified by the Engineer-in-Charge, whose certificate thereof shall be final, and binding on the contractor, clerk of the works, foreman or other authorized agent to remove such tools, plant, materials, or stores from the premises (within a time to be specified in such notice) in the event of the contractor failing to comply with any such requisition, the Engineer-in-Charge may remove them at the contractor's expense or sell them by auction or private sale on account of the contractor and his risk in all respects and the certificate of the Engineer-in-Charge as to the expenses of any such removal and the amount of the proceeds and expenses of any such sale shall be final and conclusive against the contractor.

CLAUSE 5

Time and Extension for Delay

The time allowed for execution of the Works as specified in the Schedule 'F' or the extended time in accordance with these conditions shall be the essence of the Contract. The execution of the works shall commence from such time period as mentioned in letter of acceptance or from the date of handing over of the site whichever is later. If the Contractor commits default in commencing the execution of the work as aforesaid, Corporation shall without prejudice to any other right or remedy available in law, be at liberty to forfeit the security deposit absolutely.

- 5.1 As soon as possible after the contract is concluded the Contractor shall submit a Time & Progress Chart for each milestone and get it approved by the Employer. The Chart shall be prepared in direct relation to the time stated in the Contract documents for completion of items of the work. It shall indicate the forecast of the dates of commencement and completion of various trades or sections of the work and may be amended as necessary by agreement between the Engineer-in-Charge and Contractor within the limitations of time imposed in the contract documents, and further to ensure good progress during the execution of the work, the contractor shall in all cases in which the time allowed for any work, exceeds one month (save for special jobs for which a separate Programme has been agreed upon) complete the work as per milestone given in schedule 'F'.

(Seal & Signature of Tenderer)

3/3/17 3/3/17 Rie

Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Per

5.2 If the work(s) be delayed by.

- i) force majeure, or
- ii) Serious loss or damage by fire, or
- iii) Civil commotion, local.
- iv) delay on the part of other contractors or tradesmen engaged by Engineer-in-Charge in executing work not forming part of the Contract, or
- v) non-availability of stores, which are the responsibility of Employer to supply or
- vi) non-availability or break down of tools and Plant to be supplied or supplied by Employer or
- vii) any other cause which, in the absolute discretion of the authority mentioned in Schedule 'F' is beyond the Contractor's control.

then upon the happening of any such event causing delay, the Contractor shall immediately give notice thereof in writing to the Engineer-in-Charge but shall nevertheless use constantly his best endeavors to prevent or make good the delay and shall do all that may be reasonably required to the satisfaction of the Engineer-in-Charge to proceed with the works.

5.3 Request for the rescheduling of Milestones and extension of time, to be eligible for consideration, shall be made by the contractor in writing within fourteen days of the happening of the hindering event causing delay on the prescribed form. The Contractor may also, if practicable, indicate in such a request the period for which extension is desired.

5.4 In any such case the authority mentioned in Schedule 'F' may give a fair and reasonable extension of time and reschedule the milestones for completion of work. Such extension shall be communicated to the Contractor by the Engineer-in-Charge in writing, within 3 months of the date of receipt of such request. Non application by the contractor for extension of time shall not be a bar for giving a fair and reasonable extension by the Engineer-in-Charge and this shall be binding on the contractor.

5.5 The basic centerlines, reference points and benchmarks will be fixed by the Corporation. The contractor shall establish at his own cost at suitable points, additional reference lines and bench marks as may be necessary and instructed by the Engineer-in-charge. The contractor shall remain responsible for the sufficiency and accuracy of all the bench marks and reference lines.

CLAUSE 5A


The Engineer may require the contractor to attend a progress review meeting during execution of work.

The Engineer shall record the minutes of the meeting and provide a copy to the Contractor for compliance. These minutes will be a part of evidence in case of any request for extension of time or impunitive action against the contractor.

CLAUSE 6

Measurement of Work Done Engineer-in-Charge shall, except as otherwise provided, ascertain and determine measurement and the value in accordance with the contract of work done.


(Seal & Signature of Tenderer)


25-6-2014
Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Rmb

All measurement of all items having financial value shall be entered in Measurement Book and/or level field book so that a complete record is obtained of all works perform under the contract.

All measurements and levels shall be taken jointly by the Engineer-in-Charge or his authorized representative and by the contractor or his authorized representative at least once in a month during the progress of the work and such measurements shall be signed and dated by the Engineer-in-Charge and the contractor or their representatives in token of their acceptance. If the contractor objects to any of the measurements recorded, a note shall be made to that effect with reason and signed by both the parties.

If for any reason the contractor or his authorized representative is not available and the work of recording measurements is suspended by the Engineer-in-Charge or his representative, the Engineer-in-Charge and the Corporation shall not entertain any claim from contractor for any loss or damages on this account. If the contractor or his authorized representative does not remain present at the time of such measurements after the contractor or his authorized representative has been given a notice in writing three (3) days in advance or fails to countersign or to record objection within a week from the date of the measurement, then such measurements recorded in his absence by the Engineer-in-Charge or his representative shall be deemed to be accepted by the Contractor.

The contractor shall, without extra charge, provide all assistance with every appliance labour and other things necessary for measurements and recording levels.

Except where any general or detailed description of the work expressly shows to the contrary, measurements shall be taken in accordance with the procedure set forth in the specifications notwithstanding any provision in the relevant Standard Method of measurement or any general or local custom. In the case of items which are not covered by specifications, measurements shall be taken in accordance with the relevant standard method of measurement issued by the Bureau of India Standards and if for any item no such standard is available then a mutually agreed method as approved by the Corporation shall be followed.

The contractor shall give not less than seven days notice to the Engineer-in-Charge or his authorized representative in charge of the work before covering up or otherwise placing beyond the reach of measurement any work in order that the same may be measured and correct dimension thereof be taken before the same is covered up or placed beyond the reach of measurement and shall not cover up and place beyond reach of measurement any work without consent in writing of the Engineer-in-Charge or his authorized representative in charge of the work who shall within the aforesaid period of seven days inspect the work, and if any work shall be covered up or placed beyond the reach of measurements without such notice having been given of the Engineer-in-Charge's consent being obtained in writing the same shall be uncovered at the contractor's expense, or in default thereof no payment or allowance shall be made for such work or the materials with which the same was executed.

Engineer-in-Charge or his authorized representative may cause either themselves or through another officer of the department to check the measurements recorded jointly or otherwise as aforesaid and all provisions stipulated herein above shall be applicable to such checking of measurements or levels.

It is also a term of this contract that recording of measurements of any item of work in the measurement book and/or its payment in the interim, on account or final bill shall not be considered as conclusive evidence as to the sufficiency of any work or material to which it relates nor shall it relieve the contractor from liabilities from any over measurement defects noticed till completion of the defects liability period.

25-6-2014

(Seal & Signature of Tenderer)

B. S. E. I. D. C. Patna

72
B.S.E.I.D.C. Ltd, Patna
Rmt

CLAUSE 7

**Payment on
Intermediate
Certificate to be
Regarded as
Advances**

No payment shall be made for work for less than the estimated work of Rs. 2.5 lacs till the whole of the work shall have been completed and certificate of completion given. For works estimated to cost over Rs. 2.5 lacs the interim or running account bill shall be submitted by the contractor for the work executed on the basis of such recorded measurements on the format of the Corporation in triplicate on or before the date of every month fixed for the same by the Engineer-in-Charge. The contractor shall not be entitled to be paid any such interim payment if the gross work done together with net payment/ adjustment of advances for material collected, if any, since the last such payment is less than the amount specified in Schedule 'F', in which case the interim bill shall be prepared on the appointed date of the month after the requisite progress is achieved. The Engineer-in-Charge shall arrange to have the bill verified by taking or causing to be taken, where necessary, the requisite measurements of the work. In the event of the failure of the contractor to submit the bills, Engineer-in-Charge shall prepare or cause to be prepared such bills in which event no claims whatsoever due to delays on payment including that of interest shall be payable to the contractor. Payment on account of amount admissible shall be made by the Engineer-in-Charge certifying the sum to which the contractor is considered entitled by way of interim payment at such rates as decided by the Engineer-in-Charge. The amount admissible shall be paid by 10th working day after the day of presentation of the bill by the Contractor to the Engineer-in-Charge or his Assistant Engineer together with the account of the material issued by the Corporation, or dismantled materials, if any. In the case of works outside the headquarters of the Engineer-in-Charge the period of ten working days will be extended to fifteen working days.

All such interim payments shall be regarded as payment by way of advances against final payment only and shall not preclude the requiring of bad, unsound and imperfect or unskilled work to be rejected, removed, taken away and reconstructed or re-erected. Any certificate given by the Engineer-in-Charge relating to the work done or materials delivered forming part of such payment may be modified or corrected by any subsequent such certificate(s) or by the final certificate and shall not by itself be conclusive evidence that any work or materials to which it relates is/are in accordance with the contract and specifications. Any such interim payment, or any part thereof shall not in any respect conclude, determine or affect in any way powers of the Engineer-in-Charge under the contract or any of such payments be treated as final settlement and adjustment of accounts or in any way vary or affect the contract.

Pending consideration of extension of date of completion interim payments shall continue to be made as herein provided as per clause - 2, without prejudice to the right of the Corporation to take action under the terms of this contract for delay in the completion of work, if the extension of date of completion is not granted by the competent authority.

CLAUSE 8

**Completion.
Certificate and
Completion Plans**

Within ten days of the completion of the work, the contractor shall give notice of such completion to the Engineer-in-Charge and within fifteen days of the receipt of such notice the Engineer-in-Charge shall inspect the work and if there is no defect in the work shall furnish the contractor with a final certificate of completion, otherwise a provisional certificate of physical completion indicating defects (a) to be rectified by the contractor and/or (b) for which payment will be made at reduced rates, shall be issued. But no final certificate of completion shall be issued, nor shall the work be considered to be complete until the contractor shall have removed from the premises on which the work shall be executed all scaffolding, surplus materials, rubbish and all huts and

(Seal & Signature of Tenderer)

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

sanitary arrangements required for his/their work people on the site in connection with the execution of the works as shall have been erected or constructed by the contractor(s) and cleaned off the dirt from all wood work, doors, windows, walls, floor or other parts of the building, in, upon, or about which the work is to be executed or of which he may have had possession for the purpose of execution thereof, and not until the work shall have been measured by the Engineer-in-Charge. If the contractor shall fail to comply with the requirements of this clause as to removal of scaffolding, surplus materials and rubbish and all huts and sanitary arrangements as aforesaid and cleaning off dirt on or before the date fixed for the completion of work, the Engineer-in-Charge may at the expense of the contractor remove such scaffolding surplus materials and rubbish etc. and dispose of the same as he thinks fit and clean off such dirt as aforesaid, and the contractor shall have no claim in respect of scaffolding or surplus materials as aforesaid except for any sum actually realised by the sale thereof.

CLAUSE 8A

Contractor to
Keep Site Clean

When the annual repairs and maintenance of works are carried out, the splashes and droppings from white washing, color washing, painting etc. on walls, floor, windows etc. shall be removed and the surface cleaned simultaneously with the completion of these items of work in the individual rooms, quarters or premises etc. where the work is done without waiting for the actual completion of all the other items of work in the contract. In case the contractor fails to comply with the requirements of this clause, the Engineer-in-Charge shall have the right to get this work done at the cost of the contractor either departmentally or through any other agency. Before taking such action, the Engineer-in-Charge shall give ten days notice in writing to the contractor.

CLAUSE 8 B

Completion Plans
to be Submitted
by the Contractor

The contractor shall submit completion plan as required vide General Specifications for Electrical works (Part-I internal) 1972 and (Part-II External) 1974 as applicable within thirty days of the completion of the work.

In case, the contractor fails to submit the completion plan as aforesaid, he shall be liable to pay a sum equivalent to 2.5% of the value of the work subject to a ceiling of Rs. 15,000 (Rs. Fifteen thousand only) as may be fixed by the Superintending Engineer/Chief Consultant(Technical) concerned and in this respect the decision of the Superintending Engineer/ Chief Consultant (Technical) shall be final and binding on the contractor.

CLAUSE 9

Payment of
Final Bill

The final bill shall be submitted by the contractor in the same manner as specified in interim bills within three months of physical completion of the work or within one month of the date of the final certificate of completion furnished by the Engineer-in-Charge whichever is earlier. No further claims shall be made by the contractor after submission of the final bill and these shall be deemed to have been waived and extinguished. Payments of those items of the bill in respect of which there is no dispute and of items in dispute, for quantities and rates as approved by Engineer-in-Charge, will, as far as possible be made within the period specified herein under, the period being reckoned from the date of receipt of the bill by the Engineer-in-Charge or his authorized Assistant Engineer, complete with account of materials issued by the Department and dismantled materials.

i) If the Tendered value of work is up to Rs. 1 crores : 2 months

ii) If the Tendered value of work exceeds Rs. 1 crores : 4 months

(Seal & Signature of Tenderer)



Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Rmr

CLAUSE 9 A

Payment of Contractor's Bills to Banks

Payments due to the contractor may, if so desired by him, be made to his bank instead of direct to him provided that the contractor furnishes to the Engineer-in-Charge (1) an authorisation in the form of a legally valid document such as a power of attorney conferring authority on the bank to receive payments and (2) his own acceptance of the correctness of the amount made out as being due to him by Corporation or his signature on the bill or other claim preferred against Corporation before settlement by the Engineer-in-Charge of the account or claim by payment to the bank. While the receipt given by such banks shall constitute a full and sufficient discharge for the payment, the contractor shall wherever possible present his bills duly receipted and discharges through his bankers.

Nothing herein contained shall operate to create in favour of the bank any rights or equities vis-a-vis the Governor of Bihar.

CLAUSE 10

Materials supplied by Corporation

Materials which the Corporation will supply in rare case are shown in schedule 'B' which also stipulates quantum, place of issue and rate(s) to be charged in respect thereof. The contractor shall be bound to procure them from the Engineer-in-Charge.

As soon as the work is awarded, the contractor shall finalise the programme for the completion of work as per clause 5 of this contract and shall give his estimates of materials required on the basis of drawings/or schedule of quantities of the work. The Contractor shall give in writing his requirement to the Engineer-in-Charge which shall be issued to him keeping in view the progress of work as assessed by the Engineer-in-Charge, in accordance with the agreed phased programme of work indicating monthly requirements of various materials. The contractor shall place his indent in writing for issue of such materials at least 7 days in advance of his requirement.

Such materials shall be supplied for the purpose of the contract only and the value of the materials so supplied at the rates specified in the aforesaid schedule shall be set off or deducted, as and when materials are consumed in items of work (including normal wastage) for which payment is being made to the contractor, from any sum then due or which may therefore become due to the contractor under the contract or otherwise or from the security deposit. At the time of submission of bills the contractor shall certify that balance of materials supplied is available at site in original good condition.

The contractor shall submit along with every running bill (on account or interim bill) material wise reconciliation statements supported by complete calculations reconciling total issue, total consumption and certified balance (diameter/section-wise in the case of steel) and resulting variations and reasons therefore. Engineer-in-Charge shall (whose decision shall be final and binding on the contractor) be within his rights to follow the procedure of recovery in clause 42 at any stage of the work if reconciliation is not found to be satisfactory.

The contractor shall bear the cost of getting the material issued, loading, transporting to site, unloading, storing under cover as required, cutting assembling and joining the several parts together as directed by the engineer-in-charge. Notwithstanding anything to the contrary contained in any other clause of the contract and (or the PWD Code) all stores/materials so supplied to the contractor or procured with the assistance of the Corporation shall remain the absolute property of the Corporation and the contractor shall be the trustee of the stores/materials, and the said stores/materials shall not be removed/disposed off from the site of the work on any account and shall be at all times open to inspection by the Engineer-in-Charge or his authorized agent. Any such stores/materials remaining unused shall be returned to the Engineer-in-Charge in as good a condition in which they were originally supplied at a required rate, but in case it is


(Seal & Signature of Tenderer)

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

decided not to take back the stores/materials the contractor shall have no claim for compensation on any account of such stores/materials so supplied to him as aforesaid and not used by him or for any wastage in or damage to in such stores/materials.

On being required to return the stores/materials, the contractor shall hand over the stores/materials on being paid or credited such price as the Engineer-in-Charge shall determine, having due regard to the condition of the stores/materials. The price allowed for credit to the contractor, however, shall be at the prevailing market rate not exceeding the amount charged to him, excluding the storage charge, if any. The decision of the Engineer-in-Charge shall be final and conclusive. In the event of breach of the aforesaid condition, the contractor shall in addition to the throwing himself open to account for contravention of the terms of the licences or permit and/or for criminal breach of trust, be liable to the Corporation for all advantages or profits resulting or which in the usual course would have resulted to him by reason or such breach. Provided that the contractor shall in no case be entitled to any compensation or damages on account of any delay in supply or non-supply thereof all or any such materials and stores provided further that the contractor shall be bound to execute the entire work if the materials are supplied by the Corporation within the original scheduled time for completion of the work plus 50% thereof or schedule time plus 6 months whichever is more if the time of completion of work exceeds 12 months but if a part of the materials only has been supplied within the aforesaid period then the contractor shall be bound to do so much of the work as may be possible with the materials and stores supplied in the aforesaid period. For the completion of the rest of the work, the contractor shall be entitled to such extension of time as may be determined by the Engineer-in-Charge whose decision in this regard shall be final and binding on the contractor.

The contractor shall see that only the required quantities of materials are got issued. Any such material remaining unused and in perfectly good/original condition at the time of completion or determination of the contract shall be returned to the Engineer-in-Charge at the stores from which it was issued or at a place directed by him by a notice in writing. The contractor shall not be entitled for loading, transporting, unloading and stacking of such unused material except for the extra lead, if any involved, beyond the original place of issue. Quantities issued in excess of requirement with respect to work done and not returned back to the department, recovery will be made of double of issue rate.

CLAUSE 10 A

Materials to
be provided
by the
Contractor

The contractor shall, at his own expense, provide all materials, required for the works other than those, which are stipulated, to be supplied by the Corporation.

The contractor shall, at his own expense and without delay, supply to the Engineer-in-Charge samples of materials to be used on the work and shall get these approved in advance. All such materials to be provided by the Contractor shall be in conformity with the specifications laid down or referred to in the contract. The contractor shall, if requested by the Engineer-in-Charge furnish proof, to the satisfaction of the Engineer-in-Charge that the materials so comply. The Engineer-in-Charge shall within fifteen days of supply of samples or within such further period as he may require intimate to the Contractor in writing whether sample are approved by him or not. If samples are not approved, the Contractor shall forthwith arrange to supply to the Engineer-in-Charge for his approval fresh samples complying with the specifications laid down in the contract. When materials are required to be tested in accordance with specifications, approval of the Engineer-in-Charge shall be issued after the test results are received.

The Contractor shall at his risk and cost submit the samples of materials to be tested or analysed and shall not make use of or incorporate in the work any materials

(Seal & Signature of Tenderer)

[Handwritten Signature]

Chief Engineer
B.S.E.I.D.C. Ltd, Patna
[Initials]

represented by the samples until the required tests or analysis have been made and materials finally accepted by the Engineer-in-Charge. The Contractor shall not be eligible for any claim or compensation either arising out of any delay in the work or due to any corrective measures required to be taken on account of and as a result of testing of materials.

The contractor shall, at his risk and cost, make all arrangements and shall provide all facilities as the Engineer-in-Charge may require for collecting, and preparing the required number of samples for such tests at such time and to such place or places as may be directed by the Engineer-in-Charge and bear all charges and cost of testing unless specifically provided for otherwise elsewhere in the contract or specifications. The Engineer-in-Charge or his authorized representative shall at all time have access to the works and to all workshops and places where work is being prepared or from where materials, manufactured articles or machinery are being obtained for the works and the contractor shall afford every facility and every assistance in obtaining the right to such access.

The Engineer-in-Charge shall have full powers to require the removal from the premises of all materials which in his opinion are not in accordance with the specifications and in case of default the Engineer-in-Charge shall be at liberty to employ at the expense of the contractor, other persons to remove the same without being answerable or accountable for any loss for damage that may happen or arise to such materials. The Engineer-in-Charge shall also have full powers to require other proper materials to be substituted thereof and in case of default the Engineer-in-Charge may cause the same to be supplied and all costs which may attend such removal and substitution shall borne by the Contractor.

CLAUSE 10 B

Secured Advance on Non-perishable Materials

i) The contractor, on signing an indenture in the form to be specified by the Engineer-in-Charge, shall be entitled to be paid during the progress of the execution of the work up to 75% of the assessed value of any materials which are in the opinion of the Superintending Engineer / Chief Consultant (Technical) of the Corporation nonperishable, non-fragile and noncombustible and are in accordance with the contract and on the site in connection therewith and are adequately stored and/or protected against damage by weather or other causes but which have not at the time of advance been incorporated in the works. When materials on account of which advance has been made under this sub-clause are incorporated in the work the amount of such advance shall be recovered/deducted from the next payment made under any or the clause or clauses of this contract.

ii) Mobilization advance not exceeding 10% of the tendered value may be given, requested by the contractor in writing within one month of the order to commence the work. In such a case the contractor shall execute a Bank Guarantee/ Bond from a Scheduled Nationalised Bank as specified by the Engineer-in-Charge for the full amount of such advance before it is released. Such advance shall be in two or more installments to be determined by the Engineer-In-charge at his absolute discretion. The first installment of such advance before shall be released by the Engineer-in-Charge to the contractor on a request made by the contractor to the Engineer-in-Charge in this behalf. The second and subsequent installment shall be released by the Engineer-in-Charge only after the contractor furnishes proof of the satisfactory utilisation of the earlier installment to the entire satisfaction of the Engineer-In-Charge.

Plant & Machinery & Shuttering Material Advance

iii) An advance for plant machinery required for the work and brought to site by the Contractor may be given if requested by the contractor in writing within one month of bringing such plant and machinery to site. Such advance shall be given on such plant and machinery which in the opinion of the Engineer-in-Charge will add to the

(Seal & Signature of Tenderer)

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

expeditious execution of work and improve the quality of work. The amount of advance shall be restricted to 5% of the tender value. In the case of new plant and equipment to be purchased for the work the advance shall be restricted to 85% of the price of such new plant and equipment paid by the contractor for which the contractor shall produce evidence satisfactory to the Engineer-in-Charge and approval from Engineer-in-Charge. In the case of second hand and used plants and equipment, the amount of such advance shall be limited to 50% of the depreciated value of plant and equipment as may be decided by the Engineer-in-Charge. The contractor shall, if so required by the Engineer-in-Charge, submit the statement value of such old plant and equipment duly approved by a Registered Valuer recognized by the Central Board of Direct Taxes under the Income-Tax Act, 1961. No such advance shall be paid on any plant and equipment of perishable nature and on the plant and equipment of a value less than Rs. 50,000/- Seventy five percent of such amount of advance shall be paid after the plant & equipment is brought to site and balance twenty five percent on successfully commissioning the same only after approval from Engineer-in-Charge.

Leasing of equipment shall be considered at par with purchase of equipment and shall be covered by tripartite agreement with the following:

1. Leasing company which gives certificate of agreeing to lease equipment to the contractor.
2. Engineer in Charge, and
3. The contractor.

This advance shall further be subject to the condition that such plant and equipment (a) are considered by the Engineer-in-Charge to be necessary for the works; (b) and are in and are maintained in working order; (c) hypothecated to the Government as specified by the Engineer-in-Charge before the payment of advance is released. The contractor shall not be permitted to remove from the site such hypothecated plant and equipment without the prior written permission of the Engineer-in-Charge. The contractor shall be responsible for maintaining such plant and equipment in good working order during the entire period of hypothecation falling which such advance shall be entirely recovered in lump sum. For this purpose steel scaffolding and from work shall be treated as plant and equipment.

The contractor shall insure the Plant and Machinery for which mobilization advance is sought and given, for a sum sufficient to provide for their replacement at site. Any amounts not recovered from the insurer will be borne by the contractor.

Interest &
Recovery

- iv) The mobilization advance and plant and machinery advance in (ii)&(iii) above bear simple interest and should be equal to the prevailing rate of interest charged by the bank as mentioned in contract date schedule 'F' and shall be calculated from the date of payment to the date of recovery, both days inclusive, on the outstanding amount of advance. Recovery of such sums advanced shall be made by the deduction from the contractor's bills commencing after first ten per cent of the gross value of the work is executed and paid, on pro-rata percentage basis to the gross value of the work billed beyond 10% in such a way that the entire advance is recovered by the time eighty per cent of the gross value of the contract is executed and paid, together with interest due on the entire outstanding amount up to the date of the installment.

(Seal & Signature of Tenderer)

[Handwritten Signature]

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

[Handwritten Signature]

- v) If the circumstances are considered reasonable by the Engineer-in-Charge, the period mentioned in (ii) and (iii) for request by the contractor in writing for grant of mobilization advance and plant and equipment advance may be extended in the discretion of the Chief Executive Officer.
- vi) The said bank guarantee for advances shall initially be made for the full amount and valid for the contract period, and be kept renewed from time to time to cover the balance amount and likely period of complete recovery together with interest.
- vii) Any materials including tools plants equipments etc brought to the site shall not be removed from the sites without the written permission of the Engineer-in-charge.

CLAUSE 10 C


**Payment on
Account of
Increase in
Prices/Wages
due to Statutory
Order(s)**

If after submission of the tender the price of any material incorporated in the works (not being a material supplied from the Engineer-in-Charge's stores in accordance with clause 10 thereof) and/or wages of labour increases as a direct result of the coming into force of any fresh law, or statutory rule or order (but not due to any changes in sales tax) and such increase in the price and/or wages prevailing at the time of the last stipulated date for receipt of the tenders including extensions if any for the work, and the contractor thereupon necessarily and properly pays in respect of that material (incorporated in the works) such increased price and/or in respect of labour engaged on the execution of the work such increased wages, then the amount of the contract shall accordingly be varied and provided further that any such increase shall not be payable if such increase has become operative after the stipulated date of completion of the work in question.

If after submission of the tender, the price of any material incorporated in the works (not being a material supplied from the Engineer-in-Charge's stores in accordance with clause 10 thereof) and/or wages of labour is decreased as a direct result of the coming into force of any law or statutory rules or order (but not due to any changes in sales tax) and such decrease in the prices and/or wages prevailing at the time of receipt of the tender for the work. The Corporation shall in respect of materials incorporated in the works (not being materials supplied from the Engineer-in-Charge's stores in accordance with Clause-10 hereof) and/or labour engaged on the execution of the work after the date of coming into force of such law statutory rule or order be entitled to deduct from the dues of the contractor such amount as shall be equivalent to the difference between the prices of the materials and/or wages as prevailed at the time of the last stipulated date for receipt of tenders including extensions if any for the work and the price of materials and/or wages of labour on the coming into force of such law, statutory rule or order.

The contractor shall, for purpose of this condition, keep such books of account and other documents as are necessary to show the amount of any increase claimed or reduction available and shall allow inspection of the same by a duly authorised representative of the Corporation, and further shall, at the request of the Engineer-in-Charge may require any documents so kept and such other information as the Engineer-in-Charge may require.

The contractor shall, within a reasonable time of his becoming aware of any alteration in the price of any such material and/or wages of labour, give notice thereof to the Engineer-in-Charge stating that the same is given pursuant to this condition together with all information relating thereto which he may be in position to supply.


(Seal & Signature of Tenderer)


25-6-2014
Chief Engineer
B.S.E.I.D.C. Ltd, Patna

CLAUSE 10 CA

Payment on
Account of
Increase/decrease
in Prices of
construction
materials after
receipt of
tender.

If after submission of the tender, the price of cement or steel reinforcement bars / bitumen incorporated in the works (not being a material supplied from the Engineer-in-Charge's stores in accordance with Clause 10 thereof) increase(s) beyond the price(s) prevailing at the time of the last stipulated date for receipt of tenders (including extensions, if any) for the work, then the amount of the contract shall accordingly be varied and provided further that any such increase shall not be payable if such increase has become operative after the stipulated date of completion of work in question.

If after submission of the tender, the prices of cement and/or steel reinforcement bars / bitumen incorporated in the works (not being a material stipulated from the Engineer-in-Charge's stores in accordance with the Clause 10 thereof) is decreased, Corporation shall in respect of these materials incorporated in the works (not being materials supplied from the Engineer-in-Charge's stores in accordance with Clause 10 thereof) be entitled to deduct from the dues of the contractor such amount as shall be equivalent to the difference between the prices of Cement and/or Steel reinforcement bars/ bitumen as prevailed at the time of last stipulated date for receipt of tenders including extensions if any for the work and the prices of these materials on the coming into force of such base price of cement and/or steel reinforcement bars/ bitumen issued under authority of Schedule of Rate Committee.

The increase/decrease in prices shall be determined by the All India Wholesale Price Indices for Cement and Steel (bars and rods) as published by Economic Advisor to Government of India, Ministry of Commerce and Industry and base price for cement and/or steel reinforcement bars / bitumen as issued under authority of Schedule of Rate Committee as valid on the last stipulated date of receipt of tender, including extension if any and for the period under consideration.

The amount of the contract shall accordingly be varied for cement or steel reinforcement bars / bitumen and will be worked out as per the formula given below:-

Adjustment for cement component

- (i) Price adjustment for increase or decrease in the cost of cement procured by the contractor shall be paid in accordance with the following formula:

$$V_0 = 0.85 \times P_c / 100 \times R \times (C_1 - C_0) / C_0$$

V_0 = increase or decrease in the cost of work during the month under consideration due to changes in rates for cement.

R = Value of the work.

C_0 = The all India wholesale price index for cement on 28 days preceding the date of opening of Bids as published by the Ministry of Industrial Development, Government of India, New Delhi.

C_1 = The all India average wholesale price index for cement for the month under consideration as published by Ministry of Industrial Development, Government of India, New Delhi.

P_c = Percentage of cement component of the work.

Adjustment for Steel component

- (ii) Price adjustment for increase or decrease in the cost of steel procured by the Contractor shall be paid in accordance with the following formula:

$$V_s = 0.85 \times P_s / 100 \times R \times (S_1 - S_0) / S_0$$

(Seal & Signature of Tenderer)

31/07/2014

Chief Engineer,
B.S.E.I.D.C. Ltd, Patna

25-6-2014

V_s = Increase or decrease in the cost of work during the month under consideration due to changes in the rates for steel.

S_0 = The all India wholesale price index for steel (Bars and Rods) on 28 days preceding the date of opening of Bids as published by the Ministry of Industrial Development, Government of India New Delhi.

S_1 = The all India average wholesale price index for steel (Bars and Rods) for the month under consideration as published by Ministry of Industrial Development, New Delhi.

P_s = Percentage of Steel component of the work.

Note : For the application of this clause, index of Bars and Rods has been chosen to represent steel group.

Adjustment of bitumen component

(iii) Price adjustment for increase or decrease in the cost of bitumen shall be paid in accordance with the following formula:

$$V_b = 0.85 \times P_b / 100 \times R \times (B_1 - B_0) / B_0$$

V_b = Increase or decrease in the cost of work during the month under consideration due to changes in rates for bitumen.

B_0 = The office retail price of bitumen at the IOC depot at nearest center on the day 28 days prior to date of opening of Bids.

B_1 = The official retail price of bitumen of IOC depot at nearest center for the 15th day of the month under consideration.

P_b = Percentage of bitumen component of the work.

CLAUSE 10 CC

Payment due to increase / Decrease in Prices / Wages after receipt of tender (Time of completion more than 18 months) Contract price shall be adjusted for increase or decrease in rates and price of labour, materials, fuels and lubricants in accordance with the following principles and procedures and as per formula given in the contract data :

(a) The price adjustment shall apply for the work done from the start date given in the contract data upto end of the initial intended completion date or extensions granted by the Engineer and shall not apply to the work carried out beyond the stipulated time for reasons attributable to the contractor.

(b) Following expressions and meanings are assigned to the work done during each month:

R = Total value of work done during the month. It would include the amount of secured advance granted, if any, during the month, less the amount of secured advance recovered, if any during the month. It will exclude value for works executed under variations for which price adjustment will be worked separately based on the terms mutually agreed.


(c) To the extent that full compensation for any rise or fall in costs to the contractor is not covered by the provisions of this or other clauses in the contract, the unit rates and prices included in the contract shall be deemed to include amounts to cover the contingency of such other rise or fall in costs.

The formula (e) for adjustment of prices are:

Adjustment for labour component

(i) Price adjustment for increase or decrease in the cost due to labour shall be paid in accordance with the following formula:


(Seal & Signature of Tenderer)


Chief Engineer
B.S.E.I.D.C. Ltd, Patna.
Rmb

$$V_L = 0.85 \times P_1/100 \times R \times (L_1 - L_0)/L_0$$

V_L = increase or decrease in the cost of work during the month under consideration due to changes in rates for local labour.

L_0 = the consumer price index for industrial workers for the State on 28 days preceding the date of opening of Bids as published by Labour Bureau, Ministry of Labour, Government of India.

L_1 = The consumer price index for industrial workers for the State for the under consideration as published by Labour Bureau, Ministry of Labour, Government of India.

P_1 = Percentage of labour component of the work.

Adjustment for cement component

(ii) Price adjustment for increase or decrease in the cost of cement procured by the contractor shall be paid in accordance with the following formula:

$$V_0 = 0.85 \times P_0/100 \times R \times (C_1 - C_0)/C_0$$

V_0 = increase or decrease in the cost of work during the month under consideration due to changes in rates for cement.

C_0 = The all India wholesale price index for cement on 28 days preceding the date of opening of Bids as published by the Ministry of Industrial Development, Government of India, New Delhi.

C_1 = The all India average wholesale price index for cement for the month under consideration as published by Ministry of Industrial Development, Government of India, New Delhi.

P_c = Percentage of cement component of the work.

Adjustment for Steel component

(iii) Price adjustment for increase or decrease in the cost of steel procured by the Contractor shall be paid in accordance with the following formula:

$$V_s = 0.85 \times P_s/100 \times R \times (S_1 - S_0)/S_0$$

V_s = Increase or decrease in the cost of work during the month under consideration due to changes in the rates for steel.

S_0 = The all India wholesale price index for steel (Bars and Rods) on 25 days preceding the date of opening of Bids as published by the Ministry of Industrial Development, Government of India New Delhi.

S_1 = The all India average wholesale price index for steel (Bars and Rods) for the month under consideration as published by Ministry of Industrial Development, New Delhi.

P_1 = Percentage of labour component of the work.

Note : For the application of this clause, index of Bars and Rods has been chosen to represent steel group.

Adjustment of bitumen component

(iv) Price adjustment for increase or decrease in the cost of bitumen shall be paid in accordance with the following formula:

$$V_b = 0.85 \times P_b/100 \times R \times (B_1 - B_0)/B_0$$

V_b = Increase or decrease in the cost of work during the month under consideration due to changes in rates for bitumen.

(Seal & Signature of Tenderer)

31/07/2014

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

25-6-2014

B_0 = The office retail price of bitumen at the IOC depot at nearest center on the day 28 days prior to date of opening of Bids.

B_1 = The official retail price of bitumen of IOC depot at nearest center for the 15th day of the month under consideration.

P_1 = Percentage of bitumen component of the work.

Adjustment of POL (fuel and lubricant) component

(v) Price adjustment for increase or decrease in the cost of POL (fuel and lubricant) shall be paid in accordance with the following formula.

$$V_f = 0.85 \times P_f / 100 \times R \times (F_1 - F_0) / F_0$$

V_f = Increase or decrease in the cost of work during the month under consideration due to changes in rates for fuel and lubricants.

F_0 = The official retail price of High Speed Diesel (HSD) at the existing consumer pumps of IOC at nearest center on the day 28 days prior to the date of opening of Bids.

F_1 = The official retail price of HSD at the existing consumer pumps of IOC at nearest center for the 15th day of month of the under consideration.

P_1 = Percentage of fuel and lubricants component of the work.

Note : For the application of this clause, the price of High Speed Diesel oil has been chosen to represent fuel and lubricants group.

Adjustment for Plant and Machinery Spares component

(vi) Price adjustment for increase or decrease in the cost of plant and machinery spares procured by the Contractor shall be paid in accordance with the following formula :

$$V_p = 0.85 \times P_p / 100 \times R \times (P_1 - P_0) / P_0$$

V_p = Increase or decrease in the cost of work during the month under consideration due to changes in rates for plant and machinery spares.

P_0 = The all India wholesale price index for heavy machinery and parts on 28 days preceding the date of opening of Bids as published by the Ministry of Industrial Development Government of India, New Delhi.

P_1 = The all India average wholesale price index for heavy machinery and parts for the month under consideration as published by Ministry of Industrial Development, Government of India, New Delhi.

P_1 = Percentage of plant and machinery spares component of the work.

Note : For the application of this clause, index of Heavy Machinery and Parts has been chosen to represent the Plant and Machinery Spares group.

Adjustment of other materials component

(vii) Price adjustment for increase or decrease in cost of local materials other than cement, steel, bitumen and POL procured by the contractor shall be paid in accordance with the following formula:

$$V_m = 0.85 \times P_m / 100 \times R \times (M_1 - M_0) / M_0$$

V_m = Increase or decrease in the cost of work during the month under consideration due to changes in rates for local materials other than cement, steel, bitumen and POL.

M_0 = The all India wholesale price index (all commodities) on 28 days preceding the date of opening of Bids, as published by the Ministry of Industrial Development, Government of India, New Delhi.


(Seal & Signature of Tenderer)

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

M_1 = The all India wholesale price index (all commodities) for the month under consideration as published by Ministry of Industrial Development, Government of India, New Delhi.

P_1 = Percentage of local material component (other than cement, steel, bitumen and POL) of the work.

The following percentages will govern the price adjustment for the entire contract:

1.	Labour - P_1	25 %
2.	Cement - P_c	5 %
3.	Steel - P_s	5 %
4.	Bitumen - P_b	10 %
5.	POL - P_f	5 %
6.	Plant & Machinery Spares - P_p	5 %
7.	Other materials - P_m	45 %
		Total 100%

(viii) In contract where clause 10CA is applicable, this clause 10CC will not be applicable and in contract where this clause 10CC is applicable previous clause 10CA will not be applicable.

CLAUSE 10 D

Dismantled Material Govt. Property The contractor shall treat all materials obtained during dismantling of a structure, excavation of the site for a work, etc. as Employer's property and such materials shall be disposed off to the best advantage of Employer according to the PWD codal provision.

CLAUSE 11

Work to be Executed in Accordance with Specifications, Drawings, Orders etc. The contractor shall execute the whole and every part of the work in the most substantial and workmanlike manner both as regards materials and otherwise in every respect in strict accordance with the specifications. The contractor shall also conform exactly, fully and faithfully to the design, drawings and instructions in writing in respect of the work signed by the Engineer-in-Charge and the contractor shall be furnished free of charge one copy of the contract documents together with specification, designs, drawings and instruction as are not included in the standard specifications of Public Works Department specified in Schedule 'F' or in any Bureau of Indian Standard or any other, published standard or code or, Schedule of Rates or any other printed publication referred to elsewhere in the contract.

The contractor shall comply with the provisions of the contract and with the care and diligence execute and maintain the works and provide all labour and materials, tools and plants including for measurements and supervision of all works, structural plans and other things of temporary or permanent nature required for such execution and maintenance in so far as the necessity for providing these, is specified or is reasonably inferred from the contract. The Contractor shall take full responsibility for adequacy, suitability and safety of all the works and methods of construction.

CLAUSE 12

Deviations/ Variations Extent and Pricing The Engineer-in-Charge (As per codal provision) shall have power (i) to make alternation in, omissions from, additions to, or substitutions for the original specifications, drawings, designs and instructions that may appear to him to be necessary or advisable during the progress of the work, and (ii) to omit a part of the works in case of non-availability of a portion of the site or for any other reasons and the contractor shall be bound to carry out the works in accordance with any instructions given to him in writing signed by the Engineer-in-Charge after approval from competent authority, and such alterations

(Seal & Signature of Tenderer)

[Signature]

Chief Engineer
B.S.E.I.D.C. Ltd, Patna
[Signature]

omissions, additions or substitutions shall form part of the contract as if originally provided therein and any altered, additional or substituted work which the contractor may be directed to do in the manner specified above as part of the works, shall be carried out by the contractor on the same conditions in all respects including price on which he agreed to do the main work except as hereafter provided.

12.1 The time for completion of the works shall, in the event of any deviations resulting in additional cost over the tendered value sum being ordered, be extended, if requested by the contractor, as follows :

- i) In the proportion which the additional cost of the altered, additional or substituted work, bears to the original tendered value plus.
- ii) 25% of the time calculated in (i) above or such further additional time as may be considered reasonable by the Engineer-in-Charge after approval from competent authority

12.2 In the case of extra item(s) the contractor may within fifteen days of receipt of order or occurrence of the item(s) claim rates, supported by proper analysis, for the work and the Engineer-in-Charge after approval from competent authority shall within one month of the receipt of the claims supported by analysis, after giving consideration to the analysis of the rates submitted by the contractor, determine the rates as per power delegated in PWD Code and on the basis of the market rates and the contractor shall be paid in accordance with the rates so determined.

**Deviation,
Extra items
and Pricing**

In the case of substituted items, the rate for the agreement item (to be substituted) and substituted item shall also be determined in the manner as mentioned in the aforesaid para.

**Deviation,
Substituted
Items, Pricing**

- (a) If the market rate for the substituted item so determined is more than the market rate of the agreement item (to be substituted) the rate payable to the contractor for the substituted item shall be the rate for the agreement item (to be substituted) so increased to the extent of the difference between the market rates of substituted item and the agreement item (to be substituted).
- (b) If the market rate for the substituted item so determined is less than the market rate of the agreement item (to be substituted) the rate payable to the contractor for the substituted item shall be the rate for the agreement item (to be substituted) so decreased to the extent of the difference between the market rates of substituted item and the agreement item (to be substituted).

**Deviation,
Deviated
Quantities,
Pricing**

In the case of contract items, substituted items, contract cum substituted items, which exceed the limits laid down in Schedule F, the contractor may within fifteen days of receipt of order or occurrence of the excess, claim revision of the rates, supported by proper analysis, for the work in excess of the above mentioned limits, provided that if the rates so claimed are in excess of the rates specified in the schedule of quantities the Engineer-in-Charge shall within one month of receipt of the claims supported by analysis, after giving consideration to the analysis of the rates submitted by the contractor, determine the rates as per power delegated in PWD Code and on the basis of the market rates and the contractor shall be paid in accordance with the rates so determined.

12.3 The provisions of the preceding paragraph shall also apply to the decrease in the rates of items for the work in excess of the limits laid down in Schedule 'F' and the Engineer-in-Charge shall after giving notice to the contractor within one month of occurrence of the excess and after taking into consideration any reply received from him within fifteen days of receipt of the notice, revise the rates as per power delegated in PWD Code for the work

(Seal & Signature of Tenderer)

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

in question within one month of expiry of the said period of fifteen days having regard to the market rates or current schedule of rate.

12.4 The contractor shall send to the Engineer-in-Charge once every three months an up to date account giving complete details of all claims for additional payments to which the contractor may consider himself entitled and of all additional work ordered by the Engineer-in-Charge after approval from competent authority which he has executed during the preceding quarter failing which the contractor shall be deemed to have waived his right. However, the Superintending Engineer / Chief Consultant (Technical) is authorized for consideration of such claims on merits.

12.5 For the purpose of operation of Schedule 'F' the following works shall be treated as works relating to foundation :

- i) For buildings, compound walls plinth level or 1.2 meters (4 feet) above ground level whichever is lower excluding items of flooring and D.P.C. but including base concrete below the floors.
- ii) For abutments, piers, retaining walls of culverts and bridges, walls of water reservoirs the bed of floor level.
- iii) For retaining walls where floor level is not determinate 1.2 meters above the average ground level or bed level.
- iv) For Roads all items of excavation and filling including treatment of sub-base.

12.6 Any operation incidental to or necessary has to be in contemplation of tenderer while filing tender, or necessary for proper execution of the item included in the Schedule of quantities or in the schedule of rates mentioned above, whether or not, specifically indicated in the description of the item and the relevant specifications, shall be deemed to be included in the rates quoted by the tenderer or the rate given in the said schedule of rates, as the case may be. Nothing extra shall be admissible for such operations.

CLAUSE 13

Foreclosure of Contract due to Abandonment or Reduction in Scope of Work

If at any time after acceptance of the tender, Corporation shall decide to abandon or reduce the scope of the works for any reason whatsoever and hence not require the whole or any part of the works to be carried out, the Engineer-in-Charge shall give notice in writing to that effect to the contractor and the contractor shall act accordingly in the matter. The contractor shall have no claim to any payment of compensation or otherwise whatsoever, on account of any profit or advantage which he might have derived from the execution of the works in full but which he did not derive in consequence of the foreclosure of the whole or part of the works.

The contractor shall be paid at contract rates for works executed at site only.

CLAUSE 14

Cancellation of contract in full or part

If the contractor :

- i) at any time makes default in proceeding with the works or any part of the work with due diligence and continues to do so after a notice in writing of 7 days from the Engineer-in-Charge; or
- ii) Commits default to comply with any of the terms and conditions of the contract and does not remedy it or take effective steps to remedy it within 7 days after a notice in writing is given to him in that behalf by the Engineer-in-Charge; or
- iii) Fails to complete the works or items of work with individual dates of completion, on or before the date(s) of completion, and does not complete them within the period specified in a notice given in writing in that behalf by the Engineer-in-Charge; or

(Seal & Signature of Tenderer)

Signature of Tenderer

25-6-2014
Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Signature

- iv) Shall offer or give or agree to give to any person in Government / Corporation service or to any other person on his behalf any gift or consideration of any kind as an inducement or reward for doing or forbearing to do or for having done or forborne to do any act in relation to the obtaining or execution of this or any other contract for Government / Corporation; or
- v) Shall enter into a contract with Corporation in connection with which commission has been paid or agreed to be paid by him or to his knowledge, unless the particulars of any such commission and the terms of payment thereof have been previously disclosed in writing to the Accepting Authority/Engineer-in-Charge; or
- vi) Shall obtain a contract with Corporation as a result of wrong tendering or other non-bonafide methods of competitive tendering; or
- vii) Being an individual, or if a firm, any partner thereof shall at any time be adjudged insolvent or have a receiving order or order for administration of his estate made against him or shall take any proceedings for liquidation or composition (other than a voluntary liquidation for the purpose of amalgamation or reconstruction) under any Insolvency Act for the time being in force or make any conveyance or assignment of his effects or composition or arrangement for the benefit of his creditors or purport so to do, or if any application be made under any Insolvency Act for the time being in force for the sequestration of his estate or if a trust deed be executed by him for benefit of his creditors; or
- viii) Being a company, shall pass a resolution or the Court shall make an order for the winding up of the company, or a receiver or manager on behalf of the debenture holders or otherwise shall be appointed or circumstances shall arise which entitle the Court or debenture holders to appoint a receiver or manager; or
- ix) Shall suffer an execution being levied on his goods and allow it to be continued for a period of 21 days; or
- x) Assigns, transfers, sublets (engagement of labour on a piece-work basis or of labour with materials not to be incorporated in the work, shall not be deemed to be subletting) or otherwise parts with or attempts to assign, transfer sublet or otherwise parts with the entire works or any portion thereof without the prior written approval of the Competent Authority;


The Competent Authority may, without prejudice to any other right or remedy which shall have accrued or shall accrue hereafter to Government, by a notice in writing to cancel the contract as a whole or only such items of work in default from the Contract.

The Engineer-in-Charge shall on such cancellation by the Competent Authority have powers to :

- (a) Take possession of the site and any materials, constructional plant, implements, stores, etc., thereon; and/or
- (b) Carry out the incomplete work by any means at the risk and cost of the contractor.

On cancellation of the contract in full or in part, the Engineer-in-Charge shall determine what amount, if any, is recoverable from the contractor for completion of the works or part of the works or in case the works or part of the works is not to be completed, the loss of damage suffered by Corporation. In determining the amount, credit shall be given to the contractor for the value of the work executed by him up to the time of cancellation, the value of contractor's materials taken over and incorporated in the work and use of plant and machinery belonging to the contractor.

Any excess expenditure incurred or to be incurred by the Corporation in completing the works or part of the works or the excess loss or damages suffered or which may be


(Seal & Signature of Tenderer)


Chief Engineer
B.S.E.I.D.C. Ltd, Patna

suffered by the Corporation as aforesaid after allowing such credit shall without prejudice to any other right or remedy available to the Corporation in law be recovered from any moneys due to the contractor on any account, and if such moneys are not sufficient the contractor shall be called upon in writing and shall be liable to pay the same within 31 days.

If the contractor fails to pay the required sum within the aforesaid period of 30 days the Engineer-in-Charge shall have the right to sell any or all of the contractors unused materials, constructional plant, implements, temporary buildings, etc. and apply the proceeds of sale thereof towards the satisfaction of any sums due from the contractor under the contract and if thereafter there be any balance is outstanding from the contractor, it shall be recovered in accordance with the provisions of the contract.

Any sums in excess of the amounts due to Employer and unsold materials, constructional plant, etc., shall be returned to the contractor, provided always that if cost or anticipated cost of completion by the Corporation of the works or part of the works is less than the amount which the contractor would have been paid had he completed the works or part of the works, such benefit shall not accrue to the contractor.

CLAUSE 15

Suspension of Work

i) The contractor shall, on receipt of the order in writing of the Engineer-in-Charge (whose decision shall be final and binding on the contractor) suspend the progress of the works or any part thereof for such time and in such manner as the Engineer-in-Charge may consider necessary so as not to cause any damage or injury to the work already done or endanger the safety thereof, for any of the following reasons :

- a) on account of any default on the part of the contractor or;
- b) for proper execution of the works or part thereof for reasons other than the default of the contractor; or
- c) for safety of the works or part thereof.

The contractor shall, during such suspension, properly protect and secure the works to the extent necessary and carry out the instructions given in that behalf by the Engineer-in-Charge.

ii) If the suspension is ordered for reasons (b) and (c) in sub-para (i) above, the contractor shall be entitled to an extension of time equal to the period of every such suspension PLUS 25%, for completion of the item or group of items of work for which a separate period of completion is specified in the contract and of which the suspended work forms a part, and;

CLAUSE 16

Action in case Work not done as per Specifications

All works under or in course of execution or executed in pursuance of the contract shall at all times be open and accessible to the inspection and supervision of the Engineer-in-Charge, his authorised subordinates in charge of the work and all the superior officers, officer of the Quality Control Organisation of the Corporation and of the Cabinet (Technical) Vigilance, and the contractor shall, at all times, during the usual working hours and at all other times at which reasonable notice of the visit of such officers has been given to the contractor, either himself be present to receive orders and instructions or have a responsible agent duly accredited in writing, present for that purpose. Orders given to the Contractor's agent shall be considered to have the same force as if they had been given to the contractor himself.

If it shall appear to the Engineer-in-Charge or his higher authority or his authorised subordinates in charge of the work or to the Cabinet (Technical) Vigilance or his subordinate officers, that any work has been executed with unsound, imperfect, or unskillful workmanship, or with materials or article provides by him for the execution of

the work which are unsound or of a quality inferior to that contracted or otherwise not in accordance with the contract the contractor shall, on demand in writing which shall be made within the period specified in schedule – F of contract data from the Engineer-in-Charge specifying the work, materials or articles complained of notwithstanding that the same may have been passed, certified and paid for forthwith rectify, or remove and reconstruct the work so specified in whole or in part, as the case may require or as the case may be, remove the materials or articles so specified and provide other proper and suitable materials or articles at his own charge and cost. In the event of the contractor failing to do so within a period specified by the Engineer-in-Charge in his demand aforesaid, then the contractor shall be liable to pay compensation at the same rate as under clause 2 of the contract (for non-completion of the work in time) for this default.

In such case the Engineer-in-Charge may not accept the item of work at the rate applicable under the contract but may accept such items at reduced rates as the competent authority may consider reasonable during the preparation of an account bill or final bill if the item is so acceptable without detriment to the safety and utility of the item and the structure and incidental items rectified, or removed and re-executed at the risk and cost of contractor. Decision of the Engineer-in-Charge to be conveyed in writing in respect of the same will be final and binding on the contractor.

CLAUSE 17

**Contractor
Liable for
Damages,
defects during
maintenance
period**

If the contractor or his working people or servants shall break, deface, injure or destroy any part of building in which they may be working, or any building, road, road curb, fence, enclosure, water pipe, cables, drains, electric or telephone post or wired, trees, grass or grassland, or cultivated ground contiguous to the premises on which the work or any part is being executed, or if any damage shall happen to the work while in progress, from any cause whatever or if any defect, shrinkage or other faults appear in the work within defect liability period after a certificate final or otherwise of its completion shall have been given by the Engineer-in-Charge as aforesaid arising out of defect or improper materials or workmanship the contractor shall upon receipt of a notice in writing on that behalf make the same good at his own expense or in default the Engineer-in-Charge cause the same to be made good by other workmen and deduct the expense from any sums that may be due or at any time thereafter may become due to the contractor, or from his security deposit except for the portion pertaining to asphaltic work which is governed by sub-para (iii) of clause 35 or the proceeds of sale thereof or of a sufficient portion thereof. The security deposit of the contractor shall not be refunded before the expiry of defect liability period after the issue of the certificate final or otherwise, of completion of work, or till the final bill has been prepared and passed whichever is later.

In case of Maintenance and Operation works of Electrical & Mechanical services, the security deposit deducted from contractors shall be refunded within one month from the date of final payment or within one month from the date of completion of the maintenance contract whichever is earlier.

CLAUSE 18

**Contractor to
Supply Tools &
Plants etc.**

The contractor shall provide at his own cost all materials (except such special materials if any, as may in accordance with the contract be supplied from the Engineer-in-Charge's stores), plant, tools, appliances, implements, ladders, cordage, tackle, scaffolding and temporary works required for the proper execution of the work, whether original, altered or substituted and whether included in the specification or other document forming part of the contract or referred to in these conditions or not, or which may be necessary for the purpose of satisfying or complying with the requirements of the Engineer-in-Charge as to any matter as to which under these conditions he is


(Seal & Signature of Tenderer)

Chief Engineer
BSEIDC, Ltd, Patna
Rm

entitled to be satisfied, or which he is entitled to require together with carriage therefore to and from the work. The contractor shall also supply without charge the requisite number of persons with the means and materials, necessary for the purpose of setting out works, and counting, weighing and assisting the measurement for examination at any time and from time to time of the work or materials. Failing his so doing the same may be provided by the Engineer-in-Charge at case to the contractor, under this contract or otherwise and/or from his security deposit or the proceeds of sale thereof, or of a sufficient portions thereof.

CLAUSE 18 A

**Recovery of
Compensation
paid to Workman**

In every case in which by virtue of the provisions sub-section (1) of Section 12, of the Workmen's Compensations Act, 1923, Government is obliged to pay compensation to a workman employed by the contractor, in execution of the works, Government will recover from the contractor the amount of the compensation so paid; and without prejudice to the right of the Government under sub-section (2) of section 12, of the said Act, Government shall be at liberty to recover such amount or any part thereof by deducting it from the security deposit or from any sum due by Government to the contractor whether under this contract or otherwise. Government shall not be bound to contest any claim made against it under sub-section (1) Section 12, of the said Act, except on the written request of the contractor and upon his giving to Government full security for all costs for which Government might become liable in consequence of contesting such claim.

CLUASE 18 B

**Ensuring Payment
and Amenities to
Workers if
Contractor fails**

In every case in which by virtue of the provisions of the Contract Labour (Regulation and Abolition) Act, 1970, and of the Contract Labour (Regulation and Abolition) Central Rules, 1971, Government is obliged to pay any amounts of wages to a workman employed by the contractor in execution of the works, or to incur any expenditure in providing welfare and health amenities required to be provided under the above said Act and the rules under Clause 19H or under the P.W.D. Contractor's Labour Regulations, or under the Rules framed by Government from time to time for the protection of health and sanitary arrangements for workers employed by P.W.D. Contractors, Government will recover from the contractor the amount of wages so paid or the amount of expenditure so incurred; and without prejudice to the rights of the Government under sub-section (2) of Section 20, and sub-section (4) of Section 21, of the Contract Labour (Regulation and Abolition) Act, 1970, Government shall be at liberty to recover such amount or any part thereof by deducting it from the security deposit or from any sum due by Government to the contractor whether under this contract or otherwise Government shall not be bound to contest any claim made against it under sub-section (1) of Section 20, sub-section (4) of Section 21, of the said Act, except on the written request of the contractor and upon his giving to the Government full security for all costs for which Government might become liable in contesting such claim.

CLAUSE 19

**Labour Laws to
be complied by
the Contractor**

The contractor shall obtain a valid licence under the State Labour Act, and the Contract Labour (Regulation and Abolition) Central rules 1971, before the commencement of the work, and continue to have a valid license until the completion of the work. The contractor shall also abide by the provisions of the Child Labour (Prohibition and Regulation) Act, 1986.

(Seal & Signature of Tenderer)

Signature of Tenderer

25-6-2014
Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Per

The contractor shall also comply with the provisions of the building and other Construction Workers (Regulation of Employment & Conditions of Service) Act, 1996 and the building and other Construction Workers Welfare Cess Act, 1996.

Any failure to fulfill these requirements shall attract the penal provisions of the contract arising out of the resultant non-execution of the work.

CLAUSE 19 A

No labour below the prescribed age shall be employed on the work.

CLAUSE 19 B

Payment of Wages

Payment of wages :

- i) The contractor shall pay to labour employed by him either directly or through sub-contractors, wages not less than fair wages as defined in P.W.D. Contractor's Labour Regulations or as per the provisions of the Contract Labour (Regulation and Abolition) Act 1970 and the contract Labour (Regulation and Abolition) Central Rules, 1971, wherever applicable.
- ii) The contractor shall, notwithstanding the provisions of any contract to the contrary, cause to be paid fair wage to labour indirectly engaged on the work including any labour engaged by his sub-contractors in connection with the said work, as if the labour had been immediately employed by him.
- iii) In respect of all labour directly or indirectly employed in the works for performance of the contractor's part of this contract, the contractor shall comply with or cause to be complied with the Public Works Department contractor's Labour Regulations made by Government from time to time in regard to payment of wages, wage period, deductions from wages recovery of wages not paid and deductions unauthorisedly made, maintenance of wage books or wage slips, publication of scale of wages and other terms of employment, inspection and submission of periodical returns and all other matters of the like nature or as per the provisions of the Contract Labour (Regulation and Abolition) Act, 1970, and the Contract Labour (Regulation And Abolition) Central Rules, 1971, wherever applicable.
- iv).
 - a) The Engineer-in-Charge concerned shall have the right to deduct from the moneys due to the contractor any sum required or estimated to be required for making good the loss suffered by a worker or workers by reason of nonfulfilment of the conditions of the contract for the benefit of the workers, non-payment of wages or of deductions made from his or their wages which are not justified by their terms of the contract or non-observance of the Regulations.
 - b) Under the provision of Minimum Wages (Central) Rules 1950, the contractor is bound to allow to the labours directly or indirectly employed in the works one day rest for 6 days continuous work and pay wages at same rate as for duty. In the event of default the Engineer-in-Charge shall have the right to deduct the sum or sums not paid on account of wages for weekly holidays to any labours and pay the same to the persons entitled thereto from any money due to the contractor by the Engineer-in-Charge concerned.
- v) The contractor shall comply with the provisions of the Payment of Wages Act, 1936, Minimum Wages Act, 1948, Employees Liability Act, 1938, Workmen's Compensation Act, 1923, Industrial Disputes Act, 1947, Maternity Act, 1970, or the modifications thereof or any other laws relating thereto and the rules made thereunder from time to time.


(Seal & Signature of Tenderer)

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

- vi) The contractor shall indemnify and keep indemnified Government against payments to be made under and for the observance of the laws aforesaid and the P.W.D. Contractor's Labour Regulations without prejudice to his right to claim indemnity from his sub-contractors.
- vii) The laws aforesaid shall be deemed to be a part of this contract and any breach thereof shall be deemed to be a breach of this contract.
- viii) Whatever is the minimum wage for the time being, or if the wage payable higher than such wage, such wage shall be paid by the contractor to the workmen directly without the intervention of Jamadar and that Jamadar shall not be entitled to deduct or recover any amount from the minimum wage payable to the workmen as and by way of commission or otherwise.
- ix) The contractor shall ensure that no amount by way of commission or otherwise is deducted or recovered by the Jamadar from the wage of workmen.

CLAUSE 19 C

In respect of all labour directly or indirectly employed in the work for the performance of the contractor's part of this contract, the contractor shall at his own expense arrange for the safety provisions as per P.W.D. Safety Code framed from time to time and shall at his own expense provide for all facilities in connection therewith. In case the contractor fails to make arrangement and provide necessary facilities as aforesaid he shall be liable to pay a penalty of Rs. 200/- for each default and in addition the Engineer-in-Charge shall be at liberty to make arrangement and provide facilities as aforesaid and recover the costs incurred in that behalf from the contractor.

CLAUSE 20

Minimum wages Act to be complied with.

The contractor shall at least pay and comply with all the provisions of the Minimum wages Act and rules framed there under other labour laws related to contract labour.

CLAUSE 21

Work not to be sublet. Action in case of insolvency

The contract shall not be assigned or sublet without the written approval of the Engineer-in-Charge. And if the contractor shall assign or sublet his contract, or attempt to do so, or become insolvent or commence any insolvency proceedings or make any composition with his creditors or attempt to do so, or if any bribe, gratuity, gift, loan, perquisite, reward or advantage pecuniary or otherwise, shall either directly or indirectly, be given, promised or offered by the contractor, or any of his servants or agent to any public officer or person in the employ of Corporation in any way relating to his office or employment, or if any such officer or person shall become in any way directly or indirectly interested in the contract, the Engineer-in-Charge on behalf of the M.D. of Corporation shall have power to adopt the courses specified in Clause 3 hereof in the interest of Corporation and in the event of such course being adopted the consequences specified in the said Clause 3 shall ensue.

CLAUSE 22

Compensation


All sums payable by way of compensation under any of these conditions shall be considered as reasonable compensation to be applied to the use of Corporation without reference to the actual loss or damage sustained and whether or not any damage shall have been sustained.

CLAUSE 23

Changes in firm's Constitution to be intimated

Where the contractor is a partnership firm, the previous approval in writing of the Engineer-in-Charge shall be obtained before any change is made in the constitution of the firm. Where the contractor is an individual or a Hindu undivided family, business concern such

(Seal & Signature of Tenderer)



Chief Engineer
B.S.E.I.D.C. Ltd, Patna

approval as aforesaid shall likewise be obtained before the contractor enters into any partnership agreement where under the partnership firm would have the right to carry out the works hereby undertaken by the contractor. If previous approval as aforesaid is not obtained, the contract shall be deemed to have been assigned in contravention of Clause 21 thereof and the same action may be taken, and the same consequences shall ensue as provided in the said Clause 21.

CLAUSE 24

**Approval of
Engineer In
charge**

All works to be executed under the contract shall be executed under the direction and subject to the approval in all respects of the Engineer-in-Charge who shall be entitled to direct at what point or points and in what manner they are to be commenced, and from time to time carried on.

CLAUSE 25

**Settlement of
Disputes &
Arbitration**


Except where otherwise provided in the contract all questions and disputes relating to the meaning of the specifications, design, drawings and instructions here-in-before mentioned and as to the quality of workmanship or materials used on the work or as to any other question, claim right matter or thing whatsoever in any way arising out of or relating to contract, designs, drawings, specifications, estimates, instructions, orders or these conditions or otherwise concerning the works or the execution or failure to execute the same whether arising during the progress of the work or after the cancellation, termination, completion or abandonment thereof shall be dealt with as mentioned hereinafter.

- i) If the contractor considered any work demanded of him to be outside the requirements of the contract, or dispute any drawings, record or decision given in writing by the Engineer-in-Charge on any matter in connection with or arising out of the contract or carrying out of the contract or carrying out of the work, to be unacceptable, he shall promptly within 7 days request the Superintending Engineer/Chief consultant(Technical) in writing for written instruction or decision. Thereupon, the Superintending Engineer shall give his written instructions or decision within a period of fifteen days from the receipt of the contractor's letter.

If the Superintending Engineer/Chief consultant(Technical) fails to give his instructions or decision in writing within the aforesaid period or if the contractor is dissatisfied with the instructions or decision of the Superintending Engineer/Chief consultant(Technical), the contractor may, within 15 days of the receipt of Superintending Engineer's decision, appeal to the Chief Executive Officer who shall afford an opportunity to the contractor to be heard, if the latter so desires, and to offer evidence in support of his appeal. The Chief Executive Officer shall give his decision within 30 days of receipt of contractor's appeal. If the contractor is dissatisfied with this decision, the contractor shall within a period of 30 days from receipt of the decision, give notice to the Chief Executive Officer for appointment of arbitrator failing which the said decision shall be final binding and conclusive and not referable to adjudication by the arbitrator.

- ii) Except where the decision has become final, binding and conclusive in terms of Sub Para (i) above disputes or difference shall be referred for adjudication through arbitrator appointed by Managing Director of the Corporation. If the arbitrator so appointed is unable or unwilling to act or resign his appointment or vacates his office due to any reason whatsoever another sole arbitrator shall be appointed in the manner aforesaid. Such person shall be entitled to proceed with the reference from the stage at which it was left by his predecessor.

It is a term of this contract that the party invoking arbitration shall give a list of disputes with amounts claimed in respect of each such dispute along with the


(Seal & Signature of Tenderer)


Chief Engineer
B.S.E.I.D.C. Ltd, Patna

notice for appointment of arbitrator and giving reference to the rejection by the Chief Executive Officer of the appeal.

It is also a term of this contract that no person other than a person appointed by Managing Director of the Corporation as aforesaid should act as arbitrator and if for any reason that is not possible, the matter shall not be referred to arbitrator at all.

It is also a term of this contract that if the contractor does not make any demand for appointment of arbitrator in respect of any claims in writing as aforesaid within 45 days of receiving the intimation from the Engineer-in-Charge that the final bill is ready for payment, the claim of the contractor shall be deemed to have been waived and absolutely barred and the Corporation shall be discharged and released of all liabilities under the contract in respect of these claims.

The arbitration shall be conducted in accordance with the provisions of the Arbitration and Conciliation Act, 1996 (26 of 1996) or any statutory modifications or re-enactment thereof and the rules made there under and for the time being in force shall apply to the arbitration proceeding under this clause.

It is also a term of the contract that if any fees are payable to the arbitrator these shall be paid equally by both the parties.

It is also a term of the contract that the arbitrator shall be deemed to have entered on the reference on the date he issues notice to both the parties calling them to submit their statement of claims and counter statement of claims. The venue of the arbitration shall be such place as may be fixed by the arbitrator in his sole discretion. The fees, if any, of the arbitrator shall, if required to be paid before the award is made and published, be paid half and half by each of the parties. The cost of the reference and of the award (including the fees, if any, of the arbitrator) shall be in the discretion of the arbitrator who may direct to any by whom and in what manner such costs or any part thereof shall be paid and fix or settle the amount of costs to be so paid.

All arbitration shall be held at PATNA and at no other place.

CLAUSE 26

The contractor shall fully indemnify and deep indemnified the M.D. of Corporation against any action, claim or proceeding relating to infringement or use of any patent or design or any alleged patent or design rights and shall pay any royalties which may be payable in respect of any article or part thereof included in the contract. In the event of any claims made under the action brought against Government in respect of any such matter as aforesaid the contractor shall be immediately notified thereof and the contractor shall be at liberty, at his own expense, to settle any dispute or to conduct any litigation that may arise therefrom, provided that the contractor shall not be liable to indemnify the M.D. of Corporation if the infringement of the patent or design or any alleged patent or design right is the direct result of an order passed by the Engineer-in-Charge in this behalf.

CLAUSE 27

When the estimate on which a tender is made includes lump sum in respect of parts of the work, the contractor shall be entitled to payment in respect of the items of work involved or the part of the work in question at the same rates as are payable under this contract for such items, or if the part of the work in question is not, in the opinion of the Engineer-in-Charge capable of measurement, The Engineer-in-Charge may at his discretion pay the lump-sum amount entered in the estimate, and the certificate in writing of the Engineer-in-Charge shall be final and conclusive against the contractor with regard to any sum or sums payable to him under the provisions of the clause.

(Seal & Signature of Tenderer)

310713012 RT E

Chief Engineer
BSEIDC Ltd, Patna
Er

Contractor to
indemnify Govt.
against Patent
Rights

Lumpsum
Provisions in
Tender

CLAUSE 28

Action where no Specifications are specified

In the case of any class of work for which there is no such specifications as referred to in Clause 11, such work shall be carried out in accordance with the Bureau of Indian Standards Specifications, Indian Road Congress for road works and Indian Building Congress for building works or any central government agency. In case there are no such specifications in Bureau of Indian Standards, the work shall be carried out as per manufacturers specifications. If not available then as per Corporation / Building Construction Department Specifications. In case there are no such specifications as required above, the work shall be carried out in all respects in accordance with the instructions and requirements of the Engineer-in-Charge.

CLAUSE 29

- i) Whenever any claim or claims for payment of a sum of money arises out of or under the contract or against the contractor, the Engineer-in-Charge or the Corporation shall be entitled to withhold and also have a lien to retain such sum or sums in whole or in part from the security, if any deposited by the contractor and for the purpose aforesaid, the Engineer-in-Charge or the Corporation shall be entitled to withhold the security deposit, if any, furnished as the case may be and also have a lien over the same pending finalisation or adjudication of any such claim. In the event of the security being insufficient to cover the claimed amount or amounts or if no security has been taken from the contractor, the Engineer-in-Charge or the Corporation shall be entitled to withhold and have a lien to retain to the extent of, payable or which may at any time thereafter become payable to the contractor under the same contract or any other contract with the Engineer-in-Charge of the Corporation or any contracting person through the Engineer-in-Charge of the Corporation or any contraction person through the Engineer-in-Charge pending finalisation of adjudication of any such claim.

It is an agreed term of the contract that the sum of money or moneys so withheld or retained under the lien referred to above by the Engineer-in-Charge or Corporation will be kept withheld or retained as such by the Engineer-in-Charge or Corporation till the claim arising out of or under the contract is determined by the arbitrator (if the contract is governed by the arbitration clause) or by the competent court, as the case may be and that the contractor will have no claim for interest or damages whatsoever on any account in respect of such withholding or retention under the lien referred to above and duly notified as such to the contractor. For the purpose of this clause, where the contractor is a partnership firm or a limited company, the Engineer-in-Charge or the Corporation shall be entitled to withhold and also have a lien to retain towards such claimed amount or amounts in whole or in part from any sum found payable to any partner/limited company as the case may be, whether in his individual capacity or otherwise.

- ii) Corporation shall have the right to cause an audit and technical examination of the works and the final bills of the contractor including all supporting vouchers, abstract etc., to be made after payment of the final bill and if as a result of such audit and technical examination any sum is found to have been overpaid in respect of any work done by the contractor under the contract or any work claimed to have been done by him under the contract and found not to have been executed, the contractor shall be liable to refund the amount of over-payment and it shall be lawful for Government to recover the same from him in the manner prescribed in sub-clause (i) of this clause or in any other manner legally permissible; and if it is found that the contractor was paid less than what was due to him under the contract in respect of any work executed by him under it, the amount of such under payment shall be duly paid by Corporation to the contractor without any interest thereon whatsoever.


(Seal & Signature of Tenderer)

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

CLAUSE 29 A

**Lien in respect of
claims in other
Contracts**

Any sum of money due and payable to the contractor (including the security deposit returnable to him) under the contract may be withheld or retained by way of lien by the Engineer-in-Charge or the Government or any other contracting person or persons through Engineer-in-Charge against any claim of the Engineer-in-Charge or Corporation or such other person or persons in respect of payment of a sum of money arising out of or under any other contract made by the contractor with the Engineer-in-Charge or the Corporation or with such other person or persons.

It is an agreed term of the contract that the sum of money so withheld or retained under this clause by the Engineer-in-Charge or the Corporation will be kept withheld or retained as such by the Engineer-in-Charge or the Corporation till his claim arising out of the same contract or any other contract is either mutually settled or determined by the arbitration clause or by the competent court, as the case may be and that the contractor shall have no claim for interest or damages whatsoever on this account or on any other ground in respect of any sum of money withheld or retained under this clause and duly notified as such to the contractor.

CLAUSE 30

**Unfiltered
water
supply**

The contractor(s) shall make his/their own arrangements for water required for the work and nothing extra will be paid for the same. This will be subject to the following conditions.

- i) That the water used by the contractor(s) shall be fit for construction purposes to the satisfaction of the Engineer-in-Charge.
- ii) The Engineer-in-Charge shall make alternative arrangements for supply of water at the risk and cost of contractor(s) if the arrangements made by the contractor(s) for procurement of water are in the opinion of the Engineer-in-Charge, unsatisfactory.

CLAUSE 31

**Return of
surplus
material**

Notwithstanding anything contained to the contrary in this contract, where any materials for the execution of the contract are procured with the assistance of Corporation either by issue from Corporation stocks or purchase made under orders or permits or licences issued by Corporation the contractor shall hold the said materials economically and solely for the purpose of the contract and not dispose of them without the written permission of the Corporation and return, if required by the Engineer in Charge, all surplus or unserviceable materials that may be left with him after the completion of the contract or at its termination for any reason whatsoever on being paid or credited such price as the Engineer in Charge shall determine having due regard to the condition of the materials. The price allowed to the contractor however shall not exceed the amount charged to him excluding the element of storage charges. The decision of the Engineer in Charge shall be final and conclusive. In the event of breach of the aforesaid condition the contractor shall in addition to throwing himself open to action for contravention of the term of the licence or permit and/or for criminal breach of trust, be liable to Corporation for all moneys, advantages or profits resulting or which in the usual course would have resulted to him by reason of such breach.

CLAUSE 32

**Hire of Plant & i)
Machinery**

The contractor shall arrange at his own expense all tools, plant machinery and equipment (hereinafter referred to as T & P) required for execution of the work except for the Plant & Machinery listed in Schedule 'C' and stipulated for issue to

(Seal & Signature of Tenderer)

SIGMA BMR

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

the contractor. If the contractor requires any item of T & P on hire from the T & P available will, if such item is available, hire it to the contractor at rates to be agreed upon between him and the Engineer-in-Charge. In such a case all the conditions hereunder for issue of T & P shall also be applicable to such T & P as is agreed to be issued.

- ii) Plant and Machinery when supplied on hire charges shown in Schedule 'C' shall be made over and taken back at the departmental equipment yard/shed shown in Schedule 'C' and the contractor shall bear the cost of carriage from the place of issue to the site of work and back. The contractor shall be responsible to return the plant and machinery in the condition in which it was handed over to him, and he shall be responsible for all damage caused to the said plant and machinery at the site of work or elsewhere in operation and otherwise during transit including damage to or loss of plant and for all losses due to his failure to return the same soon after the completion of the work for which it was issued. The Engineer-in-charge shall be the sole judge to determine the liability of the contractor and its extent in this regard and his decision shall be final and binding on the contractor.
- iii) The plant and machinery as stipulated above will be issued as and when available and if required by the contractor. The contractor shall arrange his programme of work according to the availability of the plant and machinery and no claim whatsoever, will be entertained from him for any delay in supply by the Corporation.
- iv) The hire charges shall be recovered at the prescribed rates from and inclusive of the date the plant and machinery made over up to and inclusive of the date of the return in good order even though the same may not have been working for any cause except major breakdown due to no fault of the contractor or faulty use requiring more than three working days continuously (excluding intervening holidays and Sundays) for bringing the plant in order. The contractor shall immediately intimate in writing to the Engineer in Charge when any plant or machinery gets out of order requiring major repairs as aforesaid. The Engineer in Charge shall record the date and time of receipt of such intimation in the log sheet of the plant or machinery. Based on this if the breakdown occurs before lunch period or major breakdown will be computed considering half a day's breakdown on the day of complaint. If the breakdown occurs in the post lunch period of major breakdown will be computed starting from the next working day. In case of any dispute under this clause the decision of the Superintending Engineer shall be final and binding on the contractor.
- v) The hire charges shown above are for each day of 8 hours (inclusive of the one hour lunch break) or part thereof.
- vi) Hire charges will include service of operating staff as required and also supply of lubricating oil and stores for cleaning purposes. Power fuel of approved type, firewood, kerosene oil etc. for running the plant and machinery and also the full time chowkidar for guarding the plant and machinery against any loss or damage shall be arranged by the contractor who shall be fully responsible for the safeguard and security of plant and machinery. The contractor shall on or before the supply of plant and machinery sign an agreement indemnifying the Corporation against any loss or damage caused to the plant and machinery either during transit or at site of work.


(Seal & Signature of Tenderer)


Chief Engineer
B.S.E.I.D.C. Ltd, Patna

- vii) Ordinarily, no plant and machinery shall work for more than 8 hours a day inclusive of one hour lunch break. In case of an urgent work however, the Engineer in Charge may, at his discretion, allow the plant and machinery to be worked for more than normal period or 8 hours a day. In that case the hourly hire charges for overtime to charge (1/8)th of the daily charges) subject to a minimum of half day's normal charges on any particular day. For working out hire charges for over time a period of half an hour and above will be charged as one hour and a period of less than half an hour will be ignored.
- viii) The contractor shall release the plant and machinery every seventh day for periodical servicing and/or wash out which may take about three to four hours or more. Hire charges for full day shall be recovered from the contractor for the day of servicing/Wash out irrespective of the period employed in servicing.
- ix) The plant and machinery once issued to the contractor shall not be returned by him on account of lack of arrangements of labour and materials, etc. on his part, the same will be returned only when they are required for major repairs or when in the opinion of the Engineer in Charge the work or a portion of work for which the same was issued is completed.
- x) Log Book for recording the hours of daily work for each of the plant and machinery supplied to the contractor will be maintained by the Corporation and will be countersigned by the contractor or his authorised agent daily. In case the contractor contests the correctness of the entries and/or fails to sign the Log Book the decision of the Engineer-in-Charge shall be final and binding on him. Hire charges will be calculated according to the entries in the Log Book and will be binding on the contractor. Recovery on account of hire charges for road rollers shall be made for the minimum number of days worked out on the assumption that a roller can consolidate per day and maximum quantity of materials or area surfacing as noted against each in the annexed statement (see attached annexure).
- xi) In the case of concrete mixers, the contractors shall arrange to get the hopper cleaned and the drum washed at the close of the work each day or each occasion.
 - a) In case rollers for consolidation are employed by the contractor himself, log book for such rollers shall be maintained in the same manner as is done in case of departmental rollers, maximum quantity of any item to be consolidated for each roller day shall also be same as in Annexure to Clause 34(x). For less use of rollers recovery for the less roller days shall be made at the stipulated issue rate.
- xii) The contractor shall be responsible to return the plant and machinery in the condition in which it was handed over to him and he shall be responsible for all damage caused to the said plant and machinery at the site of work or elsewhere in operation or otherwise or during transit including damage to or loss of parts, and for all losses due to him failure to return the same soon after the completion of the work for which it was issued. The Engineer-in-charge shall be the sole judge to determine the liability of the contractor and its extent in this regard and his decision shall be final and binding on the contractor.
- xiii) The contractor will be exempted for levy of any hire charges for the number of days he is called upon in writing by the Engineer in Charge to suspend execution of the work provided Corporation plant and machinery in question have, in fact remained idle with the contractor because of the suspension.
- xiv) In the event of the contractor not requiring any item of plant and machinery issued by the Corporation though not stipulated for issue in Schedule of any time after

(Seal & Signature of Tenderer)

[Handwritten Signature]

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

[Handwritten Signature]

taking delivery at the place of issue, he may return it after two days written notice or at any time without notice if he agrees to pay hire charges for two additional days without in any way affecting the right of the Engineer in-Charge to use the said plant and machinery during the said period of two days as he likes including hiring out to a third party.

CLAUSE 33

Contractors Superintendence, Supervision, Technical Staff & Employees

**Employment of
Technical Staff
and employees**

- i) The contractor shall provide all necessary superintendence during execution of the work and as along thereafter as may be necessary for proper fulfilling of the obligations under the contract.

The contractor along with bidding of the tender, intimate in writing to the Engineer-in-Charge the name, qualifications, experience, age, address and other particulars along with certificates, of the technical representative to be in charge of the work. If there is any change then the new incumbents qualifications and experience shall not be lower than specified in Schedule in I.T.B. (Annexure - 2). The Engineer-in-Charge shall within 15 days of issue of letter of acceptance intimate in writing his approval or otherwise it is deemed to be approved. Any such approval may at any time be withdrawn and in case of such withdrawal the contractor shall appoint another such representative according to the provisions of this clause. Decision of the tender accepting authority / Chief Consultant Officer (Technical) shall be final and binding on the contractor in this respect. Technical staff shall be available at site within fifteen days of start of work.

If the contractor (or any partner in case of firm/company) himself has such qualifications, it will not be necessary for the said contractor to appoint such a principal technical representative but the contractor shall designate and appoint a responsible agent to represent him and to be present at the work whenever the contractor is not in a position to be so present. All the provisions applicable to the principal technical representative under the Clause will also be applicable in such a case to contractor or his responsible agent. The principal technical representative and/or the contractor or his responsible authorised agent shall be actually available at site at least two working days every week, these days shall be determined in advance and also during recording of measurement of works and whenever so required by the Engineer-in-Charge by a notice as aforesaid and shall also note down instructions conveyed by the Engineer-in-Charge or his designated representative in the site order book and in token of acceptance of measurements. There shall be no objection if the representative/agent looks after more than one work and not more than three works in the same station provided these details are disclosed to the Engineer-in-Charge and he shall be satisfied that the provisions and the purpose of the clause are fulfilled satisfactorily.

If the Engineer-in-Charge, whose decision in this respect is final and binding on the contractor, is convinced that no such technical representative or agent is effectively appointed or is effectively attending or fulfilling the provision of this clause, a recovery shall be effected from the contractor as specified in Schedule 'F' and the decision of the Engineer-in-Charge as recorded in the site order book and measurement recorded in Measurement Books shall be final and binding on the contractor. Further if the contractor fails to appoint a suitable technical representative or responsible agent and if such appointed persons are not effectively present or do not discharge their responsibilities satisfactorily, the Engineer-in-Charge shall have full powers to suspend the execution of the work until such date as a suitable agent is appointed and the contractor shall submit a certificate of employment of the technical representative/responsible agent along


(Seal & Signature of Tenderer)

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

with every on account bill/fixed bill and shall produce evidence if at any time so required by the Engineer-in-Charge.

- ii) The contractor shall provide and employ on the site only such technical assistants as are skilled and experienced in their respective fields and such foremen and supervisory staff as are competent to give proper supervision to the work.

The contractor shall provide and employ skilled, semiskilled and unskilled labour as is necessary for proper and timely execution of the work.

The Engineer in Charge shall be at liberty to object to and require the contractor to remove from the works any person who in his opinion misconducts himself, or is incompetent or negligent in the performance of his duties or whose employment is otherwise considered by the Engineer in Charge to be undesirable. Such person shall not be employed again at works site without the written permission of the Engineer in Charge and the persons so removed shall be replaced as soon as possible by competent substitutes.

CLAUSE 34

- i) Sales Tax or any other tax on materials in respect of this contract shall be payable by the contractor according to law in effect.
- ii) The contractor shall deposit royalty and obtain necessary permit for supply of the red earth, moorum, sand chips bajri, stone, kankar, etc. from local authorities.
- iii) If pursuant to or under any law, notification or order any royalty, cess or the hike becomes payable to the Government of India and does not at any time become payable by the contractor to the State Government/ Local authorities in respect of any material used by the contractor in the works then in such a case, it shall be lawful to the Government of India and it will have the right and be entitled to recover the amount paid in the circumstances as aforesaid from the dues of the contractor.

CLAUSE 35

Conditions for reimbursement of levy/taxes if levied after receipt of tenders

- i) All tendered rates shall be inclusive of all taxes and levies payable under respective statutes. However, pursuant to the Constitution (46th Amendment) Act, 1982, if any further tax or levy is imposed by Statute, after the last stipulated date for the receipt of tender including extensions if any and the contractor thereupon necessarily and properly pays such taxes/levies the contractor shall be reimbursed the amount so paid, provided such payments, if any, is not, in the opinion of the Engineer-in-Charge (whose decision shall be final and binding on the contractor) attributable to delay in execution of work within the control of the contractor.
- ii) The contractor shall keep necessary books of accounts and other documents for the purpose of this condition as may be necessary and shall allow inspection of the same by a duly authorised representative of the Government and/or the Engineer-in-Charge and further shall furnish such other information/document as the Engineer-in-Charge may require from time to time.
- iii) The contractor shall, within a period of 30 days of the imposition of any such further tax or levy, pursuant to the Constitution (Forty Sixth Amendment) Act 1982, give a written notice thereof to the Engineer-in-Charge that the same is given pursuant to this condition, together with all necessary information relating thereto.

(Seal & Signature of Tenderer)



Chief Engineer
B.S.E.I.D.C. Ltd, Patna 100


CLAUSE 36

**Imprisonment
of Contractor**

If the contractor is imprisoned, becomes insolvent compound with his creditors, has a receiving order made against him or carries on business under a receiver for the benefit of the creditors or any of them, or being a partnership firm becomes dissolved, or being a company or corporations goes into liquidation or commences to be wound up not being a voluntary winding up for the purpose only of amalgamation or reconstitution the department shall be at liberty.

- (a) To give such liquidator, receiver, or other person in whom the contract may become vested, the option of carrying out the contract or a portion thereof to be determined by the department, subject to his providing an appropriate guarantee for the performance of such contract or.
- (b) To terminate the contract, forthwith by notice in writing to the contractor, the liquidator, the receiver or person in whom the contract may become vested and take further action as provided in the relevant clauses of the contract.

CLAUSE 37

**Termination
of Contract
on death of
contractor**

Without prejudice to any of the rights or remedies under this contract if the contractor dies, the Competent Authority on behalf of the BSEIDCo. shall have the option of terminating the contract without compensation to the contractor after the affidavit of his/their legal heir/heirs that they are not going to be in this profession in future.

CLAUSE 38

**If relation
working in
BSEIDCo. then
the contractor
not allowed to
tender**

The contractor shall not be permitted to tender for works in the BSEIDCo. (responsible for award and execution of contracts) in which his near relative is posted as an officer in any capacity. He shall also intimate the names of persons who are working with him in any capacity or are subsequently employed by him and who are near relatives to any Officer in the BSEIDCo.. Any breach of this condition by the contractors of this Corporation shall lead to blacklisting. If the contractor is registered in any other department, he shall be debarred from tendering in BSEIDCo. for any breach of this condition.

NOTE : By the term "near relatives" is meant wife, husband, parents and grand parents, children and grand children, brothers and sisters, uncles, aunts and cousins and their corresponding in law.

CLAUSE 39

**No-Gazetted-
Engineer to work
as Contractor
within two years
of retirement**

No engineer of gazetted rank of other gazetted officer employed in engineering or administrative duties in an engineering department of the Government of Bihar shall work as a contractor or employee of a contractor for a period of two years after his retirement from government service without the previous permission of State Government in writing. This contract is liable to be cancelled if either the contractor or any of his employees is found at any time to be such a person who had not obtained said permission prior to engagement in the contractor's service, as the case may be.

CLAUSE 40

**Return of
material and
recovery for
excess material
issued**

i). After completion of the work and also at any intermediate stage in the event of non reconciliation of materials issued, consumed and in balance (see Clause 10) theoretical quantity of materials issued by the Corporation for use in the work shall be calculated on the basis and method given hereunder.

- a) Quantity of cement & bitumen shall be calculated on the basis of quantity of cement & bitumen required different items of work as shown in the Schedule Rates mentioned in-Schedule 'F'. In case any item is executed for which standard constants for the consumption of cement or bitumen are not available in the above mentioned schedule/statement or cannot be derived from the


(Seal & Signature of Tenderer)

Chief Engineer 101
B.S.E.I.D.C. Ltd, Patna
Rmk

- same shall be calculated on the basis of standard formula to be laid down by the Engineer in Charge.
- b) Theoretical quantity of steel reinforcement of structural steel sections shall be taken as the quantity required as per design or as authorised by Engineer in Charge, including authorised lappages, chairs etc., plus 3% wastage due to cutting into pieces, such theoretical quantity being determined and compared with the actual issues each diameter wise, section wise and categoriwise separately.
- c) For any other material as per actual requirements.
- ii) Over the theoretical quantities of materials so computed a variation shall be allowed as specified in Schedule 'F'. The difference in the net quantities of material actually issued to the contractor and the theoretical quantities including such authorised variation, if not returned by the contractor or if not fully reconciled to the satisfaction of the Engineer in Charge within fifteen days of the issue of written notice by the Engineer in Charge to this effect shall be recovered at the rates specified in Schedule 'F' without prejudice to the provision of the relevant conditions regarding return of materials governing the contract. Decision of Engineer in Charge in regard to theoretical quantities of materials, which should have been actually used as per the Annexure of the standard schedule of rates and recovery at rates specified in Schedule 'F', shall be final & binding on the contractor
- For not scheduled items, the decision of the Superintending Engineer regarding theoretical quantities of materials, which should have been actually used, shall be final and binding on the contractor.
- iii) The said action under this clause is without prejudice to the right of the Government to take action against the contractor under any other conditions of contract for not doing the work according to the prescribed specifications.

CLAUSE 41

**Release of
Security
deposit**

On completion of the whole of the work, half of the total amount of security shall be repaid to the contractor after six months of completion. However, the balance half of the total amount of security will be returned after completion of defect liability period and after the Engineer has certified that all defects notified by him to the contractor before the end of this period have been corrected and also after recovery of, any dues.

CLAUSE 42

**Responsibility
of Technical
Staff and
employees**

Technical officers / staff deployed by the Contractor at any construction site will also be responsible for inferior quality / poor performance of any work and his name will be circulated to all works Department of the State Govt. to debar from any other site, if his name is being proposed by other contractor.

CLAUSE 43

**Contractor's
Risks**

All risks of loss of or damage to physical property and of personal injury and death which arise during and in consequence of the performance of the Contract other than the excepted risks are the responsibility of the Contractor.

CLAUSE 44

Insurance

The Contractor shall provide, in the joint names of the Employer and the Contractor, insurance cover from the Start Date to the end of the Defects Liability Period, in the amounts and deductibles stated in the Contract Data for the following events which are due to the Contractor's risks :

- (a) loss of or damage to the Works, Plant and Materials ;
- (b) loss of or damage to Equipment;
- (c) loss of or damage of property (except the Works, Plant, Materials and Equipment) in connection with the Contract; and

(Seal & Signature of Tenderer)

31/04/2012 RFE

2014
Chief Engineer
B.S.E.I.D.C. Ltd, Patna

(d) personal injury or death.

Policies and certificates for insurance shall be delivered by the Contractor to the Engineer for the Engineer's approval before the Start Date. All such insurance shall provide for compensation to be payable in the types and proportions of currencies required to rectify the loss or damage incurred.

If the Contractor does not provide any of the policies and certificates required, the Employer may effect the insurance which the Contractor should have provided and recover the premiums the Employer has paid from payments otherwise due to the Contractor or, if no payment is due, the payment of the premiums shall be a debt due.

Alteration to the terms of an insurance shall not be made without the approval of the Engineer.

Both parties shall comply with any conditions of the insurance policies.

CLAUSE 45

Cash Flow
Estimate to
be Submitted

The Contractor shall, within the time stated in special Conditions of contract after the date of the Letter of Acceptance, provide to the Engineer for his information a detailed cash flow estimate, in quarterly periods, of all payments to which the Contractor will be entitled under the Contract and the Contractor shall subsequently supply revised cash flow estimates at quarterly intervals, if required to do so by the Engineer. in charge

CLAUSE 46

Safety, Security
and Protection of
the Environment

The Contractor shall, throughout the execution and completion of the Works and the remedying of any defects therein :

- (a) have full regard for the safety of all persons entitled to be upon the Site and keep the Site (so far as the same is under his control) and the Works (so far as the same are not completed or occupied by the Employer) in an orderly state appropriate to the avoidance of danger to such persons,
- (b) Provide and maintain at his own cost all lights, guards, fencing, warning signs and watchmen and where necessary or required by the Engineer or by any duly constituted authority, for the protection of the Works or for the safety and convenience of the public or others, and
- (c) take all reasonable steps to protect the environment on and off the Site and to avoid damage or nuisance to persons or to property of the public or others resulting from pollution, noise or other causes arising as a consequence of his methods of operation.

CLAUSE 47

Cost of
Samples

All samples shall be supplied by the Contractor at his own cost if the supply thereof is clearly intended by or provided for in the Contract.

CLAUSE 48

Cost of
Tests

The cost of making any test shall be borne by the Contractor if such test is :

- (a) clearly intended by or provided for in the Contract, or
- (b) particularised in the Contract (in case only of a test under load or of a test to ascertain whether the design of any finished or partially finished work is appropriate for the purposes which it was intended to fulfill) in sufficient detail to enable the Contractor to price or allow for the same in his Tender.

(c)

CLAUSE 49

Cost of Tests
not Provided
for

If any test required by the Engineer which is :


(Seal & Signature of Tenderer)


Chief Engineer
B.S.E.I.D.C. Ltd, Patna

- (a) not so intended by or provided for,
- (b) (in the cases above mentioned) not so particularised, or
- (c) (though so intended or provided for) required by the Engineer to be carried out at any place other than the Site or the place of manufacture, fabrication or preparation of the materials or Plant tested,

shows the materials, Plant or workmanship not to be in accordance with the provisions of the Contract to the satisfaction of the Engineer, then the cost of such test shall be borne by the Contractor, but in any other case department will bear the cost.

CLAUSE 50

Commencement
of Works

The contractor shall commence the Works as soon as is reasonably possible after the receipt by him of a notice to this effect from the Engineer, which notice shall be issued within the time stated in the Appendix to Tender after the date of the Letter of Acceptance. Thereafter, the Contractor shall proceed with the Works with due expedition and without delay.

CLAUSE 51

Substantial
completion of
parts

If any part of the Permanent Works has been substantially completed and has satisfactorily passed any Test on Completion prescribed by the Contract, the Engineer may issue a Taking-Over Certificate in respect of that part of the Permanent Works before completion of the Works and, upon the issue of such Certificate, the Contractor shall be deemed to have undertaken to complete with due expedition any outstanding work in that part of the Permanent Works during the Defects Liability Period.

CLAUSE 52

Force Majeure

Force Majeure

Neither party shall be liable to the other for any loss or damage occasioned by or arising out of acts of GOD such as Unprecedented flood, Volcanic eruption, Earthquake or other convulsion of nature and other acts such as general/ partial strikes by a section of government employees/ invasion, the act of foreign countries/ hostilities or war like operations before or after declaration of war, rebellion/ military or usurped power which prevent performance of the contract and which could not have been foreseen or avoided by a prudent person.

CLAUSE 53

Recovery

Force Majeure

Any amount found recoverable from the contractor shall be recovered as public demand under the Bihar Public Demand Act. without prejudice to any other mode of recovery.

NOTE :

In case of difference or ambiguity in Hindi and English version, the English version will prevail.

(Seal & Signature of Tenderer)

[Signature]

[Signature]
25-6-2014
Chief Engineer
B.S.E.I.D.C. Ltd, Patna

SECTION 4
CONTRACT DATA
(PROFORMA OF SCHEDULES)


(Seal & Signature of Tenderer)


Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Rmb

PROFORMA OF SCHEDULES

(Operative Schedules to be supplied separately to each intending tenderer)

SCHEDULE 'A'

Schedule of quantities : BOQ attached with Financial bid.

Sl. No.	Description of Item(with brief specification and reference to book of specification)	BILL OF QUANTITY				Amount
		Quantity	Unit	Rate		
				In figure	In words	
1	2	3	4	5	6	7

SCHEDULE 'B' : N.A.

Schedule of materials to be issued to the contractor.: X

S. No.	Description of item	Quantity	Rates in figures & words at which the material will be charged to the contractor	Place of Issue
1	2	3	4	5

SCHEDULE 'C' : N.A.

Tools and plants to be hired to the contractor

Sl. No.	Description	Hire charge per day	Place of Issue
1	2	6	7

SCHEDULE 'D' : N.A.

Extra schedule for specific requirements/ document for the work, if any.

SCHEDULE 'E' :

Schedule of component of Cement, Steel, other Materials, Labour etc. for price escalation.

(Seal & Signature of Tenderer)



Chief Engineer
B.S.E.I.D.C. Ltd, Patna

CLAUSE 10 CC

Component of Cement-
expressed as percent of total value of work.

Pc : N.A.

Component of Steel-
expressed as percent of total value of work.

Ps : N.A.

Component of civil (except cement & steel)/
Electrical construction Materials expressed
as percent of total value of work-

Pm : N.A.

Component of Bitumen -
expressed as percent of total value of work.

Pb : _____ X _____ %

Component of Labour-
expressed as percent of total value of work.

P1 : _____ N.A. _____ %

Component of P.O.L. -
expressed as percent of total value of work.

Pf : _____ N.A. _____ %

Component of Plant & Machinery -
expressed as percent of total value of work.

Pp : _____ N.A. _____ %

SCHEDULE 'F'

Reference to General Condition of Contract.

Name of work: Construction of Senior Secondary Schools in Bihar, Gr. No. : SSS-153

Estimated cost of work : Rs. 21010782 (Rupees Two Crore Ten Lac Ten Thousand Seven Hundred and Eighty Two Only.)

- i) Earnest money : Rs. 4.21 Lac (Rupees Four Lac Twenty One Thousand Only).
- ii) Performance Guarantee: 2% of tendered value including earnest money.
- iii) Security Deposit : 8 % of tendered value.
- iv) Defect Liability period: Three Years.
- v) Rate of Interest : 14.5 %

GENERAL RULES AND DIRECTIONS

Officer inviting tender : Managing Director, BSEIDC.
Maximum percentage for quantity of
items of work to be executed beyond
which rates are to be determined in
accordance with Clauses 12.2 & 12.3

See below

Definitions:

2(v) Engineer-in-Charge

Executive Engineer (Civil).

2(x) Percentage on cost of materials and
labour to cover all overheads and
profits.

As Per SOR, BCD

2(xi) Standard Schedule of Rates

S.O.R. BCD, Dt. : 11.08.2013
& DSR (CIVIL&ELECTRICAL) 2012.

2(xii) Department & Employer

BSEIDC, Patna.


(Seal & Signature of Tenderer)

Chief Engineer
B.S.E.I.D.C. Ltd, Patna



9(ii) Standard PWD Contract Form

PWD 2/3 as modified & corrected upto

Clause 1

- i) Time allowed for submission of performance Guarantee from the date of issue of letter of acceptance, in days 15 days
- ii) Maximum allowable extension beyond the period provided in i) above in days 7 days

Clause 2

Authority for fixing compensation under clause 2.

Managing Director, BSEIDC

Clause 2A

Whether Clause 2A shall be applicable

Yes

Clause 5

Number of days from the date of issue of notice to start.

07 days

Mile stone(s) as per table given below:

Table of Mile Stone(s)

Sl. No.	Description of Milestone(Physical)	Time allowed in days (from date of start)	Amount to be with-held in case of non achievement of milestone
1.			
2.			
.			
.			

AND

Sl. No.	Financial Progress	Time allowed (from date of start)	Amount to be with-held in case of non achievement of milestone
1.	1/8 th (of whole work)	1/4 th (of whole work)	In the event of not achieving the necessary progress as assessed from the running payments, 1% of the tendered value of work will be withheld for failure of each milestone.
2.	3/8 th (of whole work)	1/2 th (of whole work)	
3.	3/4 th (of whole work)	3/4 th (of whole work)	
4.	Full	Full	

Time allowed for execution of work

15 Months.

Authority to give fair and reasonable extension of time for completion of work.

Managing Director, BSEIDC, Patna.

(Seal & Signature of Tenderer)

BSEIDC Patna

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

Pml

Clause 7

Gross work to be done together with net payment/ adjustment of advances for material collected, if any, since the last such payment for being eligible to interim payment

Rs 09.00 Lac.

Clause 10CC

Clause 10CC to be applicable in contracts with stipulated period of completion exceeding the period shown in next column

_____ months

Clause 11

Specifications to be followed for execution of work

_____ Yes _____

Clause 12

Deviation, variation
Extent and pricing.

As per P.W.D. Code
clause 182A, 292XII,
293XVII & 294XVI

Clause 16

Competent Authority for
deciding reduced rates.

Chief Consultant (Technical)

- The following document also form part of the contract.
- The law, which applies to the contract, is
- The court of jurisdiction
- The Language of contract document
- The limit of sub-contracting
- The Currency of the Contract is

SBD , NIT & B.O.Q.

The Law of Union of India.

Patna.

English

_____ X _____

Indian Rupees


(Seal & Signature of Tenderer)


Chief Engineer
B.S.E.I.D.C. Ltd, Patna

SECTION 5
SPECIAL CONDITION OF CONTRACT
(Condition of Particular Application)


(Seal & Signature of Tenderer)

गोपबन्धुनारायण

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

25-6-2014

SECTION 6
TECHNICAL SPECIFICATION
(Along with Basic drawings)


(Seal & Signature of Tenderer)



Chief Engineer
B.S.E.I.D.C. Ltd, Patna

Rmt

SECTION 7
BILL OF QUANTITY
(Attached with Financial bid)

(Seal & Signature of Tenderer)




25-6-2014

BILL OF QUANTITIES

Preamble

1. The Bill of Quantities shall be read in conjunction with the Instructions to Bidders, Conditions of Contract, Technical Specifications and Drawings.
2. The quantities given in the Bill of Quantities are estimated and provisional, and are given to provide a common basis for bidding. The basis of payment will be the actual quantities of work ordered and carried out, as measured by the Contractor and verified by the Engineer and valued at the rates and prices tendered in the priced Bill of Quantities, where applicable, and otherwise at such rates and prices as the Engineer may fix within the terms of the Contract.
3. The rates and prices tendered in the priced Bill of Quantities shall, except in so far as it is otherwise provided under the Contract, include all constructional plant, labour supervision, materials, erection, maintenance, insurance, profit, taxes and duties, together with all general risks, liabilities and obligations set out or implied in the Contract.
4. The rates and prices shall be quoted entirely in Indian Currency.
5. A rate whole cost of complying with the provisions of the Contract shall be included in the items provided in the priced Bill of Quantities, and where no items are provided the cost shall be deemed to be distributed among the rates and prices entered for the related items of Work.
6. The whole cost of complying with the provisions of the Contract shall be included in the items provided in the priced Bill of Quantities, and where no items are provided the cost shall be deemed to be distributed among the rates and prices entered for the related items of Work.
7. General directions and descriptions of work and materials are not necessarily repeated or summarized in the Bill of Quantities. References to the relevant sections of the contract documentation shall be made before entering rates or prices against each item in the Bill of Quantities.
8. The method of measurement of completed work for payment shall be in accordance with the specification issued by the department / Corporation time to time.
9. Errors will be corrected by the Employer for any arithmetic errors pursuant to Clause 29 of the Instructions to Bidders.

31/07/2014
(Seal & Signature of Tenderer)

25-6-2014
Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Rud


BILL OF QUANTITIES

Sl. No.	Description of Item (with brief specification and reference to book of specification)	Quantity	Unit	Rate		Amount
				In Figure	In Words	
	(ATTACHED with Financial bid)					

Note :

1. Item for which no rate or price has been entered in will not be paid for by the Employer when executed and shall be deemed covered by the other rates and prices in the bill of quantities
2. Unit rates and prices shall be quoted by the bidder in Indian rupee
3. Where there is a discrepancy between the rate in figures and words, the rates in words will govern.
4. Where there is a discrepancy between the unit rate and the line item total resulting from multiplying the unit rate by quantity, the unit rate quoted shall govern

(Seal & Signature of Tenderer)

 B.S.E.I.D.C. Ltd, Patna

SECTION 8
SECURITIES AND OTHER FORMS
(to be filled by Bidder/Employer)

31/07/2014
(Seal & Signature of Tenderer)

25-6-2014
Chief Engineer
B.S.E.I.D.C. Ltd, Patna

Rmb

BID SECURITY (BANK GUARANTEE UNCONDITIONAL)

WHEREAS, _____ [name of Bidder] (hereinafter called "the Bidder") has submitted his Bid dated _____ [date] for the construction of _____ [name of Contract hereinafter called "the Bid"].

KNOW ALL PEOPLE by these presents that We _____ [name of Bank] of _____ [name of country] having our _____ registered _____ office _____ at _____ (hereinafter called "the Bank") are bound unto _____ [name of Employer] (hereinafter called "the Employer") in the sum of _____ *for which payment well and truly to be made to the said Employer by the Bank itself, his successors and assigns by these presents.

SEALED with the Common Seal of the said Bank this _____ day of _____, 20____.

THE CONDITIONS of this obligation are :

- (1) If after Bid opening the Bidder withdraws his bid during the period of Bid validity specified in the Form of Bid;

OR

- (2) If the Bidder having been notified to the acceptance of his bid by the Employer during the period of Bid validity :

- (a) fails or refuses to execute the Form of Agreement in accordance with the Instructions to Bidders, if required; or
- (b) fails or refuses to furnish the Performance Security, in accordance with the Instruction to Bidders; or
- (c) does not accept the correction of the Bid Price pursuant to Clause 27.

We undertake to pay to the Employer up to the above amount upon receipt of his first written demand, without the Employer having to substantiate his demand, provided that in his demand the Employer will note that the amount claimed by him as due to him owing to the occurrence of one or any of the three conditions, (specifying the occurred condition or conditions).

(Seal & Signature of Tenderer)

[Signature]

[Signature]
25-6-2014
Chief Engineer
B.S.E.I.D.C. Ltd, Patna

This Guarantee will remain in force up to and including the date _____ ** days after the deadline for submission of Bids as such deadline is stated in the Instructions to Bidders or as it may be extended by the Employer, notice of which extension(s) to the Bank is hereby waived. Any demand in respect of this guarantee should reach the Bank not later than the above date.

DATE _____

SIGNATURE

WITNESS _____

SEAL

[Signature, name and address]

- * The Bidder should insert the amount of the guarantee in words and figures denominated in Indian Rupees. This figure should be the same as shown in Clause 16.1 of the Instructions to Bidders.
- ** 45 days after the end of the validity period of the Bid. Date should be inserted by the Employer before the Bidding documents are issued.


(Seal & Signature of Tenderer)


Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Rmb

PERFORMANCE BANK GUARANTEE

To

_____ [name of Employer]

_____ [address of Employer]

WHEREAS _____ [name and address of Contractor] (hereafter called "the Contractor") has undertaken, in pursuance of Contract No. _____ dated _____ to execute _____ [name of Contract and brief description of Works] (hereinafter called "the Contract").

AND WHEREAS it has been stipulated by you in the said Contract that the Contractor shall furnish you with a Bank Guarantee by a recognized bank for the sum specified therein as security for compliance with his obligation in accordance with the Contract;

AND WHEREAS we have agreed to give the Contractor such a Bank Guarantee :

NOW THEREFORE we hereby affirm that we are the Guarantor and responsible to you on behalf of the Contractor, up to a total of _____ [amount of guarantee]* _____ (in words), such sum being payable in the types and proportions of currencies in which the Contract Price is payable, and we undertake to pay you, upon your first written demand and without cavil or argument, any sum or sums within the limits of _____ [amount of guarantee] as aforesaid without your needing to prove or to show grounds or reasons for your demand for the sum specified therein.

We hereby waive the necessity of your demanding the said debt from the contractor before presenting us with the demand.

We further agree that no change or addition to or other modification of the terms of the Contract or of the Works to be performed there under or of any of the Contract documents which may be made between your and the Contractor shall in any way release us from any liability under this guarantee, and we hereby waive notice of any such change, addition or modification.

This guarantee shall be valid until 28 days from the date of expiry of the Defect Liability Period.

Signature and Seal of the guarantor _____

Name of Bank _____

Address _____

Date _____

* An amount shall be inserted by the Guarantor, representing the percentage the Contract Price specified in the Contract including additional security for unbalanced Bids, if any and denominated in Indian Rupees.

(Seal & Signature of Tenderer)



Chief Engineer
B.S.E.I.D.C. Ltd, Patna



UNCONDITIONAL BANK GUARANTEE FOR ADVANCE PAYMENT

To

_____ [name of Employer]
_____ [address of Employer]
_____ [name of Contractor]

Gentlemen :

In accordance with the provisions of the Conditions of Contract, sub-clause 51.1 ("Advance payment") of the above-mentioned Contract, _____ [name and address of Contractor] (hereinafter called "the Contractor") shall deposit with _____ [name of Employer] a bank guarantee to guarantee his proper and faithful performance under the said Clause of the Contract in an amount of _____ [amount of Guarantee]* _____ [in words].

We, the _____ [bank of financial institution], as instructed by the Contractor, agree unconditionally and irrevocably to guarantee as primary obligator and not as Surety merely, the payment to _____ [name of Employer] on his first demand without whatsoever right of obligation on our part and without his first claim to the Contractor, in the amount not exceeding _____ [amount of guarantee]* _____ [in words].

We further agree that no change or addition to or other modification of the terms of the Contractor or Works to be performed there under or any of the Contract documents which may be made between _____ [name of Employer] and the Contractor, shall in any way release us from any liability under this guarantee, and we hereby waive notice of any such change, addition or modification.

This guarantee shall remain valid and in full effect from the date of the advance payment under the Contract until _____ [name of Employer] receives full repayment of the same amount from the Contractor.

Yours truly,

Signature and Seal : _____

Name of Bank /Financial Institution _____

Address : _____

Date : _____

* An amount shall be inserted by the Bank or Financial Institution representing the amount of the Advance Payment, and denominated in Indian Rupees.


(Seal & Signature of Tenderer)

B.S.E.I.D.C. Ltd, Patna

INDENTURE FOR SECURED ADVANCES

FORM 31

(for use in case in which the contract is for finished work and the contractor has entered into an agreement for the execution of a certain specified quantity of work in a given time)

This indenture made the _____ day of _____, 20____ BETWEEN _____ (hereinafter called the contractor which expression shall where the context so admits or implies be deemed to include his executors, administrators and assigns) or the one part and the Employer of the other part.

Whereas by an agreement dated _____ (hereinafter called the said agreement) the contractor has agreed.


AND WHEREAS the contractor has applied to the Employer that he may be allowed advance on the security of materials absolutely belonging to him and brought by him to the site of the works the subject of the said agreement for use in the construction of such of the works as he has undertaken to execute at rates fixed for the finished work (inclusive of the cost of materials and labour and other charges)

AND WHEREAS the Employer has agreed to advance to the Contractor the sum of Rupees _____ on the security of materials the quantities and other particulars of which are detailed in Accounts of Secured Advances attached to the Running Account bill for the said works signed by the Contractor on _____ and the Employer has reserved to himself the option of making any further advance or advances on the security of other materials brought by the Contractor to the site of the said works.

Now THIS INDENTURE WITNESSETH that in pursuance of the said agreement and in consideration of the sum of Rupees _____ on or before the execution of these presents paid to the Contractor by the Employer (the receipt where of the Contractor doth hereby acknowledge) and of such further advances (if any) as may be made to him as a for said the Contractor doth hereby covenant and agree with the President and declare as follows :

- (1) That the said sum of Rupees _____ so advanced by the Employer to the Contractor as aforesaid and all or any further sum of sums advanced as aforesaid shall be employed by the Contractor in or towards expending the execution of the said works and for no other purpose whatsoever.
- (2) That the materials details in the said Account of Secured Advances which have been offered to and accepted by the Employer as security are absolutely the Contractor's own propriety and free from encumbrances of any kind and the contractor will not make any application for or receive a further advance on the security of materials which are not absolutely his own property and free from encumbrances of any kind and the Contractor indemnified the Employer against all claims to any materials in respect of which an advance has be made to him as aforesaid.
- (3) That the materials detailed in the said account of Secured Advances and all other materials on the security of which any further advance or advances may hereafter

(Seal & Signature of Tenderer)



Chief Engineer
B.S.E.I.D.C. Ltd, Patna

be made as aforesaid (hereafter called the said materials) shall be used by the Contractor solely in the Execution of the said works in accordance with the directions of the Engineer.

- (4) That the Contractor shall make at his own cost all necessary and adequate arrangements for the proper watch, safe custody and protection against all risks of the said materials and that until used in construction as aforesaid the said materials shall remain at the site of the said works in the Contractor's custody and on his own responsibility and shall at all times be open to inspection by the Engineer or any officer authorized by him. In the event of the said materials or any part thereof being stolen, destroyed or damaged or becoming deteriorated in a greater degree than is due to reasonable use and wear thereof the Contractor will forthwith replace the same with other materials of like quality or repair and make good the same required by the Engineer.
- (5) That the said materials shall not be any account be removed from the site of the said works except with the written permission of the Engineer or an officer authorized by him on that behalf.
- (6) That the advances shall be repayable in full when or before the Contractor receives payment from the Employer of the price payable to him for the said works under the terms and provisions of the said agreement. Provided that if any intermediate payments are made to the Contractor on account of work done than on the occasion of each such payment the Employer will be at liberty to made recovery from the Contractor's bill for such payment by deducting there from the value of the said materials that actually used in the construction and in respect of which recovery has not been made previously, the value for this purpose being determined in respect of each description of materials at the rates at which the amounts of the advances made under these presents were calculated.
- (7) That if the Contractor shall at any time make any default in the performance or observance in any respect of any of the terms and provisions of the said agreement or of these presents the total amount of the advance or advances that may still be owing of the Employer shall immediately on the happening of such default be repayable by the Contractor to be the Employer together with interest thereon at twelve per cent per annum from the date or respective dates of such advance or advances to the date of repayment and with all costs, charges, damages and expenses incurred by the Employer in or for the recovery thereof or the enforcement of this security or otherwise by reason of the default of the Contractor and the Contractor hereby covenants and agrees with the Employer to reply and pay the same respectively to him accordingly.
- (8) That the Contractor hereby charges all the said materials with the repayment to the Employer of the said sum of Rupees _____ and any further sum of sums advanced as aforesaid and all costs, charges, damages and expenses payable under these presents PROVIDED ALWAYS and it is hereby agreed and declared that notwithstanding anything in the said agreement and, without prejudice to the power contained therein if and whenever the covenant for payment and repayment here in before contained shall become enforceable and the money owing shall not be paid in accordance there with the Employer may at by time thereafter adopt all or any of the following courses as he may deem best :


(Seal & Signature of Tenderer)

25-6-2014
Chief Engineer
B.S.E.I.D.C. Ltd, Patna

- (a) Seize and utilise the said materials or any part thereof in the completion of the said works on behalf of the contractor in accordance with the provisions in that behalf contained in the said agreement debiting the contractor with the actual cost of effecting such completion and the amount due to the contractor with the value of work done as if he has carried it out in accordance with the said agreement and at the rests thereby provided. If the balance is against the contractor, he is to pay same to the Employer on demand.
 - (b) Remove and sell by public auction the seized materials or any part thereof and out of the moneys arising from the sale retain all the sums aforesaid repayable or payable to the Employer under these presents and pay over the surplus (if any) to the Contractor.
 - (c) Deduct all or any part of the moneys owing out of the security deposit or any sum due to the Contractor under the said agreement.
- (9) That except in the event of such default on the part of the contractor as aforesaid interest on the said advance shall not be payable.
- (10) That in the event of any conflict between the provisions of these presents and the said agreement the provisions of these presents shall prevail and in the event of any dispute or difference arising over the construction or effect of these presents the settlement of which has not been here-in-before expressly provided for the same shall be referred to the Employer whose decision shall be final and the provision of the Indian Arbitration Act for the time being in force shall apply to any such reference.

(Seal & Signature of Tenderer)

बिजेडि सी

Chief Engineer 122
B.S.E.I.D.C. Ltd, Patna

25-6-2014
Rmt

Letter of Acceptance
(Letterhead paper of the Employer)

(Date)

To

(Name and address of the Contractor)

Dear Sirs,

This is to notify you that your Bid dated _____ for execution of the _____ (name of the contract and identification number, as given in the Instructions to Bidders) for the Contract Price of Rupees _____ (amount in words and figures), as corrected and modified in accordance with the Instructions to Bidders¹ is hereby accepted by our agency.

We accept/ do not accept that _____ be appointed as the Adjudicator². You are hereby requested to furnish Performance Security, in the form detailed in Para 34.1 of ITB for an amount equivalent to Rs. _____ within 21 days of the receipt of this letter of acceptance valid up to 28 days from the date of expiry of defects Liability Period i.e. up to _____ and sign the contract, failing which action as stated in Para 34.3 of ITB will be taken.

Yours faithfully,

Authorized Signature

Name and title of Signatory

Name of Agency

¹ Delete "corrected and" or "and modified" if only one of these actions applies. Delete as corrected and modified in accordance with the Instructions to Bidders, if corrections or modifications have not been affected.

² To be used only if the Contractor disagrees in his Bid with the Adjudicator proposed by the Employer in the "Instructions to Bidders".


(Seal & Signature of Tenderer)

Chief Engineer
B.S.E.I.D.C. Ltd, Patna 123
Rout

Issue of Notice to proceed with the work
(Letterhead of the Employer)

_____(Date)

To

_____(Name and address of the Contractor)

Dear Sirs,

Pursuant to your furnishing the requisite security as stipulated in ITB Clause 34.1 and signing of the Contract for the construction of _____

_____ at a Bid
Price of Rs. _____

You are hereby instructed to proceed with the execution of the said works in accordance with the contract documents.

Yours faithfully,

(Signature, name and title of signatory authorized to sign on behalf of Employer)

(Seal & Signature of Tenderer)

BIGTA BATTAL

Chief Engineer
B.S.E.I.D.C. Ltd, Patna

124

25-6-2014
Rmg

Agreement Form

Agreement

This agreement, made the _____ day of _____ between _____ (name and address of Employer) [hereinafter called "the (name and address of contractor) hereinafter called "the Contractor" of the other part.]

Whereas the Employer is desirous that the Contractor execute

_____ (name and identification number of Contract) (hereinafter called "the Works") and the Employer has accepted the Bid by the Contractor for the execution and completion of such works and the remedying of any defects therein, at a cost of Rs. _____

NOW THIS AGREEMENT WITNESSETH as follows :

1. In this Agreement, words and expression shall have the same meanings as are respectively assigned to them in the conditions of contract hereinafter referred to and they shall be deemed to form and be read and construed as part of this Agreement.
2. In consideration of the payments to be made by the Employer to the Contractor as hereinafter mentioned, the Contractor hereby covenants with the Employer to execute and complete the Works and remedy any defects therein in conformity in all aspects with the provisions of the contract.
3. The Employer hereby covenants to pay the Contractor in consideration of the Execution and completion of the Works and the remedying the defects wherein Contract Price or such other sum as may become payable under the provisions of the Contract at the times and in the manner prescribed by the Contract.
4. The following documents shall be deemed to form and be ready and construed as part of this Agreement viz.
 - (i) Letter of Acceptance
 - (ii) Notice to proceed with the works;
 - (iii) Contractor's Bid
 - (iv) Condition of Contract : General and Special
 - (v) Contract Data
 - (vi) Additional condition
 - (vii) Drawings
 - (viii) Bill of Quantities and
 - (ix) Any other documents listed in the Contract Data as forming part of the Contract.


(Seal & Signature of Tenderer)


Chief Engineer
B.S.E.I.D.C. Ltd, Patna

In witnessed whereof the parties there to have caused this Agreement to be executed the day and year first before written.

The Common Seal of _____
was hereunto affixed in the presence of :

Signed, Sealed and Delivered by the said. _____

in the presence of :

Binding Signature of Employer _____

Binding Signature of Contractor _____

(Seal & Signature of Tenderer)

[Handwritten Signature]

[Handwritten Signature]
25-6-2014
Chief Engineer
B.S.E.I.D.C. Ltd, Patna

[Handwritten Signature]

UNDERTAKING


I, the undersigned do hereby undertake that our firm M/s _____
_____ agree to abide by this bid for a period _____ days for the
date fixed for receiving the same and it shall be binding on us and may be accepted at any
time before the expiration of that period.


(Signed by an Authorised Officer of the Firm)

Title of Officer

Name of Firm

DATE


(Seal & Signature of Tenderer)


Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Rmt

SECTION 9
DRAWINGS
(To be Attached)

(Seal & Signature of Tenderer)




25-6-2014
Chief Engineer
B.S.E.I.D.C. Ltd, Patna
Rmbr

SECTION 10
DOCUMENTS TO BE FURNISHED BY BIDDER)
(Attached)


(Seal & Signature of Tenderer)


Chief Engineer
B.S.E.I.D.C. Ltd, Patna 129
Rout

Chief Engineer
B.S.E.I.D.C. Ltd, Patna.

63
